

Report By:

National TAB
105 Stone Village Drive
Fort Mill, SC 29708



Report: Deficiency Report
Function: Test, Adjust, & Balance
Date: 08/20/2025
Completed By: National TAB

PROJECT
08-18-25 QT #1101 SENECA, SC

109 BYPASS 123

SENECA, SC

Client

QUIKTRIP
4705 SOUTH 129TH EAST AVENUE
TULSA, OK 74134

Issue List

- EF1-1 not installed
- EF1-5 no flow
- Hood not finished
- RTU 3 SGRD 1 through 4 not proper size
- RTU multiple OA damper positions could not be set




08-18-25 QT #1101 SENECA, SC

Project Issue Information

Issue Name : EF1-1 not installed
Description : To complete balance, EF1-1 needs to be installed. According to GC the SGRD will be installed later this week.
Created By : National TAB **Assigned To :** National TAB - Daniel Covaci
Status : Open
Priority : **Urgent** **Asset Tag :** EF1
Originated Date : 08/20/2025 - Chistian Moller - National TAB

Project Issue File Details

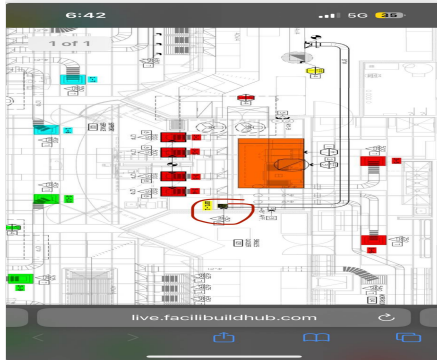

08/20/2025



08/20/2025



08-18-25 QT #1101 SENECA, SC


Project Issue Information

Issue Name : EF1-5 no flow
Description : EF1-5 did not have an airflow when total cfm for EF1 was being taken. Could not diagnose problem while on site.
Created By : National TAB **Assigned To :** National TAB - Daniel Covaci
Status : Open
Priority : Medium **Asset Tag :** EF1
Originated Date : 08/20/2025 - Chistian Moller - National TAB

Project Issue File Details



08/20/2025

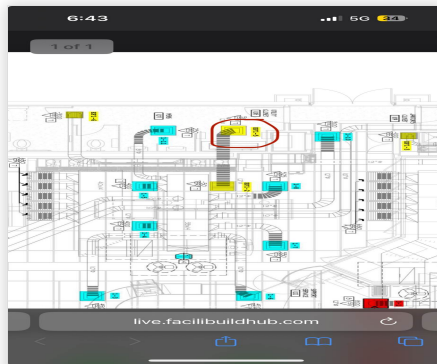

08/20/2025



08-18-25 QT #1101 SENECA, SC

Project Issue Information

Issue Name : Hood not finished
Description : Per the GC the hood will not be completed until late Thursday (8/21) or early Friday (8/22)
Created By : National TAB **Assigned To :** National TAB - Dan Hertenstein
Status : Open
Priority : Urgent **Asset Tag :** HD1
Originated Date : 08/20/2025 - Chistian Moller - National TAB

Project Issue File Details



08/20/2025



08/20/2025



08-18-25 QT #1101 SENECA, SC


Project Issue Information

Issue Name : RTU 3 SGRD 1 through 4 not proper size
Description : SGRD's 1 through 4 are not the proper size and could not be balanced accordingly. RTU 3 is balanced to total.
Created By : National TAB **Assigned To :** National TAB - Daniel Covaci
Status : Open
Priority : Urgent **Asset Tag :** RT-3
Originated Date : 08/20/2025 - Chistian Moller - National TAB

Project Issue File Details



08/20/2025

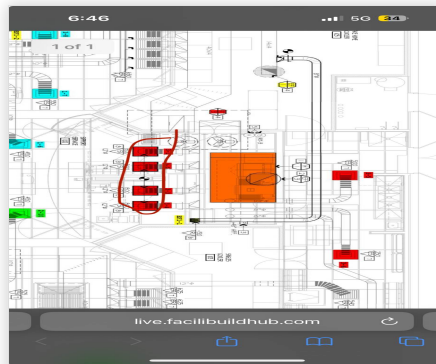

08/20/2025



08-18-25 QT #1101 SENECA, SC

Project Issue Information

Issue Name : RTU multiple OA damper positions could not be set
Description : Site plans call for multiple OA positions to be set (800 & 350 CFM) both positions were found and marked but could not be set as alternating positions. All 3 RTU's left at 800 OA CFM.
Created By : National TAB **Assigned To :** National TAB - Daniel Covaci
Status : Open
Priority : Urgent **Asset Tag :**
Originated Date : 08/20/2025 - Chistian Moller - National TAB

Project Issue File Details



08/20/2025



08/20/2025



08/20/2025
