

## Issue List

- EF-4 Missing Ductwork
- FCU's Not Operational
- FCU-4 Not Installed
- Flow Setpoints for SVAV-2 and SVAV-3
- SCAV-11 no power
- SCAV-2 Missing Cap
- VAV-3 tubing issue



### SPCC Aseptic Training Facility (Monroe, NC)

#### Project Issue Information

**Issue Name :** EF-4 Missing Ductwork  
**Description :** According to the sheet notes, it is to be 6' from the autoclave, unless it is required to be connected to the equipment via a thimble connection. Unsure what the final configuration will be. If going to be 6', birdscreen is missing to TAB.

**Created By :** National TAB                      **Assigned To :** National TAB - Antonio Flores-De La Cruz

**Status :** Open

**Priority :** Urgent                                      **Asset Tag :**

**Originated Date :** 02/17/2026 - Antonio Flores-De La Cruz - National TAB

#### Project Issue File Details



02/17/2026



**SPCC Aseptic Training Facility (Monroe, NC)**

**Project Issue Information**

**Issue Name :** FCU's Not Operational  
**Description :** Controls stated that FCU's program to control is not currently loaded.  
**Created By :** National TAB                      **Assigned To :** National TAB - Antonio Flores-De La Cruz  
**Status :** Open  
**Priority :** **Urgent**                                      **Asset Tag :**  
**Originated Date :** 02/17/2026 - Antonio Flores-De La Cruz - National TAB

Project Issue File Details



02/17/2026



**SPCC Aseptic Training Facility (Monroe, NC)**

**Project Issue Information**

**Issue Name :** FCU-4 Not Installed  
**Description :** FCU-4 is not installed.  
**Created By :** National TAB                      **Assigned To :** National TAB - Antonio Flores-De La Cruz  
**Status :** Open  
**Priority :** Urgent                                      **Asset Tag :**  
**Originated Date :** 02/17/2026 - Antonio Flores-De La Cruz - National TAB

Project Issue File Details



02/17/2026



02/17/2026



## SPCC Aseptic Training Facility (Monroe, NC)


### Project Issue Information

**Issue Name :** Flow Setpoints for SVAV-2 and SVAV-3  
**Description :** SVA-2 and SVAV-3 do not match based on the schedule and connected load CFM values. Need clarification on what is required.  
**Created By :** National TAB **Assigned To :** National TAB - Antonio Flores-De La Cruz  
**Status :** Open  
**Priority :** Urgent **Asset Tag :**  
**Originated Date :** 02/16/2026 - Antonio Flores-De La Cruz - National TAB

#### Project Issue File Details

TERMINAL AIR UNIT W/ ELECTRIC REHEAT SCHEDULE				
NUMBER	SYSTEMSERVING	CFM		INLET SIZE (IN)
		MIN	MAX	
SVAV-1	AHU-1 / CLRMS 117	680	1700	12
SCAV-1A	AHU -1 / CLEAN ROOM TRAINING 134	650	1870	14
SCAV-1B	AHU -1 / CLEAN ROOM TRAINING 134	650	1870	14
SCAV-1C	AHU -1 / CLEAN ROOM TRAINING 134	650	1870	14
SCAV-2	AHU-1 / PAL 129	60	100	4
SCAV-3	AHU-1 / PAL 130	60	190	4
SCAV-4	AHU-1 / MAL 131	80	150	4

02/16/2026

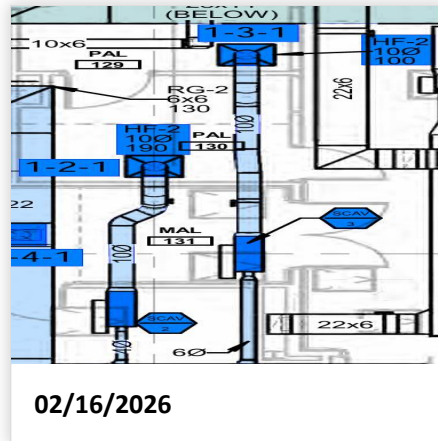



**SPCC Aseptic Training Facility (Monroe, NC)**

**Project Issue Information**

**Issue Name :** SCAV-11 no power  
**Description :** Unable to balance SCAV-11 due to no power. There is also no TSAT to manipulate the VAV. The TSAT installed in the room is for FCU F3-1. The box could maybe be balanced through Controls, unsure at the moment.  
**Created By :** National TAB                      **Assigned To :** National TAB - Antonio Flores-De La Cruz  
**Status :** Open  
**Priority :** Urgent                                      **Asset Tag :**  
**Originated Date :** 02/17/2026 - Antonio Flores-De La Cruz - National TAB



**SPCC Aseptic Training Facility (Monroe, NC)**

**Project Issue Information**

**Issue Name :** SCAV-2 Missing Cap  
**Description :** SCAV-2 is missing the cap on the T fitting for one of the pressure tubes.  
**Created By :** National TAB                      **Assigned To :** National TAB - Antonio Flores-De La Cruz  
**Status :** Open  
**Priority :** Urgent                                      **Asset Tag :**  
**Originated Date :** 02/17/2026 - Antonio Flores-De La Cruz - National TAB

Project Issue File Details



02/17/2026

Project Issue Response Details

- **02/17/2026 National TAB - Antonio Flores-De La Cruz**
  - FSS was made aware of the issue and was going to replace the cap. Unsure if it was done.




## SPCC Aseptic Training Facility (Monroe, NC)

### Project Issue Information

**Issue Name :** VAV-3 tubing issue  
**Description :** One of the pressure tubes for the VAV is missing the cap on the T-fitting. Tape was used to allow for balancing and recommended to replace the cap to ensure proper function.  
**Created By :** National TAB                      **Assigned To :** National TAB - Antonio Flores-De La Cruz  
**Status :** Open  
**Priority :** Urgent                                      **Asset Tag :**  
**Originated Date :** 02/16/2026 - Antonio Flores-De La Cruz - National TAB

#### Project Issue File Details

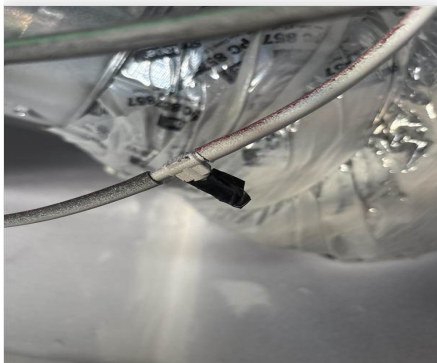

02/16/2026

#### Project Issue Response Details

- **02/17/2026 National TAB - Antonio Flores-De La Cruz**
  - FSS is aware of it, unsure if the caps were replaced.
