

# PlanGrid Task Report - Aug 8, 2024

Prepared by Dale Wheeler

Aug 8, 2024

## Description

10 tasks in this report.

## Contents

#61 [REFG 511] [NEW] PVC pipe chase (gooseneck) installation.....	2
#60 [REFG 500] [NEW] WIC/WIF temperatures. ....	3
#59 [UNIT 999] [NEW] (MISC) [FACTORY OA PANEL].....	4
#58 [REFG 517] [NEW] Hail guards.....	5
#57 [EXHA 003] [NEW] CRITICAL – Incorrect grease exhaust duct ells. ....	6
#56 [UNIT 517] [NEW] Condensate piping construction. ....	8
#55 [DUCT 007] [NEW] CRITICAL – Diffuser rigid 90's. ....	9
#54 [DUCT 501] [NEW] Insulation stick pins.....	10
#53 [DUCT 009] [NEW] CRITICAL – Damper incorrect type. ....	11
#52 [DUCT 010] [NEW] CRITICAL – Damper(s) missing hardware. ....	12

## #61 [REFG 511] [NEW] PVC pipe chase (gooseneck) installation.

**Status**

Open

**Start Date**

Aug 8, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:04 PM  
dale@nationaltab.com

**Description**

WIC & WIF gooseneck penetrations need to be sealed with spray foam.

**Last Updated**

Aug 8, 2024 12:11 PM

**Photos**



IMG\_5100

Dale Wheeler

Aug 8, 2024 12:05 PM



IMG\_5098

Dale Wheeler

Aug 8, 2024 12:05 PM

**L04954\_Chapel Hill University Place FSU (NC)**

Fordham Boulevard, Chapel Hill, North Carolina

L1020004954

**#60 [REFG 500] [NEW] WIC/WIF temperatures.**

**Status**

Open

**Start Date**

Aug 8, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:04 PM  
dale@nationaltab.com

**Description**

WIC is at 45F should be at 35F.

**Last Updated**

Aug 8, 2024 12:13 PM

**Photos**



IMG\_5096

**Dale Wheeler**

Aug 8, 2024 12:04 PM

## #59 [UNIT 999] [NEW] (MISC) [FACTORY OA PANEL]

**Status**

Open

**Start Date**

Aug 7, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:03 PM  
dale@nationaltab.com


**Description**

AC1 econ is missing a factory installed block off plate to seal outside air canopy.

**Last Updated**

Aug 8, 2024 12:15 PM

**Photos**

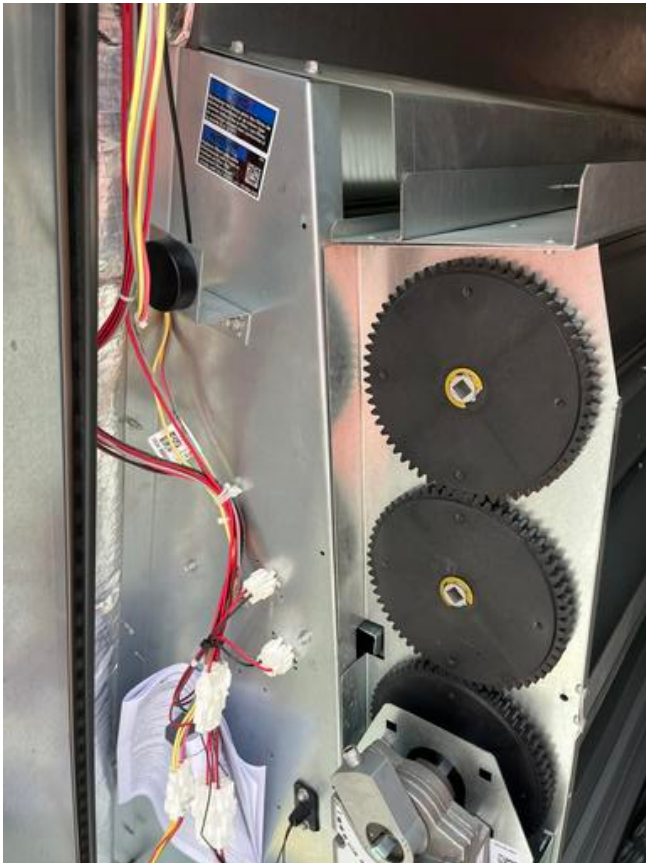

IMG\_5087

Dale Wheeler

Aug 8, 2024 12:04 PM

**L04954\_Chapel Hill University Place FSU (NC)**

Fordham Boulevard, Chapel Hill, North Carolina

L1020004954

**#58 [REFG 517] [NEW] Hail guards.**

**Status**

Open

**Start Date**

Aug 8, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:03 PM  
dale@nationaltab.com

**Description**

WIC & WIF hail guards are missing from condensers.

**Last Updated**

Aug 8, 2024 12:17 PM

**Photos**



IMG\_5085

**Dale Wheeler**

Aug 8, 2024 12:03 PM



IMG\_5086

**Dale Wheeler**

Aug 8, 2024 12:03 PM

**#57 [EXHA 003] [NEW] CRITICAL – Incorrect grease exhaust duct ells.**

**Status**

Open

**Start Date**

Aug 7, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:03 PM  
dale@nationaltab.com

**Description**

EF2 has two short radius turns installed. Plans call for long radius centerline R=3W/2 fittings per specification. Short radius, mitered ells, and offsets greater than 45 degrees are not allowed.

**Last Updated**

Aug 8, 2024 12:21 PM

**Photos**

**L04954\_Chapel Hill University Place FSU (NC)**

Fordham Boulevard, Chapel Hill, North Carolina

L1020004954



IMG\_5070

**Dale Wheeler**

Aug 8, 2024 12:03 PM

## #56 [UNIT 517] [NEW] Condensate piping construction.

**Status**

Open

**Start Date**

Aug 7, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:02 PM  
dale@nationaltab.com

**Description**

AC1, AC2, AC3, AC4 union between p-trap and unit should be the same size as condensate line called for in prints.

**Last Updated**

Aug 8, 2024 12:23 PM

**Photos**



IMG\_5059

Dale Wheeler

Aug 8, 2024 12:02 PM

## #55 [DUCT 007] [NEW] CRITICAL – Diffuser rigid 90's.

**Status**

Open

**Start Date**

Aug 7, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:01 PM  
dale@nationaltab.com

**Description**

AC1 SGRD9 is missing the hard rigid hard 90 at the diffuser.

**Last Updated**

Aug 8, 2024 12:30 PM

**Photos**



IMG\_5049

Dale Wheeler

Aug 8, 2024 12:02 PM



IMG\_5097

Dale Wheeler

Aug 8, 2024 12:02 PM

**L04954\_Chapel Hill University Place FSU (NC)**

Fordham Boulevard, Chapel Hill, North Carolina

L1020004954

**#54 [DUCT 501] [NEW] Insulation stick pins.**

**Status**

Open

**Start Date**

Aug 7, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:00 PM  
dale@nationaltab.com

**Description**

AC2 supply trunk line needs stick pins installed. Duct is over 24" in width.

**Last Updated**

Aug 8, 2024 12:29 PM

**Photos**



IMG\_5046

Dale Wheeler

Aug 8, 2024 12:01 PM

## #53 [DUCT 009] [NEW] CRITICAL – Damper incorrect type.

**Status**

Open

**Start Date**

Aug 7, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 12:00 PM  
dale@nationaltab.com

**Description**

AC4 SGRD4 has the incorrect damper type installed.

**Last Updated**

Aug 8, 2024 1:07 PM

**Photos**



IMG\_5103

Dale Wheeler

Aug 8, 2024 1:06 PM

**L04954\_Chapel Hill University Place FSU (NC)**

Fordham Boulevard, Chapel Hill, North Carolina

L1020004954

**#52 [DUCT 010] [NEW] CRITICAL – Damper(s) missing hardware.**

**Status**

Open

**Start Date**

Aug 7, 2024

**Type**

Planned Work

**Created**

Aug 8, 2024 11:59 AM  
dale@nationaltab.com

**Description**

AC4 SGRD3 is missing the damper handle. SGRD3 is at design CFM.

**Last Updated**

Aug 8, 2024 12:26 PM

**Photos**



IMG\_5053

Dale Wheeler

Aug 8, 2024 12:00 PM
