

Report By:

National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246



Report: Issue Data
Function: Test, Adjust, & Balance
Date: 02/05/2026
Completed By: National TAB

PROJECT
CW 9111 - OCC Expansion (Coppell, TX)

91111 CYPRESS WATERS BLVD

COPPELL, TX

Client

Venture Mechanical Inc
1644 W Crosby Rd
Carrollton, TX 75006

National TAB

Project: CW 9111 - OCC Expansion (Coppell, TX)

Table Of Contents

Section	Page #
Issue Data	3

Issue List

- VAV5-10 NOT OPERATIONAL (VAV-2A-10 CONTROLS LABEL)
- VAV5-3 NOT OPERATIONAL (VAV-2A-30 Controls Label)



CW 9111 - OCC Expansion (Coppell, TX)

Project Issue Information

Issue Name : VAV5-10 NOT OPERATIONAL (VAV-2A-10 CONTROLS LABEL)
Description : Unit is assumed to be VAV-2A-10 via controls graphics based on thermostat address. Unit is showing "NR" on controls graphics, unable to calibrate or balance this unit due to that issue.


Created By : National TAB **Assigned To :** National TAB - Dan Hertenstein

Status : Open


Priority : Urgent **Asset Tag :**

Originated Date : 02/06/2026 - Bayley Morvant - National TAB

Project Issue File Details

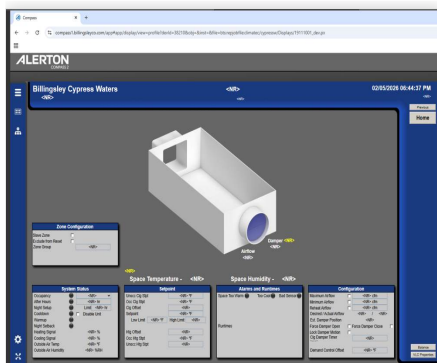

02/06/2026

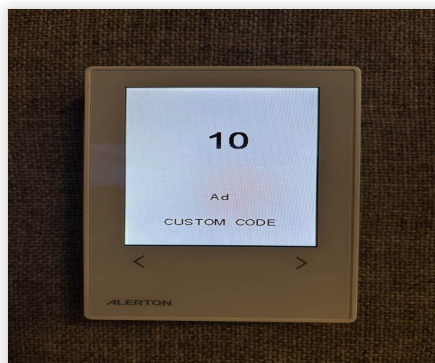

02/06/2026



02/06/2026



CW 9111 - OCC Expansion (Coppell, TX)

Project Issue Information

Issue Name : VAV5-3 NOT OPERATIONAL (VAV-2A-30 Controls Label)
Description : Unit is not operational. Unit is showing "NR" on controls graphics. Unit is wired for power and power switch is in ON position. Scrolling through thermostat options and it shows "No Custom Codes". This leads to believe this box has not been programmed. Box shows up on controls graphics matrix for the floor but not on the floor layout page.


Created By : National TAB **Assigned To :** National TAB - Dan Hertenstein

Status : Open

Priority : Urgent **Asset Tag :**

Originated Date : 02/06/2026 - Bayley Morvant - National TAB

Project Issue File Details

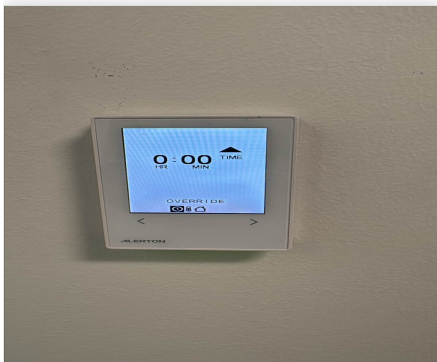

02/06/2026



02/06/2026
