

Report By:

National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246



Report: TAB Report
Function: Test, Adjust, & Balance
Date: 03/30/2026
Completed By: National TAB

PROJECT
03-30-26 QT #0813 NEWNAN, GA

1060 BULLSBORO DR.

NEWNAN, GA

Client

QUIKTRIP
4705 SOUTH 129TH EAST AVENUE
TULSA, OK 74134

National TAB

Project: 03-30-26 QT #0813 NEWNAN, GA

Table Of Contents

Section	Page #
Summary	3
Issue Data	4
Balance Schedule	6
Checklist	7
RTU-1	13
RTU-2	15
RTU-3	17
EF-1 - Exhaust	20
Combi-Oven Grille	22
EF-3 - Hood Exhaust	23
Kitchen Hood Type I	25
GRD Layout	27



National TAB

Project: 03-30-26 QT #0813 NEWNAN, GA
Function: Test, Adjust, & Balance

Project Summary

Project Summary

The summary below provides a quick understanding of our scope of work and general testing procedures. Enclosed in the report are further details about your building performance including recommendations, asset data, and pictures. Our focus is to work with the trades to remedy any issues or deficiencies during the actual field balancing and not after the balancing has occurred to achieve a positive environment and outcome. The level of success is determined by the availability of the trades, possible parts needed, or time constraints.

RTU's (Roof Top Units)

Each of the RTU's was measured with a flow hood to establish total flow. The total flow was then adjusted via the VFD so that airflow fell within design tolerances. All diffusers on the kitchen RTU were balanced to the engineer's design flow. The diffusers on the sales floor were only adjusted when there were noticeable issues present like drafting or dampers that were found completely closed. The Hoods On outside air rate was set by first establishing the typical QT set point at the Emerson controller and then making manually adjustments on the roof. The hoods off airflow setpoint was found by adjusting the damper position at the Emerson controller until the design airflow was achieved. Outside air was measured by reading the intake air opening with a velocity grid and multiplying by the free area. After completion of TAB all overrides were released.

Kitchen Exhaust Hood & Associated Fans

The kitchen exhaust fan was measured at the hood filter bay utilizing a velocity matrix and a manufacturer's correction factor. Each filter velocity is multiplied by the manufacturer's corrected area. The sum of these readings equals the total flow of the exhaust fans. The total flow of the exhaust was then adjusted to within tolerance of the design flow.

Restroom Exhaust Fans

The restroom exhaust fans were measured with a flow hood. The total flow was balanced for the fan with the exception of the new grille over the combi-oven, which was balanced to the listed design.

Final Building Tests

After completing the test and balance the final building pressure was measured. It was confirmed that the building pressure fell within acceptable tolerances and that the pressure measurement coincides with the actual and design net airflow. Any deviations from these standards are noted throughout the report. The hood capture was tested at the perimeter of the hood and the cook top level with the equipment heat on to ensure satisfactory hood capture and containment.

Issue List

- RTU-3: Hole in Flex Duct for Diffuser 3-4



03-30-26 QT #0813 NEWNAN, GA

Project Issue Information

Issue Name : RTU-3: Hole in Flex Duct for Diffuser 3-4
Description : There are holes in the flex duct for diffuser 3-4, farthest diffuser from the combi-oven/ closest to the walk-in cooler. This is releasing a lot of air into the ceiling. Tech attempted to patch on hole and found a second hole wrapping around the duct to the other side of it.
Created By : National TAB **Assigned To :** National TAB - Brianna Biggs
Status : Open
Priority : Urgent **Asset Tag :**
Originated Date : 03/30/2026 - Sagar Patel - National TAB

Project Issue File Details



03/30/2026



03/30/2026

AIR BALANCE SCHEDULE

UNIT	AREA SERVED	HOOD ON OA		HOOD OFF OA		HOOD ON EXHAUST		HOOD OFF EXHAUST	
		DESIGN	ACTUAL	DESIGN	ACTUAL	DESIGN	ACTUAL	DESIGN	ACTUAL
RTU 1	SALES	800	839	350	364				
RTU-2	SALES	800	784	350	378				
RTU-3	BOH/KITCHEN	800		350					
EF-1	RR/JANITOR					750	779	750	779
EF-3	HOOD					1350	1322	0	0
TOTALS		2400	1623	1050	742	2100	2101	750	779

HOODS ON

NET AIRFLOW CALCULATION

TOTALS	DESIGN	ACTUAL
TOTAL OA	2400	1623
TOTAL EXHAUST	2100	2101
NET AIRFLOW	300	-478

DOOR TESTED	BUILDING PRESSURE MEASUREMENTS
FRONT	-0.0103
SIDE	-0.0122
REAR	0.0025
AVERAGE	-0.0067

HOODS OFF

NET AIRFLOW CALCULATION

TOTALS	DESIGN	ACTUAL
TOTAL OA	1050	742
TOTAL EXHAUST	750	779
NET AIRFLOW	300	-37

DOOR TESTED	BUILDING PRESSURE MEASUREMENTS
FRONT	-0.0024
SIDE	-0.0051
REAR	0.0036
AVERAGE	-0.0013

NOTES:

CheckList List

- 01: RTU's/AHU's
- 02: Exhaust Fans
- 03: Hoods
- 04: Final Tests



03-30-26 QT #0813 NEWNAN, GA

CheckList Information

Name : 01: RTU's/AHU's **Status :** Completed
Assigned Organization : National TAB **Asset :**
Requesting Organization : National TAB
Created Date : 01/27/2026 - Trinity Dodds - National TAB
Completed Date : 03/30/2026 - Sagar Patel - National TAB

CheckList Item Details

RTU's/AHU's

Evaporator coils are clean? Pass

Comment:

Condenser coils are clean? Pass

Comment:

Gas piping is installed and valves are turned on? N/A

Comment:

Unit free of noticeable noise and vibration Pass

Comment:



03-30-26 QT #0813 NEWNAN, GA

CheckList Information

Name : 02: Exhaust Fans **Status :** Completed

Assigned Organization : National TAB **Asset :**

Requesting Organization : National TAB

Created Date : 01/27/2026 - Trinity Dodds - National TAB

Completed Date : 03/30/2026 - Sagar Patel - National TAB

CheckList Item Details

EF's

Hinge kit installed installed on hood fan?	Pass
--	------

Comment:

Flex conduit is long enough so that fan can be completely tilted back?	Pass
--	------

Comment:

No major leakage around the fan base	Pass
--------------------------------------	------

Comment:

Unit is free of noise and vibration	Pass
-------------------------------------	------

Comment:



03-30-26 QT #0813 NEWNAN, GA

CheckList Information

Name : 03: Hoods **Status :** Completed
Assigned Organization : National TAB **Asset :**
Requesting Organization : National TAB
Created Date : 01/27/2026 - Trinity Dodds - National TAB
Completed Date : 03/30/2026 - Sagar Patel - National TAB

CheckList Item Details

HOODS

Hood is free of alarms? Pass

Comment:

Hood is free of damage? Pass

Comment:

End panels are installed per prototype? N/A

Comment:



03-30-26 QT #0813 NEWNAN, GA

CheckList Information

Name : 04: Final Tests **Status :** Completed

Assigned Organization : National TAB **Asset :**

Requesting Organization : National TAB

Created Date : 01/27/2026 - Trinity Dodds - National TAB

Completed Date : 03/30/2026 - Sagar Patel - National TAB

CheckList Item Details

FINAL CHECKS

HOOD CAPTURE TEST

List kitchen equipment turned on for testing

Comment:

Fryer and Oven

List smoke candle type used

Comment:

45 Second Smoke Emitter

Smoke test capture % - Perimeter of hood

Comment:

100%

Smoke test capture % - Top of cooking surface

Comment:

100%

WITNESS

Date test was completed

03/30/2026

Comment:

Video

TAB tech name / Firm

Comment:

Sagar Patel / National TAB Intelligence

Site super name / Firm

Comment:

Not on Site

Owner representative name / Firm (if Applicable)

Comment:

N/A

BUILDING PRESSURE

Do actual net building airflow, design net building airflow, and pressure coincide? If not why? (All three should either be positive or negative) Fail

Comment:

Unable to balance RTU-3 due to hole in flex duct.



National TAB

Project: 03-30-26 QT #0813 NEWNAN, GA

System/Unit: AHU/RTU

Asset: RT-1

AREA:SALES FLOOR

Unit Data	
	Actual
MFG	AAON
Serial Num	202201-ANEK23512
Model Num	RN-013-8-0-EA0A-152
Num OA Filters 1	1
OA Filter Size 1	22X45
Num Final Filter 1	4
Final Filter Size 1	20X25X2

Motor Data	
	Actual
Motor MFG	N/L
Frame	N/L
Horsepower	3
Motor Rpm	1760
Phase	3
Rated Voltage	208
Rated Amperage	10.6

Test Data		
	Design	Actual
SF CFM	4200	4124
SF RPM	-	1390
OA CFM (Hoods On)	800	839
OA CFM (Hoods Off)	350	364
RL Voltage	-	167 VFD
RL Amperage	-	8.09 VFD
VFD Max SetPt	-	47.4 Hz
VFD Min SetPt	-	24 Hz
OA Damper Position (Hoods On)	-	46%
OA Damper Position (Hoods Off)	-	26%

Performance Data	
	Actual
MA Plenum SP	-0.47"
Fan Suction SP	-0.71"
Fan Discharge SP	0.74"
Total ESP	1.21"
Fan Total SP	1.45"

General	
	Actual
Fan Rotation Correct	YES
Unit Filters Clean	YES
Condensate Drain Installed	YES

Completed By: Sagar Patel on 03/30/2026

Unit Data - PHOTO LOG



03/30/2026



03/30/2026



National TAB

Project: 03-30-26 QT #0813 NEWNAN, GA

System/Unit: AHU/RTU

Asset: RT-2

AREA:SALES FLOOR

Unit Data	
	Actual
MFG	AAON
Serial Num	202201-ANEK23513
Model Num	RN-013-8-0-EA0A-152
Num OA Filters 1	1
OA Filter Size 1	22X45
Num Final Filter 1	4
Final Filter Size 1	20X25X2

Motor Data	
	Actual
Motor MFG	N/L
Frame	N/L
Horsepower	3
Motor Rpm	1760
Phase	3
Rated Voltage	208
Rated Amperage	10.6


Test Data		
	Design	Actual
SF CFM	4200	4172
SF RPM	-	1373
OA CFM (Hoods On)	800	784
OA CFM (Hoods Off)	350	378
RL Voltage	-	163 VFD
RL Amperage	-	7.94 VFD
VFD Max SetPt	-	46.8 Hz
VFD Min SetPt	-	24 Hz
OA Damper Position (Hoods On)	-	46%
OA Damper Position (Hoods Off)	-	26%

Performance Data	
	Actual
MA Plenum SP	-0.55"
Fan Suction SP	-0.81"
Fan Discharge SP	0.57"
Total ESP	1.12"
Fan Total SP	1.38"

General	
	Actual
Fan Rotation Correct	YES
Unit Filters Clean	YES
Condensate Drain Installed	YES

Completed By: Sagar Patel on 03/30/2026

Unit Data - PHOTO LOG

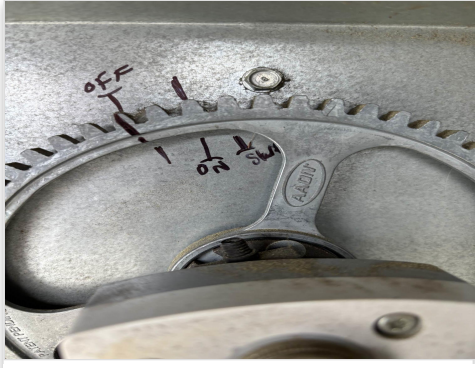

03/30/2026



03/30/2026



National TAB

Project: 03-30-26 QT #0813 NEWNAN, GA

System/Unit: AHU/RTU

Asset: RT-3

AREA:BOH/KITCHEN

Unit Data	
	Actual
MFG	AAON
Serial Num	202201-ANEK23514
Model Num	RN-013-8-0-EA0A-152
Num OA Filters 1	1
OA Filter Size 1	22X45
Num Final Filter 1	4
Final Filter Size 1	20X25X2

General	
	Actual
Fan Rotation Correct	YES
Unit Filters Clean	YES
Condensate Drain Installed	YES

Motor Data	
	Actual
Motor MFG	N/L
Frame	N/L
Horsepower	3
Motor Rpm	1760
Phase	3
Rated Voltage	208
Rated Amperage	10.6

Completed By: Sagar Patel on 03/30/2026

Unit Data - PHOTO LOG



03/30/2026



National TAB

Project:03-30-26 QT #0813 NEWNAN, GA

AHU/RTU

Diffuser Supply (GRD)

RT-3/BOH/KITCHEN

Asset									
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	CFM(2)	FINAL CFM	% to design
SGRD1	SUPPORT SERVICE	SI	12"	800					-
SGRD2	SUPPORT SERVICE	SI	12"	800					-
SGRD3	SUPPORT SERVICE	SI	12"	800					-
SGRD4	SUPPORT SERVICE	SI	12"	800					-
SGRD5	DOCK	ES	10"	500					-
SGRD6	WORKROOM	ES	10"	250					-
SGRD7	WORKROOM 2	ES	8"	250					-
Total				4200		0	0	0	0%



National TAB

Project: 03-30-26 QT #0813 NEWNAN, GA

System/Unit: FAN - Exhaust

Asset: EF1

AREA:RR/JANITOR

Unit Data	
	Actual
MFG	CAPTIVEAIRE
Model Num	DR50HFA
Serial Num	527558
Type	DOWNBLAST
Configuration	VERTICAL

Test Data		
	Design	Actual
CFM	750	779
Fan Rotation	-	CCW
System SetPt	-	MEDIUM HIGH
RL Voltage	-	[1]
RL Amperage	-	[1]
Total ESP	-	0.28"
Fan Inlet SP	-	-0.28"
Fan Discharge SP	-	ATM

Motor Data	
	Actual
Motor MFG	CENTURY
Frame	48Y
Horsepower	0.50
Motor Rpm	1075
Phase	1
Voltage (rated)	208
Amperage (rated)	3.6
Service Factor	N/L

Completed By: Sagar Patel on 03/30/2026

Notes:

[1] UNABLE TO READ VOLTS AND AMPS SAFELY

Written By: Sagar Patel on 03/30/2026

Unit Data - PHOTO LOG



03/30/2026



National TAB

Project:03-30-26 QT #0813 NEWNAN, GA

Diffuser Ret/Exh (GRD)

EF1/RR/JANITOR

Asset									
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	CFM(2)	FINAL CFM	% to design
EGRD4	COMBI-OVEN	RI	8"	150	1	207	158	158	105.3
Total				150		207	158	158	105.33%

Completed By: Sagar Patel on 03/30/2026



National TAB

Project: 03-30-26 QT #0813 NEWNAN, GA

System/Unit: FAN - Exhaust

Asset: EF3

AREA:KITCHEN HD

Unit Data		
	Design	Actual
MFG	NA	CAPTIVEAIRE
Model Num	NA	DU50HFA
Serial Num	-	7657561
Type	UPBLAST	UPBLAST
Configuration	VERTICAL	VERTICAL

Motor Data		
	Design	Actual
Motor MFG	-	TELECO GREEN
Frame	-	N/L
Horsepower	1/2	0.50
Motor Rpm	-	1800
Phase	-	1
Voltage (rated)	-	208
Amperage (rated)	-	3.8
Service Factor	-	N/L

Test Data		
	Design	Actual
CFM	1350	1322
Fan RPM	-	1196
Fan Rotation	-	CCW
Motor RPM	-	1196
System SetPt	-	52.8 Hz (66% on MSC)
RL Voltage	-	210
RL Amperage	-	1.8
Total ESP	-	0.32"
Fan Inlet SP	-	-0.32"
Fan Discharge SP	-	ATM

Completed By: Sagar Patel on 03/30/2026

Unit Data - PHOTO LOG



03/30/2026



National TAB

Project: 03-30-26 QT #0813 NEWNAN, GA

System/Unit: Kitchen Hood Type I

Asset: HD1

AREA:GRIDDLE

Unit Data

	Design	Actual
MFG	CAPTIVEAIRE	CAPTIVEAIRE
Model Num	6030ND-2-F	6030ND-2-F
Job / Serial Num	-	7657561
Type	TYPE I CANOPY	TYPE I CANOPY
Hood length	108"	108"
Hood Width	60"	60"

Test Data Exhaust

	Design	Actual
Filter Type	-	CAPTRATE SOLO FILTER
Filter Size 1	-	20X16
Filter Qty 1	-	6
Filter AK factor size 1	-	2.08
Filter Total AK Area	-	12.48
Filter1 FPM	-	98
Filter2 FPM	-	103
Filter3 FPM	-	111
Filter4 FPM	-	116
Filter5 FPM	-	108
Filter6 FPM	-	97
Filter Ave FPM(corr)	-	106
CFM	1350	1322

Cooking Equipment

	Actual
Item 1	FRYER
Item 2	OVEN

Completed By: Sagar Patel on 03/30/2026

Unit Data - PHOTO LOG



03/30/2026



03/30/2026

