

**Report By:**

**National TAB  
1329 E. KEMPER ROAD  
SUITE 4210  
CINCINNATI, OH 45246**



**Report: Bethany ES Cafeteria (Clover, SC)**

**Function: Test, Adjust, & Balance**

**Date: 01/24/2024**

**PROJECT**  
**Bethany ES (Clover, SC)**

CLOVER, SC

**Client**

Action Mechanical Inc.

PO Box 7325

CHARLOTTE, NC 28241

# National TAB

Project: Bethany ES (Clover, SC)

## Table Of Contents

Section	Page #
Equipment Calibrations	3
Abbreviations	4
GRD	5
AHU/RTU	6



# National TAB

## Testing, Adjusting, and Balancing Equipment




Function		Range	Minimum Accuracy	Instrument Information	Calibration Date	Date Due
AIR	AIR PRESSURE	0 in wg to 10 in wg	2% +/- 0.001 in wg	Shortridge ADM-860C S/N M19547	10/17/2023	10/16/2024
	AIR VELOCITY INSTRUMENT	50 fpm to 3900 fpm	+/- 5 % +/- 7 fpm	Shortridge ADM-860C S/N M19548	10/17/2023	10/16/2024
	DIRECT HOOD READING	100 cfm to 2000 cfm	+/- 3 % +/- 7 cfm	Shortridge Flow Hood	10/17/2023	10/16/2024
TEMPERATURE	AIR METER	-20 F to 240 F	+/- .5 % 2 F	Cooper ATKINS - SRH77A S/N 081820093	10/20/2023	10/19/2024
	AIR PROBE	-20 F to 240 F	+/- .5 % 2 F	Cooper ATKINS - PD1388 7-6 S/N 5028	10/20/2023	10/19/2024
	IMMERSION METER	-20 F to 240 F	+/- .5 % 2 F	Cooper ATKINS - SRH77A S/N 081820093	10/20/2023	10/19/2024
	IMMERSION PROBE	-20 F to 240 F	+/- .5 % 2 F	Cooper ATKINS - PD1388 7-6 S/N 1075	10/20/2023	10/19/2024
	CONTACT METER	-20 F to 240 F	+/- .5 % 2 F	Cooper ATKINS - SRH77A S/N 081820093	10/20/2023	10/19/2024
	CONTACT PROBE	-20 F to 240 F	+/- .5 % 2 F	Cooper ATKINS - PD1388 7-6 S/N 4011	10/20/2023	10/19/2024
HUMIDITY	HUMIDITY PROBE	10 % RH to 90 % RH	3% of reading	Cooper ATKINS - SRH77A S/N 090315046	10/20/2023	10/19/2024
ELECTRICAL	VOLTAGE MEASUREMENT	0 VAC to 600 VAC	2 % reading +/- 5 digits	Dwyer CM-1 - S/N 190800099	10/16/2023	10/15/2024
	AMPERAGE MEASUREMENT	0 Amperers to 100 Amperes	2 % reading +/- 5 digits	Dwyer CM-1 - S/N 190800099	10/16/2023	10/15/2024
ROTATION	ROTATION MEASUREMENT	60 rpm to 5000 rpm	2 % reading 2 rpm	Dwyer TAC-L - S/N S1100123	10/16/2023	10/15/2024
HYDRONIC	PRESSURE MEASUREMENT	-30 in Hg to 200 psi	±2% of reading +/- 1 psi	Dwyer 490W-6 - S/N 01L6NK	6/21/2023	6/20/2024
	DIFFERENTIAL PRESSURE MEASUREMENT	0 psi - 80 psi	±2% of reading +/- 1 psi	Dwyer 490W-6 - S/N 01L6NK	6/21/2023	6/20/2024
DALT	DUCT LEAKAGE	-10" - +10" wc	±1% of reading +/- 0.004" wc	Kanomax DALT 6900 S/N: 080439	5/2023	5/2024


## Abbreviation List

A = Area (ft <sup>2</sup> )	S.F. = Service Factor
AHU = Air Handling Unit	SF = Supply Fan
A <sub>k</sub> = Effective Area	SP = Static Pressure
BHP = Brake Horsepower (IP) HP	SR = Supply Register
Btu = British Thermal Unit	T = Temperature
Btu/h = Btuh = BTUH = BTU/Hour	T <sub>ma</sub> = Mixed Air Temperature
CL = Center Distance (used in belt formula)	T <sub>oa</sub> = Outside Air Temperature
CD = Ceiling Diffuser	T <sub>ra</sub> = Return Air Temperature
CF = Correction Factor	H = Head (in wc, ft wc, psi)
CFM = Volumetric Flow: Cubic Feet Per Minute	h = Enthalpy
CO <sub>2</sub> = Carbon Dioxide	HP = Horsepower
CO = Carbon Monoxide	hr = Hour
C <sub>v</sub> = Flow Constant	K <sub>v</sub> = Flow constant (SI)
d = Diameter (in.) IP	kW = Kilowatt = 1000 Watts
Δ = Difference or Change (Final - Initial)	LAT = Leaving Air Temperature
DB = Dry Bulb	lb = Pounds
EA = Exhaust Air	LWT = Leaving Water Temperature
EAT = Entering Air Temperature	ma = Mixed Air
EF = Exhaust Fan	MIN = Minimum
Eff = Efficiency	MAX = Maximum
EG = Exhaust Grille	N/A = Not Applicable
ESP = External Static Pressure	NA = No Access
EWT = Entering Water Temperature	NL = Not Listed
°F = Degrees Fahrenheit, °F	NPSHA = Net Positive Suction Head Available
FPB = Fan Powered Box	NS = Not Specified
FLA = Full Load Amps	OA = Outside Air
fpm = Feet per Minute (fpm)	OAT = Outside Air Temperature
ft = Foot	PD = Sheave Pitch Diameter
gal = Gallons	P.D. = Pressure Drop
GPM = Gallons Per Minute (GPM)	PF = Power Factor
h = Enthalpy (BTU/lb dry air)	SG = Supply Grille
P = Pressure	SR = Supply Register
ppm = parts per million	TP = Total Pressure
psi = Pounds Per Square Inch	T <sub>ra</sub> = Return Air Temperature
psid = PSI Differential	TS = Tip Speed (fpm) IP, (m/s) SI
r = Radius (in)	TSP = Total Static Pressure
% <sub>ra</sub> = % of Return Air	V = Velocity
RA = Return Air	VAV = Variable Air Volume
RAT = Return Air Temperature	VD = Volume Damper
RF = Return Fan	VFD = Variable Frequency Drive
RG = Return Grille	W = Watt
RH = Relative Humidity	WB = Wet Bulb
RPM = Revolutions Per Minute	wg = wc = water gauge = water column
RTU = Roof Top Unit	WHP = Water Horsepower (IP)
SA = Supply Air	ω = Humidity Ratio

RTU-38

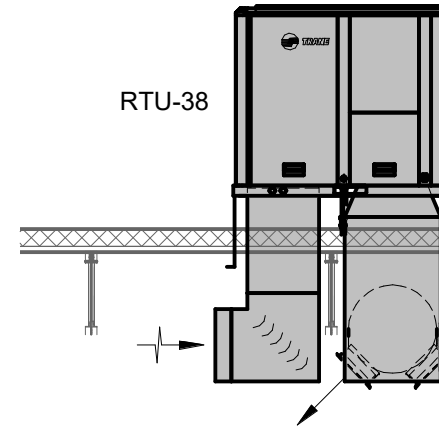

**3** SECTION  
M101 1/4" = 1'-0"

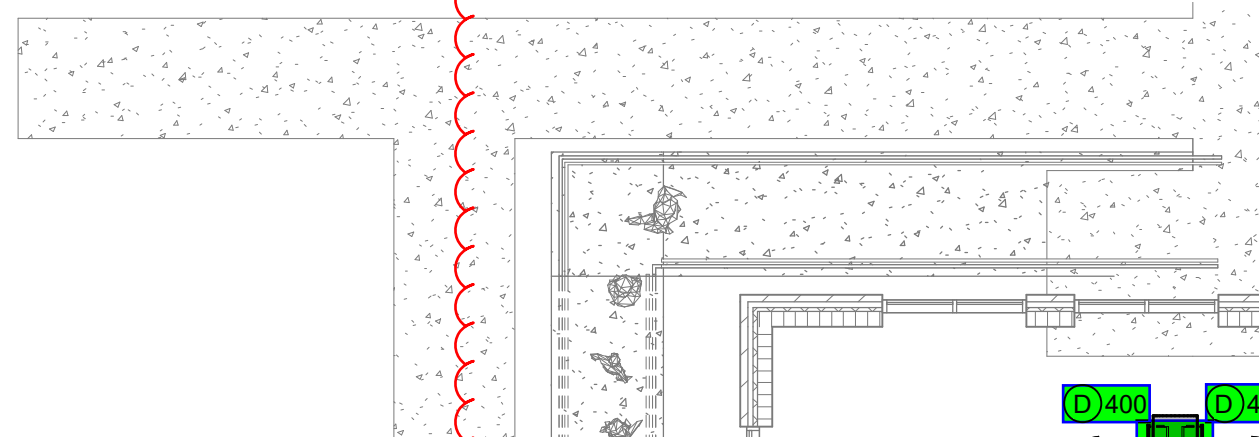

D 400

D 400

# National TAB

Project: Bethany ES (Clover, SC)

System/Unit: AHU/RTU



Asset: RTU-38

AREA:

Unit Data		
	Design	Actual
MFG	TRANE	TRANE
Serial Num	-	233813143L
Model Num	NA	WHC092H4
Configuration	VERTICAL	VERTICAL
Num OA Filters 1	-	1
OA Filter Size 1	-	36X15.5
Num PreFilter 1	-	4
PreFilter Size 1	-	20X25X2

Test Data		
	Design	Actual
SF CFM	3000	3162
RA CFM	2330	2507
OA CFM	670	655
RL Voltage	460	491/491/493
RL Amperage	3.6	0.8/0.8/0.9
OA Damper Position	-	30%
Brake Horse Power	0.61	0.64

Motor Data		
	Design	Actual
Motor MFG	-	NA
Frame	-	NA
Horsepower	2.75	2.75
Motor Rpm	-	NA
Phase	3	3
Rated Voltage	460	460
Rated Amperage	3.6	3.6
Service Factor	-	1

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.11"
Fan Suction SP	-	-0.23"
Fan Discharge SP	-	0.21"
Total ESP	0.40	0.32"
Fan Total SP	-	0.44"

Completed By: Antonio Flores-De La Cruz on 01/15/2024

Notes:

SGRD 38-3 AND 38-4 WERE LEFT HIGH TO AVOID DAMPER CAUSING A LOUD WHISTLE. NO BRANCH DAMPERS

Written By: Antonio Flores-De La Cruz on 01/15/2024

# National TAB

Project: Bethany ES (Clover, SC)

## AHU/RTU



### Diffuser Supply (GRD)

#### RTU-38/

Asset							
Asset Name	Location	Type	Size	DESIGN CFM	CFM(1)	FINAL CFM	% to design
RTU-38-SGRD1	200	D	16X12	400	494	399	99.8
RTU-38-SGRD2	200	D	16X12	400	77	385	96.3
RTU-38-SGRD3	200	D	16X12	400	786	484	121.0
RTU-38-SGRD4	200	D	16X12	400	682	486	121.5
RTU-38-SGRD5	200	D	16X12	400	757	414	103.5
RTU-38-SGRD6	200	D	16X12	400	750	417	104.3
RTU-38-SGRD7	201	A	8	200	220	190	95.0
RTU-38-SGRD8	201	A	8	200	209	182	91.0
RTU-38-SGRD9	201	A	8	200	258	205	102.5
Total				3000	4233	3162	105.4%

Completed By: Antonio Flores-De La Cruz on 01/15/2024
