

**Report By:**

National TAB  
1329 E. KEMPER ROAD  
SUITE 4210  
CINCINNATI, OH 45246



**Report: TAB Report**  
**Function: Test, Adjust, & Balance**  
**Date: 12/10/2025**  
**Completed By: National TAB**

**PROJECT**  
**12-08-25 CHIPOTLE #5187 CAMAS, WA**

19530 SE BRADY RD

CAMAS, WA 98607

**Client**

Chipotle Mexican Grill  
610 Newport Center Drive, Suite 1100  
Newport Beach, CA 92660

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

## Table Of Contents

| <b>Section</b>      | <b>Page #</b> |
|---------------------|---------------|
| Summary             | 3             |
| Checklist Data      | 4             |
| AHU/RTU             | 13            |
| FAN - Exhaust       | 24            |
| FAN - Supply        | 30            |
| Kitchen Hood Type I | 32            |
| GRD                 | 34            |
| Balance Schedule    | 35            |

## Project Summary

The summary below provides a quick understanding of our scope of work and general testing procedures. Enclosed in the report is further detail about your building performance including recommendations, asset data, and pictures. Our focus is to work with the trades to remedy any issues or deficiencies during the actual field balancing and not after the balancing has occurred to achieve a positive environment and outcome. The level of success is determined by the availability of the trades, possible parts needed, or time constraints.

### RTU's (Roof Top Units) w/ Diffusers

Each of the RTU's were measured at their terminal devices or via traverse to establish a total flow for that unit. Each RTU was adjusted to within tolerance of the engineer's design flow. Each outlet was then adjusted to within tolerance of the design flow. Outside air was measured by reading the intake air opening with a velocity grid and multiplying by the free area. The outside air damper was adjusted until the airflow was within the design requirements. Any equipment that fell outside of that tolerance is noted throughout the report.

### Kitchen Exhaust Hood & Associated Fans

Each kitchen exhaust fan was measured at the hood filter bay utilizing a velocity matrix and a manufacturer's correction factor. Each filter velocity is multiplied by the manufacturer's corrected area. The sum of these readings equals the total flow of the exhaust fans. The total flow of the exhaust was then adjusted to within tolerance of the design flow. . Any EF's that fell outside of this tolerance is noted throughout the report.

### MUA (Make Up Air Unit) w/ PSP

Total flow for the MAU (Make-up Air Unit) unit was measured by readings taken at the discharge of the hood's perforated supply plenum. Readings taken with a velocity matrix were averaged and multiplied by a manufacturer's corrected area. Adjustments to the fan speed were made in order to bring the unit to within design tolerance. Any MUA's that fell outside of this tolerance is noted throughout the report.

### General Exhaust Fans w/ Grilles

The general exhaust fans were measured by reading each air device with a flow hood. The total airflow for each fan is equivalent to the sum of these readings. Fan speed was then adjusted so that the airflow was within tolerance of design. Each terminal device was balanced to within tolerance of the design volume using the installed volume dampers. Any equipment that fell outside of this tolerance is noted throughout the report.

### Final Building Tests

After completing the test and balance the final building pressure was measured. It was confirmed that the building pressure fell within acceptable tolerances of  $-0.02''$  wc to  $+0.02''$  wc and that the pressure measurement coincides with the actual and design net airflow. Any deviations from these standards are noted throughout the report.

The hood capture was tested at the perimeter of the hood and the cook top level with the equipment heat on to ensure satisfactory hood capture and containment.

## CheckList List

- 01: RTU'S/AHU'S
- 02: EF'S
- 03: MUA
- 04: HOODS
- 05: FINAL TESTS



**12-08-25 CHIPOTLE #5187 CAMAS, WA**

**CheckList Information**

**Name :** 01: RTU'S/AHU'S **Status :** Completed  
**Assigned Organization :** National TAB **Asset :**  
**Requesting Organization :** National TAB  
**Created Date :** 09/03/2025 - Tyce Fox - National TAB  
**Completed Date :** 12/11/2025 - David Nicolas Sanchez - National TAB

**CheckList Item Details**

RTU's/AHU's

Thermostats installed and have power? Yes

Comment:

All diffusers and grilles are installed and match design? Yes

Comment:

Deflector plates are removed from 1x1 diffusers on the serve line (double check that this is specified on the diffuser schedule first) Yes

Comment:

Economizer blank plate is installed below the outside air intake (Trane only) (N/A = not applicable) N/A

Comment:

Economizers are assembled and functional? N/A

Comment:

DCV Max damper opening position is set to minimum? N/A

Comment:

Free cooling enthalpy set point set for lowest setting (Typically "D")

N/A

Comment:

Motors are all operating below the FLA rating?

Yes

Comment:

Are belts tight?

N/A

Comment:

If direct drive unit is the speed controller working?

Yes

Comment:

Is gas piping installed and valves turned on?

Yes

Comment:

Unit free of noticeable noise and vibration

Yes

Comment:

Final outside air damper position is marked with permanent marker?

N/A

Comment:



12-08-25 CHIPOTLE #5187 CAMAS, WA

**CheckList Information**

**Name :** 02: EF'S **Status :** Completed  
**Assigned Organization :** National TAB **Asset :**  
**Requesting Organization :** National TAB  
**Created Date :** 09/03/2025 - Tyce Fox - National TAB  
**Completed Date :** 12/11/2025 - David Nicolas Sanchez - National TAB

**CheckList Item Details**

EF's

**Rotation is correct?** Yes

**Comment:**

**Belts are tight?** N/A

**Comment:**

**Viroguard installed on hood fan(s)?** N/A

**Comment:**

**Hinge kit installed installed on hood fan?** N/A

**Comment:**

**Lean fan back. Is grease duct installation adequate and is duct ran all the way to the base of the fan?** N/A

**Comment:**

**Flex conduit is long enough so that fan can be completely tilted back?** N/A

**Comment:**

**There is no major leakage around base of fan?**

Yes

**Comment:**

**Is the motor operating below the motor FLA rating?**

Yes

**Comment:**

**For restroom fan(s) is the back draft damper installed and can it fully open?**

Yes

**Comment:**

**Unit free of noticeable noise and vibration?**

Yes

**Comment:**



12-08-25 CHIPOTLE #5187 CAMAS, WA

**CheckList Information**

**Name :** 03: MUA **Status :** Completed

**Assigned Organization :** National TAB **Asset :**

**Requesting Organization :** National TAB

**Created Date :** 09/03/2025 - Tyce Fox - National TAB

**Completed Date :** 12/11/2025 - David Nicolas Sanchez - National TAB

**CheckList Item Details**

MUA

|                      |     |
|----------------------|-----|
| Rotation is correct? | Yes |
|----------------------|-----|

Comment:

|  |     |
|--|-----|
| Gas piping is installed and valves are in on position? | Yes |
|--|-----|

Comment:

|   |     |
|---|-----|
| Internal motorized damper is fully opening? | Yes |
|---|-----|

Comment:

|  |     |
|--|-----|
| Motor is operating below the FLA rating? | Yes |
|--|-----|

Comment:

|  |     |
|--|-----|
| Unit free of noticeable noise and vibration? | Yes |
|--|-----|

Comment:



12-08-25 CHIPOTLE #5187 CAMAS, WA

**CheckList Information**

**Name :** 04: HOODS **Status :** Completed

**Assigned Organization :** National TAB **Asset :**

**Requesting Organization :** National TAB

**Created Date :** 09/03/2025 - Tyce Fox - National TAB

**Completed Date :** 12/11/2025 - David Nicolas Sanchez - National TAB

**CheckList Item Details**

**HOODS**

---

**All hood filters installed and accounted for?** Yes

**Comment:**

---

**Hoods are wired and have power?** Yes

**Comment:**

---

**Hood is free of alarms?** Yes

**Comment:**

---

**Hood is free of damage?** Yes

**Comment:**

---

**Quarter or full vertical end panels are installed if specified?** Yes

**Comment:**



12-08-25 CHIPOTLE #5187 CAMAS, WA

**CheckList Information**

**Name :** 05: FINAL TESTS **Status :** Completed

**Assigned Organization :** National TAB **Asset :**

**Requesting Organization :** National TAB

**Created Date :** 09/03/2025 - Tyce Fox - National TAB

**Completed Date :** 12/11/2025 - David Nicolas Sanchez - National TAB

**CheckList Item Details**

**FINAL CHECKS**

**Is space free of drafting?** Yes

**Comment:**

**Is space comfortable in all areas?** Yes

**Comment:**

**Is the space free of ventilation noise?** Yes

**Comment:**

**List kitchen equipment turned on for testing**

**Comment:**

None

**List smoke candle type used**

**Comment:**

CEO 163 45 Seconds

**HOOD CAPTURE TEST**

**Smoke test capture % - Perimeter of hood**

**Comment:**

100%

---

**Smoke test capture % - Top of cooking surface**

**Comment:**

100%

---

**WITNESS**

**Date test was completed**

12/10/2025

**Comment:**

---

**TAB tech name / Firm**

**Comment:**

David Nicolas Sanchez / National TAB Intelligence

---

**Site super name / Firm**

**Comment:**

Luis / Western Construction

---

**Owner representative name / Firm (if Applicable)**

**Comment:**

N/A

---

**BUILDING PRESSURE**

---

**Do actual net building airflow, design net building airflow, and pressure coincide? If not why? (All three should either be positive or negative)**

Pass

**Comment:**

Front: 0.0026" Side: 0.0015" Back: 0.0009"

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

System/Unit: AHU/RTU



Asset: FUR1

AREA: DINING

| Unit Data           |                 |                 |
|---------------------|-----------------|-----------------|
|                     | Design          | Actual          |
| MFG                 | CARRIER         | CARRIER         |
| Serial Num          | -               | 3625A45121      |
| Model Num           | 59SC6A080M21-20 | 59SC6A080M21-20 |
| Type                | FUR             | FUR             |
| Configuration       | VERTICAL        | VERTICAL        |
| Num Final Filter 1  | -               | 1               |
| Final Filter Size 1 | -               | 25X21.25        |

| Motor Data     |        |        |
|----------------|--------|--------|
|                | Design | Actual |
| Motor MFG      | -      | NL     |
| Frame          | -      | NL     |
| Horsepower     | 1      | 1      |
| Motor Rpm      | -      | NL     |
| Phase          | 1      | 1      |
| Rated Voltage  | 120    | 115    |
| Rated Amperage | -      | NL     |

| Drive Data         |        |
|--------------------|--------|
|                    | Actual |
| Motor Sheave Size  | DD     |
| Motor Bore Size    | DD     |
| Motor Sheave SetPt | DD     |
| Fan Sheave Size    | DD     |
| Fan Sheave Bore    | DD     |
| Belt CL Distance   | DD     |
| Num of Belts       | DD     |
| Belt Size          | DD     |
| Belt Alignment     | DD     |

| Test Data              |        |          |
|------------------------|--------|----------|
|                        | Design | Actual   |
| SF CFM                 | 1450   | 3043 [1] |
| SF RPM                 | -      | DD       |
| RA CFM                 | 950    | 2008 [2] |
| OA CFM                 | 500    | 1035 [3] |
| RL Voltage             | -      | 116      |
| RL Amperage            | -      | 10.3     |
| SF Rotation            | -      | CCW      |
| SF System SetPt        | -      | 17       |
| RA Damper Position     | -      | 100%     |
| Min OA Damper Position | -      | 25%      |
| Min OA Damper Type     | -      | MANUAL   |
| OA Enthalpy Setpt      | -      | N/A      |

| Performance Data |        |        |
|------------------|--------|--------|
|                  | Design | Actual |
| MA Plenum SP     | -      | -0.49" |
| Fan Suction SP   | -      | -0.72" |
| Fan Discharge SP | -      | 0.37"  |
| Total ESP        | 0.75"  | 0.86"  |
| Fan Total SP     | -      | 1.09"  |

| General                    |        |
|----------------------------|--------|
|                            | Actual |
| Fan Rotation Correct       | YES    |
| Unit Filters Clean         | YES    |
| Condensate Drain Installed | YES    |

Completed By: David Nicolas Sanchez on 12/10/2025

Notes:

- [1] FUR-1 & FUR-2 SERVE SAME DIFFUSER LINES. SUPPLY SHARE SAME DUCTS.
- [2] FUR-1 & FUR-2 SHARE THE SAME RETURNS.
- [3] FUR-1 & FUR-2 SHARE THE SAME OA DUCT

Written By: David Nicolas Sanchez on 12/10/2025

## Unit Data - PHOTO LOG



12/10/2025

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

System/Unit: AHU/RTU



Asset: FUR2

AREA:DINING

| Unit Data           |                 |                 |
|---------------------|-----------------|-----------------|
|                     | Design          | Actual          |
| MFG                 | CARRIER         | CARRIER         |
| Serial Num          | -               | 3625A45109      |
| Model Num           | 59SC6A080M21-20 | 59SC6A080M21-20 |
| Type                | FUR             | FUR             |
| Configuration       | VERTICAL        | VERTICAL        |
| Num Final Filter 1  | -               | 1               |
| Final Filter Size 1 | -               | 25X21.25        |

| Motor Data     |        |        |
|----------------|--------|--------|
|                | Design | Actual |
| Motor MFG      | -      | NL     |
| Frame          | -      | NL     |
| Horsepower     | 1      | 1      |
| Motor Rpm      | -      | NL     |
| Phase          | 1      | 1      |
| Rated Voltage  | 120    | 120    |
| Rated Amperage | -      | NL     |

| Drive Data         |        |
|--------------------|--------|
|                    | Actual |
| Motor Sheave Size  | DD     |
| Motor Bore Size    | DD     |
| Motor Sheave SetPt | DD     |
| Fan Sheave Size    | DD     |
| Fan Sheave Bore    | DD     |
| Belt CL Distance   | DD     |
| Num of Belts       | DD     |
| Belt Size          | DD     |
| Belt Alignment     | DD     |

| Test Data              |        |        |
|------------------------|--------|--------|
|                        | Design | Actual |
| SF CFM                 | 1450   | 3043   |
| SF RPM                 | -      | DD     |
| RA CFM                 | 950    | 2008   |
| OA CFM                 | 500    | 1035   |
| RL Voltage             | -      | 116    |
| RL Amperage            | -      | 10.2   |
| SF Rotation            | -      | CCW    |
| SF System SetPt        | -      | 17     |
| RA Damper Position     | -      | N/A    |
| Min OA Damper Position | -      | N/A    |
| Min OA Damper Type     | -      | N/A    |
| OA Enthalpy Setpt      | -      | N/A    |

| Performance Data |        |        |
|------------------|--------|--------|
|                  | Design | Actual |
| MA Plenum SP     | -      | -0.49" |
| Fan Suction SP   | -      | -0.63" |
| Fan Discharge SP | -      | 0.37"  |
| Total ESP        | 0.75"  | 0.86"  |
| Fan Total SP     | -      | 1.00"  |

| General                    |        |
|----------------------------|--------|
|                            | Actual |
| Fan Rotation Correct       | YES    |
| Unit Filters Clean         | YES    |
| Condensate Drain Installed | YES    |

Completed By: David Nicolas Sanchez on 12/10/2025

## Unit Data - PHOTO LOG



12/10/2025

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

## AHU/RTU



**Diffuser Supply (GRD)**

**FUR2/DINING**

| Asset      |           |      |      |            |    |        |        |           |             |
|------------|-----------|------|------|------------|----|--------|--------|-----------|-------------|
| Asset Name | Location  | Type | Size | DESIGN CFM | AK | CFM(1) | CFM(2) | FINAL CFM | % to design |
| SGRD1      | ORDERLINE | SR1  | 14"  | 600        | 1  | 752    | 568    | 568       | 94.7        |
| SGRD2      | ORDERLINE | SR1  | 14"  | 600        | 1  | 645    | 554    | 554       | 92.3        |
| SGRD3      | ORDERLINE | SR1  | 14"  | 600        | 1  | 697    | 573    | 573       | 95.5        |
| SGRD4      | ORDERLINE | SR1  | 14"  | 600        | 1  | 526    | 538    | 558       | 93.0        |
| SGRD5      | ORDERLINE | SR1  | 14"  | 600        | 1  | 372    | 542    | 542       | 90.3        |
| SGRD6      | RESTROOM  | CD3  | 6"   | 50         | 1  | 62     | 54     | 54        | 108.0       |
| SGRD7      | RESTROOM  | CD3  | 6"   | 50         | 1  | 86     | 51     | 51        | 102.0       |
| SGRD8      | BOH       | CD1  | 8"   | 150        | 1  | 238    | 143    | 143       | 95.3        |
| Total      |           |      |      | 3250       |    | 3378   | 3023   | 3043      | 93.63%      |

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

System/Unit: AHU/RTU



Asset: FUR3

AREA:KITCHEN

| Unit Data           |                 |                 |
|---------------------|-----------------|-----------------|
|                     | Design          | Actual          |
| MFG                 | CARRIER         | CARRIER         |
| Serial Num          | -               | NL              |
| Model Num           | 59SC6A080M21-20 | 59SC6A080M21-20 |
| Type                | FUR             | FUR             |
| Configuration       | VERTICAL        | VERTICAL        |
| Num Final Filter 1  | -               | 1               |
| Final Filter Size 1 | -               | 25X21.25        |

| Motor Data     |        |        |
|----------------|--------|--------|
|                | Design | Actual |
| Motor MFG      | -      | NL     |
| Frame          | -      | NL     |
| Horsepower     | 1      | 1      |
| Motor Rpm      | -      | NL     |
| Phase          | 1      | 1      |
| Rated Voltage  | 120    | 120    |
| Rated Amperage | -      | NL     |

| Drive Data         |        |
|--------------------|--------|
|                    | Actual |
| Motor Sheave Size  | DD     |
| Motor Bore Size    | DD     |
| Motor Sheave SetPt | DD     |
| Fan Sheave Size    | DD     |
| Fan Sheave Bore    | DD     |
| Belt CL Distance   | DD     |
| Num of Belts       | DD     |
| Belt Size          | DD     |
| Belt Alignment     | DD     |

| Test Data              |        |        |
|------------------------|--------|--------|
|                        | Design | Actual |
| SF CFM                 | 1600   | 1604   |
| SF RPM                 | -      | DD     |
| RA CFM                 | 1350   | 1366   |
| OA CFM                 | 250    | 238    |
| RL Voltage             | -      | 116    |
| RL Amperage            | -      | 10.7   |
| SF Rotation            | -      | CCW    |
| SF System SetPt        | -      | 17     |
| RA Damper Position     | -      | 100%   |
| Min OA Damper Position | -      | 20%    |
| Min OA Damper Type     | -      | MANUAL |

| Performance Data |        |        |
|------------------|--------|--------|
|                  | Design | Actual |
| MA Plenum SP     | -      | -0.84" |
| Fan Suction SP   | -      | -1.06" |
| Fan Discharge SP | -      | 0.29"  |
| Total ESP        | 0.75"  | 1.13"  |
| Fan Total SP     | -      | 1.35"  |

| General                    |        |
|----------------------------|--------|
|                            | Actual |
| Fan Rotation Correct       | YES    |
| Unit Filters Clean         | YES    |
| Condensate Drain Installed | YES    |

Completed By: David Nicolas Sanchez on 12/10/2025

## Unit Data - PHOTO LOG



12/10/2025

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

## AHU/RTU



**Diffuser Supply (GRD)**

**FUR3/KITCHEN**

| Asset      |           |      |      |            |    |        |        |           |             |
|------------|-----------|------|------|------------|----|--------|--------|-----------|-------------|
| Asset Name | Location  | Type | Size | DESIGN CFM | AK | CFM(1) | CFM(2) | FINAL CFM | % to design |
| SGRD1      | KITCHEN   | CD2  | 8"   | 340        | 1  | 315    | 315    | 315       | 92.6        |
| SGRD2      | KITCHEN   | CD2  | 8"   | 340        | 1  | 336    | 336    | 336       | 98.8        |
| SGRD3      | SERVELINE | CD2  | 8"   | 340        | 1  | 332    | 332    | 332       | 97.6        |
| SGRD4      | SERVELINE | CD2  | 8"   | 340        | 1  | 310    | 310    | 310       | 91.2        |
| SGRD5      | SERVELINE | CD2  | 8"   | 340        | 1  | 311    | 311    | 311       | 91.5        |
| Total      |           |      |      | 1700       |    | 1604   | 1604   | 1604      | 94.35%      |

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

## System/Unit: AHU/RTU



Asset: FUR4

AREA:KITCHEN

| Unit Data           |                 |                 |
|---------------------|-----------------|-----------------|
|                     | Design          | Actual          |
| MFG                 | CARRIER         | CARRIER         |
| Serial Num          | -               | 3625A45101      |
| Model Num           | 59SC6A080M21-20 | 59SC6A080M21-20 |
| Type                | FUR             | FUR             |
| Configuration       | VERTICAL        | VERTICAL        |
| Num Final Filter 1  | -               | 1               |
| Final Filter Size 1 | -               | 25X21.25        |

| Motor Data     |        |        |
|----------------|--------|--------|
|                | Design | Actual |
| Motor MFG      | -      | NL     |
| Frame          | -      | NL     |
| Horsepower     | 1      | 1      |
| Motor Rpm      | -      | NL     |
| Phase          | 1      | 1      |
| Rated Voltage  | 120    | 115    |
| Rated Amperage | -      | NL     |

| Drive Data         |        |
|--------------------|--------|
|                    | Actual |
| Motor Sheave Size  | DD     |
| Motor Bore Size    | DD     |
| Motor Sheave SetPt | DD     |
| Fan Sheave Size    | DD     |
| Fan Sheave Bore    | DD     |
| Belt CL Distance   | DD     |
| Num of Belts       | DD     |
| Belt Size          | DD     |
| Belt Alignment     | DD     |

| Test Data              |        |        |
|------------------------|--------|--------|
|                        | Design | Actual |
| SF CFM                 | 1600   | 1515   |
| SF RPM                 | -      | DD     |
| RA CFM                 | 1350   | 1275   |
| OA CFM                 | 250    | 240    |
| RL Voltage             | -      | 116    |
| RL Amperage            | -      | 10.7   |
| SF Rotation            | -      | CCW    |
| SF System SetPt        | -      | 17     |
| RA Damper Position     | -      | 100%   |
| Min OA Damper Position | -      | 20%    |
| Min OA Damper Type     | -      | MANUAL |
| OA Enthalpy Setpt      | -      | N/A    |

| Performance Data |        |        |
|------------------|--------|--------|
|                  | Design | Actual |
| MA Plenum SP     | -      | -1.09" |
| Fan Suction SP   | -      | -1.33" |
| Fan Discharge SP | -      | 0.20"  |
| Total ESP        | 0.75"  | 1.29"  |
| Fan Total SP     | -      | 1.53"  |

| General                    |        |
|----------------------------|--------|
|                            | Actual |
| Fan Rotation Correct       | YES    |
| Unit Filters Clean         | YES    |
| Condensate Drain Installed | YES    |

Completed By: David Nicolas Sanchez on 12/10/2025

## Unit Data - PHOTO LOG



12/10/2025

**National TAB**  
 Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA  
**AHU/RTU**



**Diffuser Supply (GRD)**

**FUR4/KITCHEN**

| <b>Asset</b>      |                 |             |             |                   |           |               |               |                  |                    |
|-------------------|-----------------|-------------|-------------|-------------------|-----------|---------------|---------------|------------------|--------------------|
| <b>Asset Name</b> | <b>Location</b> | <b>Type</b> | <b>Size</b> | <b>DESIGN CFM</b> | <b>AK</b> | <b>CFM(1)</b> | <b>CFM(2)</b> | <b>FINAL CFM</b> | <b>% to design</b> |
| SGRD1             | HOOD            | ACPSP       | N/A         | 700               | 5.23      | 709           | 709           | 709              | 101.3              |
| SGRD2             | KITCHEN         | CD-2        | 8"          | 340               | 1         | 313           | 313           | 313              | 92.1               |
| SGRD3             | BOH             | CD-1        | 10"         | 250               | 1         | 240           | 240           | 240              | 96.0               |
| SGRD4             | BOH             | CD-1        | 10"         | 250               | 1         | 253           | 253           | 253              | 101.2              |
| <b>Total</b>      |                 |             |             | <b>1540</b>       |           | <b>1515</b>   | <b>1515</b>   | <b>1515</b>      | <b>98.38%</b>      |

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

## System/Unit: FAN - Exhaust



Asset: EF1

AREA:COOKLINE

| Unit Data     |             |             |
|---------------|-------------|-------------|
|               | Design      | Actual      |
| MFG           | CAPTIVEAIRE | CAPTIVEAIRE |
| Model Num     | SIF15DD     | SIF15DD     |
| Serial Num    | -           | 6887814     |
| Type          | UPBLAST     | INLINE      |
| Configuration | VERTICAL    | VERTICAL    |

| Motor Data       |        |        |
|------------------|--------|--------|
|                  | Design | Actual |
| Motor MFG        | -      | NL     |
| Frame            | -      | NL     |
| Horsepower       | 2      | 2      |
| Motor Rpm        | -      | NL     |
| Phase            | 3      | 3      |
| Voltage (rated)  | 208    | 208    |
| Amperage (rated) | -      | NL     |
| Service Factor   | -      | NL     |

| Test Data        |        |         |
|------------------|--------|---------|
|                  | Design | Actual  |
| CFM              | 2550   | 2609    |
| Fan RPM          | 1805   | 45.2HZ  |
| Fan Rotation     | -      | CCW     |
| Motor RPM        | -      | 45.2HZ  |
| System SetPt     | -      | 45.2HZ  |
| RL Voltage       | -      | 88@VFD  |
| RL Amperage      | -      | 9.3@VFD |
| Total ESP        | 1.20"  | N/A     |
| Fan Inlet SP     | -      | N/A     |
| Fan Discharge SP | -      | N/A     |

Completed By: David Nicolas Sanchez on 12/10/2025

## Unit Data - PHOTO LOG



12/10/2025

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

System/Unit: FAN - Exhaust



Asset: EF2

AREA:RESTROOM

| Unit Data     |              |            |
|---------------|--------------|------------|
|               | Design       | Actual     |
| MFG           | WHISPERGREEN | PANASONIC  |
| Model Num     | FV-0511VK2   | FV-0511VK3 |
| Serial Num    | -            | 50219      |
| Type          | INLINE       | CEILING    |
| Configuration | VERTICAL     | VERTICAL   |

| Test Data    |        |        |
|--------------|--------|--------|
|              | Design | Actual |
| CFM          | 80     | 82     |
| Fan RPM      | -      | DD     |
| Fan Rotation | -      | CCW    |
| Motor RPM    | -      | DD     |
| System SetPt | -      | 100CFM |

| Motor Data       |        |           |
|------------------|--------|-----------|
|                  | Design | Actual    |
| Motor MFG        | -      | PANASONIC |
| Frame            | -      | NL        |
| Horsepower       | -      | NL        |
| Motor Rpm        | -      | NL        |
| Phase            | 1      | 1         |
| Voltage (rated)  | 120    | 120       |
| Amperage (rated) | -      | 0.37      |
| Service Factor   | -      | NL        |

Completed By: David Nicolas Sanchez on 12/10/2025

**Unit Data - PHOTO LOG**



**12/10/2025**

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

System/Unit: FAN - Exhaust



Asset: EF3

AREA:RESTROOM

| Unit Data     |              |            |
|---------------|--------------|------------|
|               | Design       | Actual     |
| MFG           | WHISPERGREEN | PANASONIC  |
| Model Num     | FV-0511VK2   | FV-0511VK3 |
| Serial Num    | -            | 50219      |
| Type          | INLINE       | CEILING    |
| Configuration | VERTICAL     | VERTICAL   |

| Test Data    |        |        |
|--------------|--------|--------|
|              | Design | Actual |
| CFM          | 80     | 88     |
| Fan RPM      | -      | DD     |
| Fan Rotation | -      | CCW    |
| Motor RPM    | -      | DD     |
| System SetPt | -      | 100CFM |

| Motor Data       |        |           |
|------------------|--------|-----------|
|                  | Design | Actual    |
| Motor MFG        | -      | PANASONIC |
| Frame            | -      | NL        |
| Horsepower       | -      | NL        |
| Motor Rpm        | -      | NL        |
| Phase            | 1      | 1         |
| Voltage (rated)  | 120    | 120       |
| Amperage (rated) | -      | 0.37      |
| Service Factor   | -      | NL        |

Completed By: David Nicolas Sanchez on 12/10/2025

**Unit Data - PHOTO LOG**



**12/10/2025**

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

## System/Unit: FAN - Supply



Asset: MAU1

AREA:HOOD

| Unit Data     |              |              |
|---------------|--------------|--------------|
|               | Design       | Actual       |
| MFG           | CAPTIVEAIRE  | CAPTIVEAIRE  |
| Model Num     | A1-D.250-15D | A1-D.250-15D |
| Serial Num    | -            | 6887814      |
| Type          | MAU          | MAU          |
| Configuration | VERTICAL     | VERTICAL     |

| Motor Data       |        |        |
|------------------|--------|--------|
|                  | Design | Actual |
| Motor MFG        | -      | NEMA   |
| Frame            | -      | NL     |
| Horsepower       | 1.000  | 1.00   |
| Motor Rpm        | -      | 1740   |
| Phase            | 3      | 3      |
| Voltage (rated)  | 208    | 230    |
| Amperage (rated) | -      | 2.90   |
| Service Factor   | -      | 1.15   |

| Gas Heat                  |        |        |
|---------------------------|--------|--------|
|                           | Design | Actual |
| Heater Operates (y/n)     | -      | Y      |
| Flame Status (pass/fail)  | -      | PASS   |
| Inlet Air Temp SetPt      | 55     | 55     |
| Discharge Air Temp SetPt  | 60     | 60     |
| Air Flow Switch SP Actual | -      | -0.32" |

| Test Data        |        |         |
|------------------|--------|---------|
|                  | Design | Actual  |
| CFM              | 1300   | 1402    |
| SF RPM           | 1574   | 1711    |
| Motor RPM        | -      | 1711    |
| SF System SetPt  | -      | 59HZ    |
| RL Voltage       | -      | 174@VFD |
| RL Amperage      | -      | 2.4@VFD |
| Total ESP        | -      | N/A     |
| Fan Discharge SP | -      | N/A     |

| General              |        |
|----------------------|--------|
|                      | Actual |
| Fan Rotation Correct | YES    |

Completed By: David Nicolas Sanchez on 12/10/2025

## Unit Data - PHOTO LOG



12/10/2025

# National TAB

Project: 12-08-25 CHIPOTLE #5187 CAMAS, WA

## System/Unit: Kitchen Hood Type I



Asset: HD1

AREA:COOKLINE

| Unit Data            |                   |                   |
|----------------------|-------------------|-------------------|
|                      | Design            | Actual            |
| MFG                  | CAPTIVEAIRE       | CAPTIVEAIRE       |
| Model Num            | 5424 ND-2-ACPSP-F | 5424 ND-2-ACPSP-F |
| Job / Serial Num     | -                 | 6887814           |
| Type                 | TYPE I CANOPY     | TYPE I CANOPY     |
| Hood length          | 153"              | 153"              |
| Hood Width           | 54"               | 54"               |
| Supply Plenum Type   | -                 | ACPSP             |
| Supply Plenum Width  | 9"                | 9"                |
| Supply Plenum Length | 165"              | 165"              |

| Test Data Exhaust       |                      |                      |
|-------------------------|----------------------|----------------------|
|                         | Design               | Actual               |
| Filter Type             | CAPTRATE SOLO FILTER | CAPTRATE SOLO FILTER |
| Filter Size 1           | 16X16                | 16X16                |
| Filter Qty 1            | 9                    | 9                    |
| Filter AK factor size 1 | 1.62                 | 1.62                 |
| Filter Total AK Area    | 14.58                | 14.58                |
| Filter1 FPM             | -                    | 160                  |
| Filter2 FPM             | -                    | 168                  |
| Filter3 FPM             | -                    | 185                  |
| Filter4 FPM             | -                    | 203                  |
| Filter5 FPM             | -                    | 206                  |
| Filter6 FPM             | -                    | 191                  |
| Filter7 FPM             | -                    | 170                  |
| Filter8 FPM             | -                    | 169                  |
| Filter9 FPM             | -                    | 164                  |
| Filter Ave FPM(corr)    | -                    | 179                  |
| CFM                     | 2550                 | 2609                 |

| Cooking Equipment |         |
|-------------------|---------|
|                   | Actual  |
| Item 1            | FRYER   |
| Item 2            | FRYER   |
| Item 3            | STOVE   |
| Item 4            | GRIDDLE |


| Test Data Supply |        |        |
|------------------|--------|--------|
|                  | Design | Actual |
| Total Area       | 10.31  | 10.31  |
| Kv factor (Vel)  | 0.81   | 0.81   |
| Num of Readings  | -      | 12     |
| Reading1 FPM     | -      | 158    |
| Reading2 FPM     | -      | 123    |
| Reading3 FPM     | -      | 154    |
| Reading4 FPM     | -      | 185    |
| Reading5 FPM     | -      | 187    |
| Reading6 FPM     | -      | 132    |
| Reading7 FPM     | -      | 132    |
| Reading8 FPM     | -      | 184    |
| Reading9 FPM     | -      | 219    |
| Reading10 FPM    | -      | 164    |
| Reading11 FPM    | -      | 181    |
| Reading12 FPM    | -      | 205    |
| Ave FPM(corr)    | -      | 168    |
| CFM              | 1300   | 1402   |

Completed By: David Nicolas Sanchez on 12/10/2025

## Unit Data - PHOTO LOG



12/10/2025

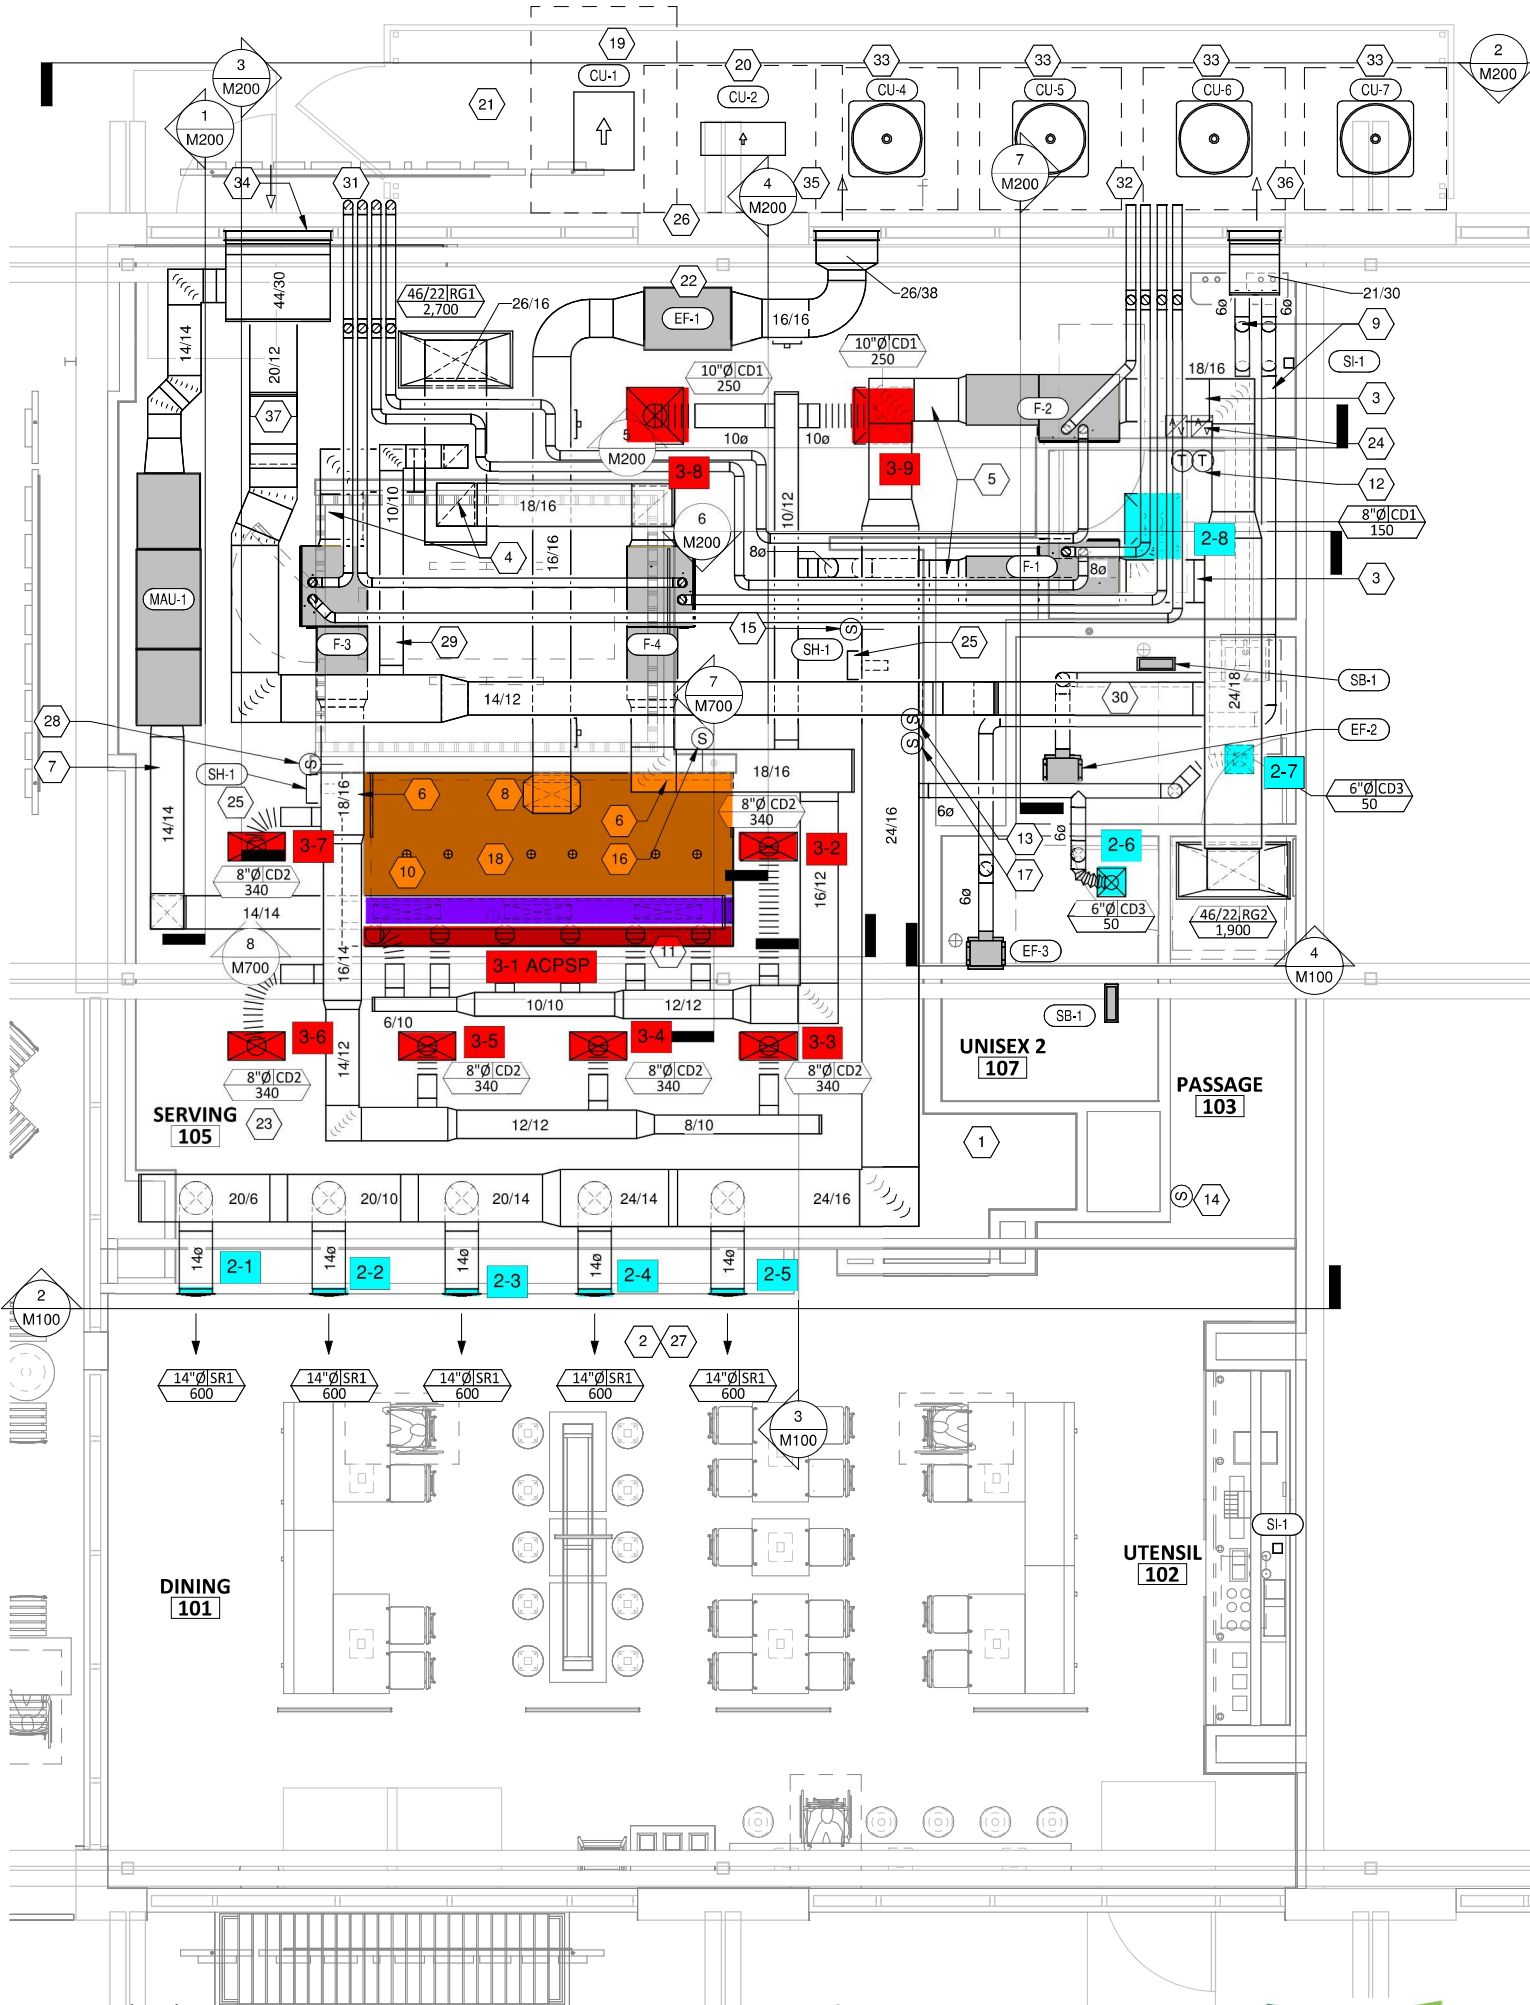

### AIR BALANCE SCHEDULE

| UNIT          | AREA SERVED | HVAC SUPPLY |        | HVAC RETURN |        | HVAC OUTDOOR |        | OA %   |        | HOOD MAKE-UP |        | HOOD EXHAUST |        | GENERAL EXH. |        |
|---------------|-------------|-------------|--------|-------------|--------|--------------|--------|--------|--------|--------------|--------|--------------|--------|--------------|--------|
|               |             | DESIGN      | ACTUAL | DESIGN      | ACTUAL | DESIGN       | ACTUAL | DESIGN | ACTUAL | DESIGN       | ACTUAL | DESIGN       | ACTUAL | DESIGN       | ACTUAL |
| FUR 1&2       | DINING      | 2900        | 3043   | 1900        | 2008   | 1000         | 1035   | 34.5%  | 34.0%  |              |        |              |        |              |        |
| FUR 3&4       | KITCHEN     | 3200        | 3119   | 2700        | 2641   | 500          | 478    | 15.6%  | 15.3%  |              |        |              |        |              |        |
| MUA-1         | KITCHEN HD  |             |        |             |        |              |        |        |        | 1300         | 1402   |              |        |              |        |
| EF-1          | KITCHEN HD  |             |        |             |        |              |        |        |        |              |        | 2550         | 2609   |              |        |
| EF-2&3        | RESTROOM    |             |        |             |        |              |        |        |        |              |        |              |        | 160          | 170    |
| <b>TOTALS</b> |             | 6100        | 6162   | 4600        | 4649   | 1500         | 1513   |        |        | 1300         | 1402   | 2550         | 2609   | 160          | 170    |

#### NET BUILDING AIRFLOW CALCULATION

| TOTALS             | DESIGN    | ACTUAL     |
|--------------------|-----------|------------|
| TOTAL OA           | 2800      | 2915       |
| TOTAL EXHAUST      | 2710      | 2779       |
| <b>NET AIRFLOW</b> | <b>90</b> | <b>136</b> |

| DOOR TESTED    | BUILDING PRESSURE MEASUREMENTS (IN. H2O) |
|----------------|--|
| FRONT          | 0.0026                                   |
| SIDE           | 0.0015                                   |
| REAR           | 0.0009                                   |
| <b>AVERAGE</b> | <b>0.0017</b>                            |

#### FINAL CHECKS

- ACTUAL NET AIRFLOW COINCIDES WITH DESIGN: ✓

---

- MEASURED PRESSURES COINCIDES WITH ACTUAL NET AIRFLOW: ✓

---

- PRESSURE FALLS WITHIN IMC TOLERANCE OF +/-0.02" W.C. ✓

NOTES:
