

PlanGrid Task Report - Jan 23, 2025

Prepared by Michael McDonnell

Jan 23, 2025

Description

4 tasks in this report.

Contents

#108 [EXHA 509] [NEW] Grease exhaust duct Paint.....	2
#107 [CNTL 508] [NEW] Controls labeling.....	3
#106 [UNIT 504][NEW] Equipment Fresh Air Tempering	5
#105 [UNIT 999][NEW](MISC) AC-1 OA Damper Feedback.....	6

#108 [EXHA 509] [NEW] Grease exhaust duct Paint

Status

Open

Created

Jan 23, 2025 10:07 AM
mmcdonnell@nationaltab.com

Type

Issue

Last Updated

Jan 23, 2025 2:46 PM

Description

Grease duct is painted per specification. However, rust is showing through in several spots. Recommend this is addressed.

Photos



IMG_4130

Michael McDonnell

Jan 23, 2025 2:46 PM



IMG_4129

Michael McDonnell

Jan 23, 2025 2:46 PM

L05138 Charlotte Hall FSU (MD)

29920 Three Notch Road, Charlotte Hall, Maryland

L01020005138

#107 [CNTL 508] [NEW] Controls labeling.

Status

Open

Created

Jan 23, 2025 9:50 AM
mmcdonnell@nationaltab.com

Type

Issue

Last Updated

Jan 23, 2025 2:47 PM

Description

Label all sensors, humidistats, thermostats, smoke annunciators and remote space mounted OADs, MODs, VFD's for which piece of equipment they serve.

Photos

L05138 Charlotte Hall FSU (MD)

29920 Three Notch Road, Charlotte Hall, Maryland

L01020005138



IMG_4006

Michael McDonnell

Jan 23, 2025 2:47 PM



IMG_3940

Michael McDonnell

Jan 23, 2025 2:47 PM



IMG_3939

Michael McDonnell

Jan 23, 2025 2:47 PM

#106 [UNIT 504][NEW] Equipment Fresh Air Tempering

Status

Open

Created

Jan 22, 2025 11:44 AM
mmcdonnell@nationaltab.com

Type

Issue

Last Updated

Jan 23, 2025 2:47 PM

Description

Units with Fresh Air Tempering kits are to have the discharge sensor routed per specification into the discharge duct via wiring portal. If Trane set turn-on/turn-off temps to 60/65 in Kitchen, 62/67 in Drive-Thru/Serving, 63/68 in Dining/Play Area.

Photos



IMG_4179

Michael McDonnell

Jan 23, 2025 2:47 PM

#105 [UNIT 999][NEW](MISC) AC-1 OA Damper Feedback

Status

Open

Created

Jan 22, 2025 11:39 AM
mmcdonnell@nationaltab.com

Type

Issue

Last Updated

Jan 22, 2025 11:44 AM

Description


AC-1 OA damper was not functional on arrival. The connector was damaged from the factory, MC corrected. Damper is now operating properly and goes to correct setpoint, however, damper feedback indicates damper is at 49%, when it is only at 25%. While damper is operating properly, recommend this issue is addressed while unit is under warranty.

Photos

L05138 Charlotte Hall FSU (MD)

29920 Three Notch Road, Charlotte Hall, Maryland


L01020005138

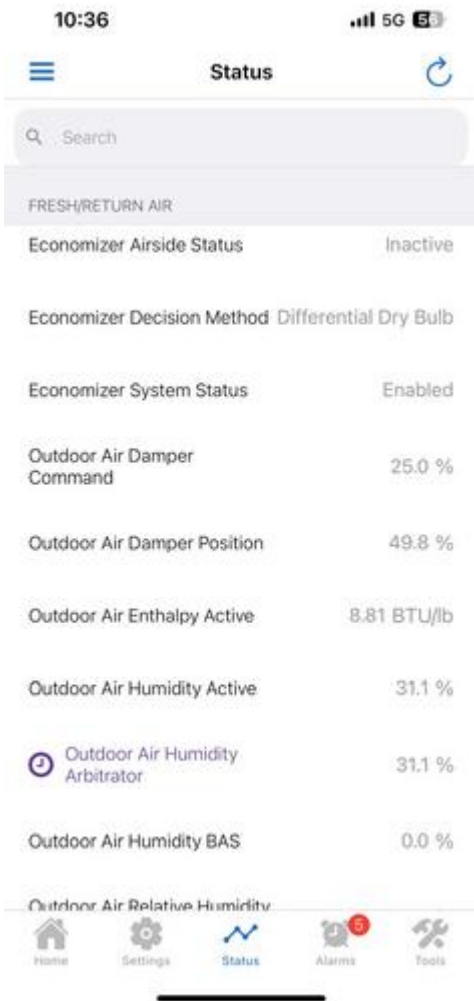

IMG_4137

Michael McDonnell

Jan 22, 2025 11:43 AM

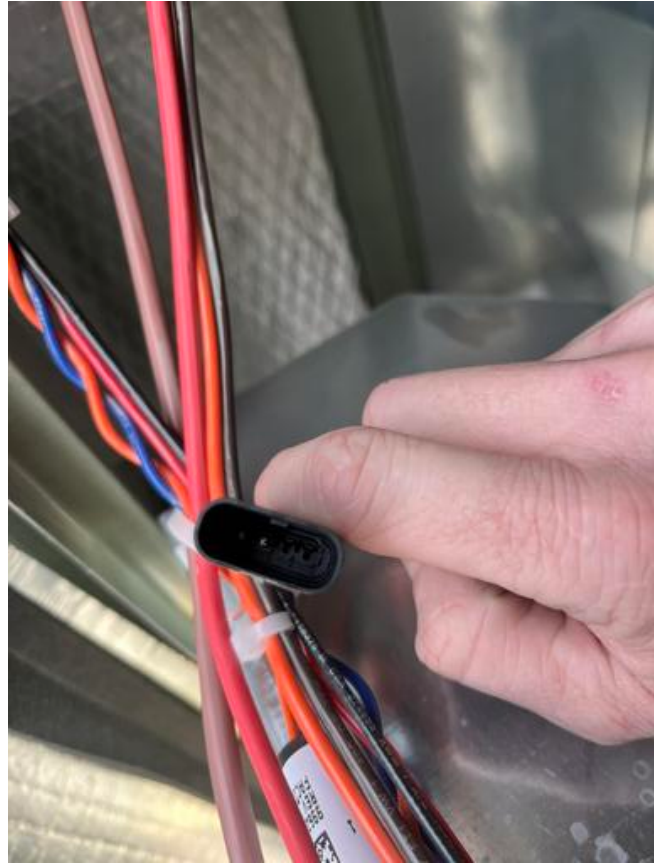

IMG_4040

Michael McDonnell

Jan 22, 2025 11:43 AM

L05138 Charlotte Hall FSU (MD)

29920 Three Notch Road, Charlotte Hall, Maryland

L01020005138



IMG_4041

Michael McDonnell

Jan 22, 2025 11:43 AM
