

# Final TAB Punchlist

Prepared by Jacob Davidson

Dec 23, 2024

## Description

12 tasks in this report.

## Contents

#141 [SITE 500] [NEW] TAB is complete. ....	2
#140 [CURT 501] [NEW] Air curtain power. ....	3
#139 [CURT 503] [NEW] Air curtain door switches. ....	4
#138 [CURT 505] [NEW] Air curtain remote switch installation. ....	5
#137 [DUCT 501] [NEW] Insulation stick pins. ....	6
#136 [UNIT 501] [NEW] Equipment low voltage diagrams. ....	7
#135 [DUCT 502] [NEW] Restroom round exhaust duct insulation. ....	9
#65 [CNTL 509] [NEW] Amerex pull labeling. ....	10
#30 [CNTL 508] [NEW] Controls labeling. ....	12
#27 [UNIT 510] [NEW] Gas inlet grommet. ....	15
#25 [EXHA 510] [NEW] Grease exhaust duct is not supported. ....	16
#24 [EXHA 508] [NEW] Exhaust fan G2 Drip Guard. ....	17

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774

**#141 [SITE 500] [NEW] TAB is complete.**

**Status**

Open

**Created**

Dec 23, 2024 11:25 AM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

**Description**

TAB is complete with only non-critical tasks open or all critical/non-critical tasks closed.

---

## #140 [CURT 501] [NEW] Air curtain power.

### Status

Open

### Created

Dec 19, 2024 11:00 AM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

### Description

Air curtain power does not cycle properly from local disconnect at time of TAB inspection.

### Photos



IMG\_0460

Jacob Davidson

Dec 19, 2024 11:02 AM



IMG\_0461

Jacob Davidson

Dec 19, 2024 11:02 AM

## #139 [CURT 503] [NEW] Air curtain door switches.

### Status

Open

### Created


Dec 19, 2024 10:54 AM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

### Description

Air curtain magnetic door switches are not installed correctly or not properly controlling mode activation in Auto at time of TAB inspection.

### Photos

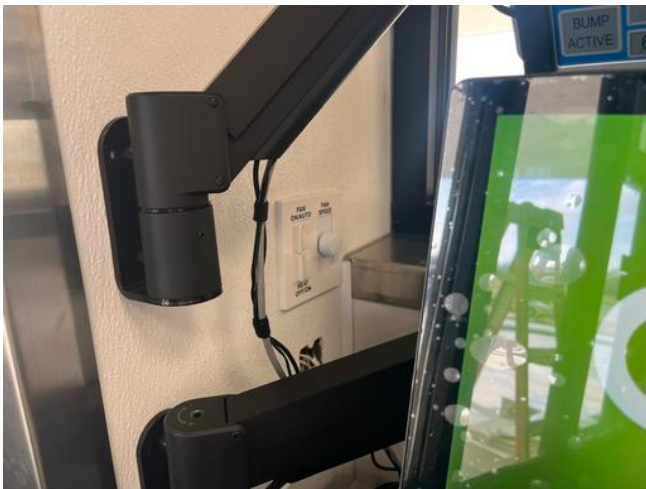

IMG\_0458

Jacob Davidson

Dec 19, 2024 11:02 AM



IMG\_0459

Jacob Davidson

Dec 19, 2024 11:02 AM

## #138 [CURT 505] [NEW] Air curtain remote switch installation.

### Status

Open

### Created

Dec 19, 2024 10:53 AM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

### Description

Air curtain remote switches are not installed or do not control curtain functions properly between modes (fan on / auto, heat on / off) at time of TAB inspection.

### Photos



IMG\_0457

Jacob Davidson

Dec 19, 2024 11:03 AM



IMG\_0456

Jacob Davidson

Dec 19, 2024 11:03 AM

# #137 [DUCT 501] [NEW] Insulation stick pins.

Status

Open

Created

Dec 19, 2024 8:56 AM

jacobd@nationaltab.com

Sheet

M-001

## Description

External insulation on bottom of ducts 24" or wider is to be supported by stick pins 18" on center. Cut pins and apply tape or mastic over stick pin washers.

## Photos



IMG\_0437

Jacob Davidson

Dec 19, 2024 8:56 AM

<p>1. THE CONTRACTOR SHALL VERIFY THE LOCATION AND DEPTH OF ALL EXISTING FOUNDATION AND FOOTING. ALL FOUNDATION AND FOOTING SHALL BE REPAIRED OR REPLACED AS NECESSARY TO SUPPORT THE PROPOSED STRUCTURE. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE LOCAL AUTHORITY.</p> <p>2. THE CONTRACTOR SHALL VERIFY THE LOCATION AND DEPTH OF ALL EXISTING FOUNDATION AND FOOTING. ALL FOUNDATION AND FOOTING SHALL BE REPAIRED OR REPLACED AS NECESSARY TO SUPPORT THE PROPOSED STRUCTURE. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE LOCAL AUTHORITY.</p>	<p>3. THE CONTRACTOR SHALL VERIFY THE LOCATION AND DEPTH OF ALL EXISTING FOUNDATION AND FOOTING. ALL FOUNDATION AND FOOTING SHALL BE REPAIRED OR REPLACED AS NECESSARY TO SUPPORT THE PROPOSED STRUCTURE. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE LOCAL AUTHORITY.</p> <p>4. THE CONTRACTOR SHALL VERIFY THE LOCATION AND DEPTH OF ALL EXISTING FOUNDATION AND FOOTING. ALL FOUNDATION AND FOOTING SHALL BE REPAIRED OR REPLACED AS NECESSARY TO SUPPORT THE PROPOSED STRUCTURE. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE LOCAL AUTHORITY.</p>	<p>5. THE CONTRACTOR SHALL VERIFY THE LOCATION AND DEPTH OF ALL EXISTING FOUNDATION AND FOOTING. ALL FOUNDATION AND FOOTING SHALL BE REPAIRED OR REPLACED AS NECESSARY TO SUPPORT THE PROPOSED STRUCTURE. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE LOCAL AUTHORITY.</p> <p>6. THE CONTRACTOR SHALL VERIFY THE LOCATION AND DEPTH OF ALL EXISTING FOUNDATION AND FOOTING. ALL FOUNDATION AND FOOTING SHALL BE REPAIRED OR REPLACED AS NECESSARY TO SUPPORT THE PROPOSED STRUCTURE. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE LOCAL AUTHORITY.</p>
<p><b>KITCHEN HOOD SYSTEMS NOTES</b></p> <p>1. THE CONTRACTOR SHALL VERIFY THE LOCATION AND DEPTH OF ALL EXISTING FOUNDATION AND FOOTING. ALL FOUNDATION AND FOOTING SHALL BE REPAIRED OR REPLACED AS NECESSARY TO SUPPORT THE PROPOSED STRUCTURE. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE LOCAL AUTHORITY.</p> <p>2. THE CONTRACTOR SHALL VERIFY THE LOCATION AND DEPTH OF ALL EXISTING FOUNDATION AND FOOTING. ALL FOUNDATION AND FOOTING SHALL BE REPAIRED OR REPLACED AS NECESSARY TO SUPPORT THE PROPOSED STRUCTURE. THE CONTRACTOR SHALL BE RESPONSIBLE FOR OBTAINING ALL NECESSARY PERMITS AND APPROVALS FROM THE LOCAL AUTHORITY.</p>		

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774

**#136 [UNIT 501] [NEW] Equipment low voltage diagrams**

**Status**

Open

**Created**


Dec 18, 2024 5:41 PM  
jacobd@nationaltab.com

**Sheet**

M-701

**Description**

Equipment missing  
laminated copy of controls  
detail low voltage wiring  
diagrams.

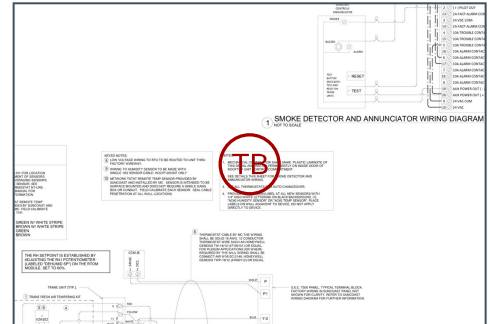

**Photos**



IMG\_0444

Jacob Davidson

Dec 18, 2024 5:43 PM



IMG\_0447

Jacob Davidson

Dec 18, 2024 5:43 PM

## 5774 Burlington (IA) FSU

241 Legacy Dr, Burlington, Iowa

L1020005774



IMG\_0443

**Jacob Davidson**

Dec 18, 2024 5:43 PM

---



## #65 [CNTL 509] [NEW] Amerex pull labeling.

### Status

Open

### Created

Dec 18, 2024 9:56 AM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

### Description

Label all Amerex pull stations for which hoods they serve. Per M-201 detail 1, label should be red bakelite label with 1/4" high white lettering indicating which hoods served.

### Photos



IMG\_0451

Jacob Davidson

Dec 19, 2024 10:42 AM



IMG\_0450

Jacob Davidson

Dec 19, 2024 10:42 AM

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774



IMG\_0436

**Jacob Davidson**

Dec 18, 2024 5:38 PM



IMG\_0435

**Jacob Davidson**

Dec 18, 2024 5:38 PM

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774

**#30 [CNTL 508] [NEW] Controls labeling.**

**Status**

Open

**Created**

Dec 16, 2024 3:51 PM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

**Description**

Label all sensors, humidistats, thermostats, smoke annunciators and remote space mounted OADs, MODs, VFD's for which piece of equipment they serve.

**Photos**



IMG\_0349

**Jacob Davidson**

Dec 16, 2024 3:59 PM



IMG\_0348

**Jacob Davidson**

Dec 16, 2024 3:59 PM

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774



IMG\_0350

**Jacob Davidson**

Dec 16, 2024 3:59 PM



IMG\_0346

**Jacob Davidson**

Dec 16, 2024 3:59 PM

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774



IMG\_0374

**Jacob Davidson**

Dec 16, 2024 3:59 PM

---

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774

**#27 [UNIT 510] [NEW] Gas inlet grommet.**

**Status**

Open

**Created**

Dec 16, 2024 3:48 PM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

**Description**

AC gas inlet grommet is missing at the gas line/RTU penetration point on AC1 and AC3

**Photos**



IMG\_0357

**Jacob Davidson**

Dec 16, 2024 4:00 PM



IMG\_0355

**Jacob Davidson**

Dec 16, 2024 4:00 PM

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774

**#25 [EXHA 510] [NEW] Grease exhaust duct is not supported.**

**Status**

Open

**Created**

Dec 16, 2024 3:45 PM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

**Description**

Exhaust duct is to be supported per kitchen hood exhaust fan detail on 6'0" centers and at each drop into the space.

**Comments**

Stands are on order.

Jacob Davidson Dec 19, 2024

**Photos**



IMG\_0353

Jacob Davidson

Dec 16, 2024 4:00 PM



IMG\_0354

Jacob Davidson

Dec 16, 2024 4:00 PM

**5774 Burlington (IA) FSU**

241 Legacy Dr, Burlington, Iowa

L1020005774

**#24 [EXHA 508] [NEW] Exhaust fan G2 Drip Guard**

**Status**

Open

**Created**

Dec 16, 2024 3:40 PM

[jacobd@nationaltab.com](mailto:jacobd@nationaltab.com)

**Description**

Exhaust fan G2 Drip Guard is missing.

**Photos**



IMG\_0351

**Jacob Davidson**

Dec 16, 2024 4:01 PM



IMG\_0352

**Jacob Davidson**

Dec 16, 2024 4:01 PM
