

Report By:

National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246



Report: Deficiency Report
Function: Test, Adjust, & Balance
Date: 11/11/2024
Completed By: National TAB

PROJECT

11-11-24 WAWA #5438 ALACHUA, FL

16304 NW US HWY 441

ALACHUA, FL 32615

Client

Wawa
260 West Baltimore Pike
Wawa, PA 19063

National TAB

Project: 11-11-24 WAWA #5438 ALACHUA, FL

Table Of Contents

Section	Page #
Issue Data	3

Issue List

- EF-1 Power
- EF-1 Vent 1 Damper
- EF-2 Power
- RTU-3 Diffuser 1 Damper
- RTU-3 Outside Air Damper

11-11-24 WAWA #5438 ALACHUA, FL

Project Issue Information

Issue Name : EF-1 Power
Description : EF-1 doesn't not have power. Recommend electrician wire power to the fan.
Created By : National TAB **Assigned To :** National TAB - Kristopher Passley
Status : Closed
Priority : **Urgent** **Asset Tag :**
Originated Date : 11/11/2024 - Kristopher Passley - National TAB

Project Issue File Details



11/11/2024

Project Issue Response Details

- **11/13/2024 National TAB - Kristopher Passley**
 - Issue is resolved: EF-1 now has power.



11-11-24 WAWA #5438 ALACHUA, FL

Project Issue Information

Issue Name : EF-1 Vent 1 Damper
Description : Damper missing from EF-1 Vent 1. This vent is 113.4% high and is preventing other vents from being in design. Recommend having mechanical install damper to allow all vents to be in design.
Created By : National TAB **Assigned To :** National TAB - Kristopher Passley
Status : Open
Priority : Urgent **Asset Tag :**
Originated Date : 11/13/2024 - Kristopher Passley - National TAB


Project Issue File Details



11/13/2024



11/13/2024

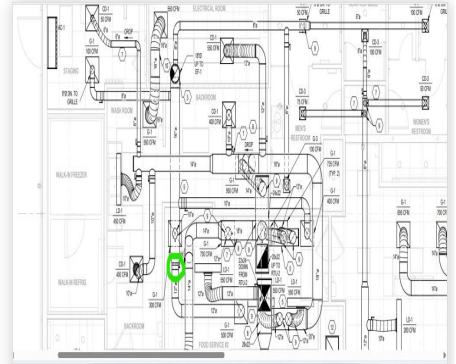

11/13/2024

11-11-24 WAWA #5438 ALACHUA, FL

Project Issue Information

Issue Name : EF-2 Power
Description : EF-2 doesn't not have power. Recommend electrician wire power to the fan.
Created By : National TAB **Assigned To :** National TAB - Kristopher Passley
Status : Closed
Priority : Urgent **Asset Tag :**
Originated Date : 11/11/2024 - Kristopher Passley - National TAB

Project Issue File Details



11/11/2024

Project Issue Response Details


- **11/13/2024 National TAB - Kristopher Passley**
 - Issue is resolved. EF-2 now has power.

11-11-24 WAWA #5438 ALACHUA, FL

Project Issue Information

Issue Name : RTU-3 Diffuser 1 Damoer
Description : Damper missing from RTU-3 Diffuser 1. Diffuser is at 120% and needs airflow to be reduced to have diffuser with design. Recommend mechanical install damper as per plan.
Created By : National TAB **Assigned To :** National TAB - Kristopher Passley
Status : Open
Priority : Urgent **Asset Tag :**
Originated Date : 11/13/2024 - Kristopher Passley - National TAB

Project Issue File Details

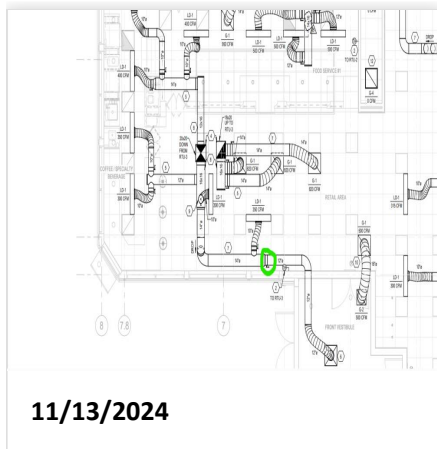

11-11-24 WAWA #5438 ALACHUA, FL


Project Issue Information

Issue Name : RTU-3 Outside Air Damper
Description : RTU-3 Outside Air damper is non-functional. When calibrating outside air in “Lennox Core” motor did not open fin. Recommend having mechanical service unit to resolve issue. Damper was manually set and marked.
Created By : National TAB **Assigned To :** National TAB - Kristopher Passley
Status : Open
Priority : Urgent **Asset Tag :**
Originated Date : 11/12/2024 - Kristopher Passley - National TAB

Project Issue File Details



11/12/2024

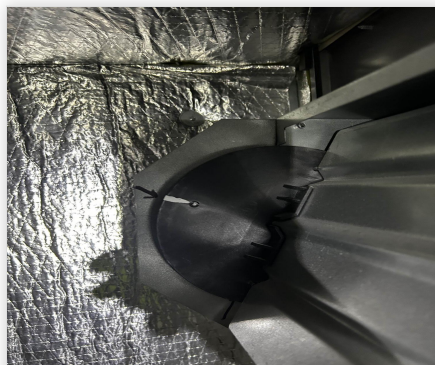

11/13/2024
