

Report By:

National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246



Report: TAB Punchlist
Function: Test, Adjust, & Balance
Date: 02/18/2025
Completed By: National TAB

PROJECT
02-17-25 CULVERS ALMA, MI

7520 N ALGER RD

ALMA , MI 48801

Client

Accurex
PO Box 410
Schofield, WI 54476

Issue List

- Missing dampers on RTU-2 (Kitchen)




02-17-25 CULVERS ALMA, MI


Project Issue Information

Issue Name : Missing dampers on RTU-2 (Kitchen)
Description : Diffuser 1-3,1-11,1-12 missing dampers. 1-3 is high on flow at 455/350CFM 1-11 is very high on flow at 782/350CFM unable to reduce airflow to these diffusers. Diffuser 1-12 was able to be restricted with duct straps to bring flow to design. Recommend Mechanical Contractor install dampers so these diffusers can be sufficiently balanced.
Created By : National TAB **Assigned To :** National TAB - Dylan Crisman
Status : Open
Priority : High **Asset Tag :**
Originated Date : 02/18/2025 - Dylan Crisman - National TAB


Project Issue File Details

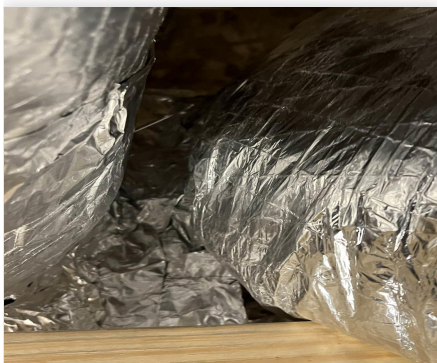

02/18/2025

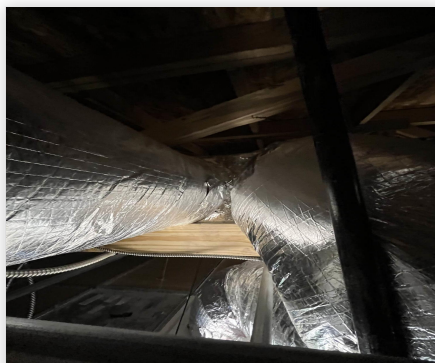

02/18/2025

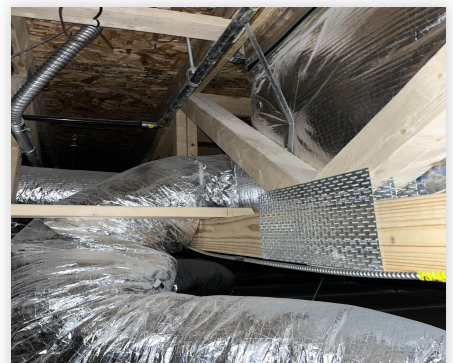

02/18/2025
