

Report By:

**National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246**

NATIONAL

TAB

Comfort. Under control.

**Report: ISSUES
Function: Test, Adjust, & Balance
Date: 04/24/2023**

**PROJECT
04-24-23 CULVERS - CAMDENTON, MO**

70 JACK CROWELL RD

CAMDENTON, MO 65020

Client

Accurex

PO Box 410

Schofield, WI 54476

National TAB

Project: 04-24-23 CULVERS - CAMDENTON, MO

Table Of Contents

Section	Page #
Issue Data	3



Comfort. Under control.

04-24-23 CULVERS - CAMDENTON, MO

Project Issue Information

Issue Name : Diffuser 2-15 is not installed

Description : Diffuser 2-15 for the electrical room is not installed. GC said diffuser should be on site and should be installed, but they just got the ceiling up back there so they were waiting until then. Tech cannot balance RTU2 until this is resolved.


Created By : National TAB

Assigned To : National TAB - Jacob Davidson

Status : Open

Originated Date : 04/24/2023 - Jacob Davidson - National TAB

Project Issue File Details

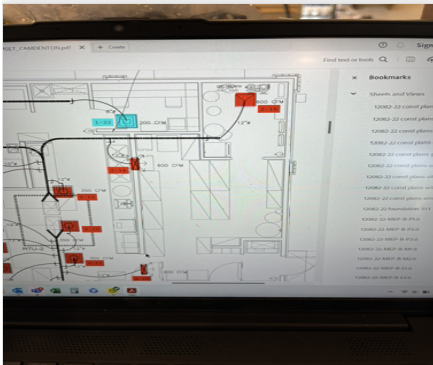

GRD.jpeg



Diffusermissing.jpeg



Comfort. Under control.

04-24-23 CULVERS - CAMDENTON, MO

Project Issue Information

Issue Name : EF1A not installed

Description : 75CFM Exhaust fan above the mop sink is not installed. I asked the GC and he said they had an extra fan in the end so he's going to see what can be done.


Created By : National TAB

Assigned To : National TAB - Jacob Davidson

Status : Open

Originated Date : 04/24/2023 - Jacob Davidson - National TAB

Project Issue File Details

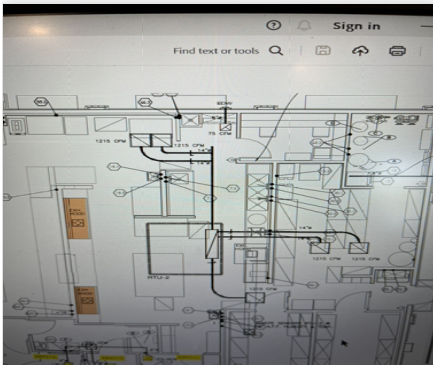

FANGRD.jpeg



Exhaustfanmissing.jpe...



Comfort. Under control.

04-24-23 CULVERS - CAMDENTON, MO

Project Issue Information

Issue Name : PRV1 employee restroom has no damper accessible

Description : PRV1 men and women restrooms have a face damper to adjust flow. The employee restroom does not have any damper visible. If there is a damper, it would have to be at the takeoff which is not accessible. Tech is unable to balance airflow without damper on diffuser in employee restroom.

Created By : National TAB

Assigned To : National TAB - Jacob Davidson

Status : Open

Originated Date : 04/24/2023 - Jacob Davidson - National TAB

Project Issue File Details



EmpRRr.jpeg



MenwowenRR.jpeg



Takeoff.jpeg



Comfort. Under control.

04-24-23 CULVERS - CAMDENTON, MO

Project Issue Information

Issue Name : PRV1 missing backdraft damper

Description : INFO ONLY Restroom exhaust fan is missing the backdraft damper at the curb on the roof. This needs to be installed but will not affect the scope of the TAB.


Created By : National TAB

Assigned To : National TAB - Jacob Davidson

Status : Open

Originated Date : 04/24/2023 - Jacob Davidson - National TAB

Project Issue File Details

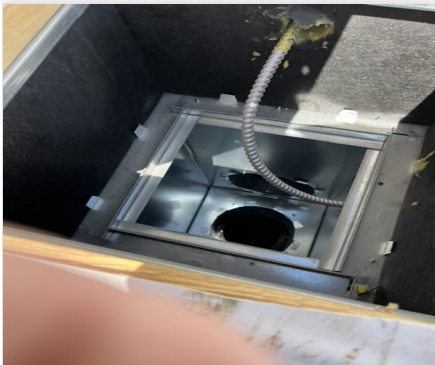

Duct.jpeg



PRV1.jpeg



Comfort. Under control.

04-24-23 CULVERS - CAMDENTON, MO

Project Issue Information

Issue Name : PRV2/PRV3 missing grease cups

Description : INFO ONLY The grease cups for both hood fans have not been installed. They will need to be installed for when the restaurant starts cooking. This does not affect scope of the TAB.

Created By : National TAB

Assigned To : National TAB - Jacob Davidson

Status : Open

Originated Date : 04/24/2023 - Jacob Davidson - National TAB

Project Issue File Details



PRV2.jpeg



PRV3.jpeg



Comfort. Under control.

04-24-23 CULVERS - CAMDENTON, MO

Project Issue Information

Issue Name : RTU1 noise when running.

Description : INFO ONLY RTU1 fan makes a noise when running. Tech inspected the fan and found nothing. The noise seems to be coming from the discharge. This does not affect the scope of the TAB.

Created By : National TAB

Assigned To : National TAB - Jacob Davidson

Status : Open

Originated Date : 04/24/2023 - Jacob Davidson - National TAB

Project Issue File Details

1. [Open](#) IMG_Noise.MOV
