



Comfort. Under control.

09-12 FIVE GUYS #0420 - HIGHLANDS RANCH, CO (RENEW)

CheckList Information

Name : 5 GUYS HVAC PERFORMACE EVALUATION **Status :** NotSubmitted
Assigned Organization : National TAB **Asset :**
Requesting Organization : National TAB

CheckList Item Details

STORE FRONT PICTURE



Screenshot_20221026_175347.jpg

ROOFTOP PICTURES (ADD THREE FROM DIFFERENT ANGLES)



20221026_135138.jpg



20221026_135125.jpg



20221026_135108.jpg

RTU1 (TAKE PICTURE OF UNIT)



20221026_135313.jpg

MFG & MODEL NUMBER

CARRIER 48TMF016

OA CFM

345 CFM

OA DAMPER POSITION

15% OPEN



20221026_135727.jpg

FAN SUCTION AND DISCHARGE PRESSURE

-0.22" FAN SUCTION 0.15" FAN DISCHARGE

BLOWER MOTOR RLA / FLA

7.1/7.2/7.1 FLA 15.8 5 HP

RTU2 (TAKE PICTURE OF UNIT)



20221026_135317.jpg

| | |
|--------------------|------------------------|
| MFG & MODEL NUMBER | TRANE YSC060A3EMA0WA10 |
| OA CFM | 660 CFM |
| OA DAMPER POSITION | E(100% OPEN) |



20221026_140142.jpg


| | |
|-------------------------------------|--------------------------|
| FAN SUCTION AND DISHCHARGE PRESSURE | -0.52" FAN SUCTION 0.11" |
| BLOWER MOTOR RLA / FLA | 5.6/5.8/1.2 FLA 6.2 1HP |
| RTU3 (TAKE PICTURE OF UNIT) | |



20221026_135327.jpg

MFG & MODEL NUMBER

TRANE YSC060A3RHA0L NOT FUNCTIONAL

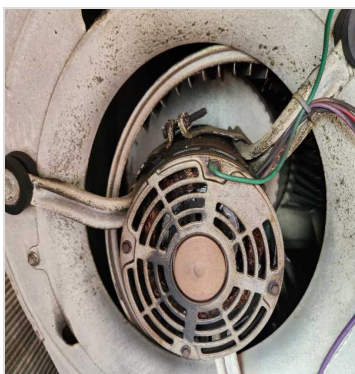

20221026_154835.jpg

OA CFM

0

OA DAMPER POSITION

E (100% OPEN)

FAN SUCTION AND DISCHARGE PRESSURE

0

BLOWER MOTOR RLA / FLA

0 FLA 6.2 0.9HP

KEF1 - HOOD 1 (TAKE PICTURE OF UNIT)



20221026_135333.jpg

| | |
|--------------------------------------|---------------|
| MFG & MODEL NUMBER | COOK 165VCRH |
| EXH-CFM | 836 CFM |
| MOTOR RLA / FLA | NA FLA 11/5.5 |
| KEF2 - HOOD 2 (TAKE PICTURE OF UNIT) | |



20221026_135334.jpg

| | |
|--|----------------------------|
| MFG & MODEL NUMBER | MARSHALL AIR SYSTEMS G1530 |
| EXH-CFM | 1419 CFM |
| MOTOR RLA / FLA | NA FLA 8.4/7.8 |
| MUA - ALL HOODS (TAKE PICTURE OF UNIT) | |



20221026_135349.jpg

MFG & MODEL NUMBER

ABSOLUTE AIR V1-HOM

MUA-CFM

365 CFM

MOTOR RLA/FLA

1.4/1.6/1.3 FLA 3.4

KITCHEN HOODS (TAKE PICTURE OF HOODS)




20221026_162503.jpg

CONTROLS AND PERFORMANCE

TAKE PICTURE OF THERMOSTATS AND WALL SENSORS



20221026_162611.jpg

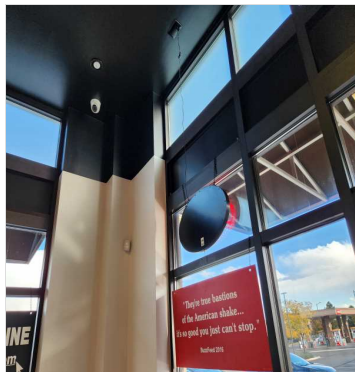

20221026_162545.jpg

ARE THERMOSTATS PROGRAMMED FOR OCCUPIED HOURS AND IS THE FAN IN "ON" MODE DURING OCCUPIED TIMES

YES

BUILDING PRESSURE (FINAL)

-0.0189"

HOOD CAPTURE (WITNESS COOKING OR SMOKE TEST)

KEF-1 50% CAPTURE KEF-2 100% CAPTURE JOSEPH

ANY COMMENTS:

Notes/Comments :
