

**Report By:**

National TAB  
1329 E. KEMPER ROAD  
SUITE 4210  
CINCINNATI, OH 45246



**Report: TAB Report**  
**Function: Test, Adjust, & Balance**  
**Date: 02/05/2026**  
**Completed By: National TAB**

**PROJECT**  
**03-02-26 QT #1730 FORSYTH, GA**

240 HAROLD G CLARKE PRKWY

FORSYTH, GA

**Client**

QUIKTRIP  
4705 SOUTH 129TH EAST AVENUE  
TULSA, OK 74134

# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

## Table Of Contents

<b>Section</b>	<b>Page #</b>
Summary	3
Issue Data	4
Checklist	6
RTU-1	12
RTU-2	15
RTU-3	18
RTU-4	21
EF-1 - Exhaust	24
Combi-Oven Grille	26
EF-2 - Exhaust	27
EF-3 - Hood Exhaust	29
Kitchen Hood Type I	31
File Data	33
GRD Layout	34



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA  
Function: Test, Adjust, & Balance

## Project Summary

### Project Summary

The summary below provides a quick understanding of our scope of work and general testing procedures. Enclosed in the report are further details about your building performance including recommendations, asset data, and pictures. Our focus is to work with the trades to remedy any issues or deficiencies during the actual field balancing and not after the balancing has occurred to achieve a positive environment and outcome. The level of success is determined by the availability of the trades, possible parts needed, or time constraints.

### RTU's (Roof Top Units)

Each of the RTU's was measured with a flow hood to establish total flow. The total flow was then adjusted via the VFD so that airflow fell within design tolerances. All diffusers on the kitchen RTU were balanced to the engineer's design flow. The diffusers on the sales floor were only adjusted when there were noticeable issues present like drafting or dampers that were found completely closed. The Hoods On outside air rate was set by first establishing the typical QT set point at the Emerson controller and then making manually adjustments on the roof. The hoods off airflow setpoint was found by adjusting the damper position at the Emerson controller until the design airflow was achieved. Outside air was measured by reading the intake air opening with a velocity grid and multiplying by the free area. After completion of TAB all overrides were released.

### Kitchen Exhaust Hood & Associated Fans

The kitchen exhaust fan was measured at the hood filter bay utilizing a velocity matrix and a manufacturer's correction factor. Each filter velocity is multiplied by the manufacturer's corrected area. The sum of these readings equals the total flow of the exhaust fans. The total flow of the exhaust was then adjusted to within tolerance of the design flow.

### Restroom Exhaust Fans

The restroom exhaust fans were measured with a flow hood. The total flow was balanced for the fan with the exception of the new grille over the combi-oven, which was balanced to the listed design.

### Final Building Tests

After completing the test and balance the final building pressure was measured. It was confirmed that the building pressure fell within acceptable tolerances and that the pressure measurement coincides with the actual and design net airflow. Any deviations from these standards are noted throughout the report. The hood capture was tested at the perimeter of the hood and the cook top level with the equipment heat on to ensure satisfactory hood capture and containment.

## Issue List

- EF-1 Detached Duct




**03-02-26 QT #1730 FORSYTH, GA**

**Project Issue Information**

**Issue Name :** EF-1 Detached Duct  
**Description :** Unable to balance diffuser EF1-1 as the individual duct is detached from the take off of the main duct. The GC was notified of the issue.  
**Created By :** National TAB                      **Assigned To :** National TAB - Dan Hertenstein  
**Status :** Closed  
**Priority :** Urgent                                      **Asset Tag :**  
**Originated Date :** 03/02/2026 - Anthony Taylor - National TAB

Project Issue File Details

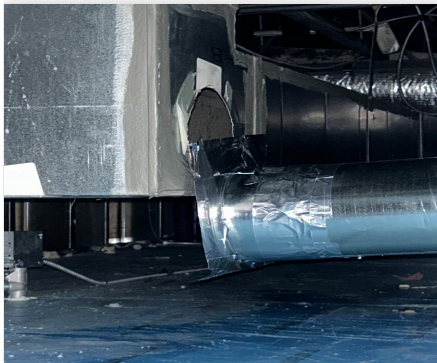

03/02/2026



03/02/2026

Project Issue Response Details

- **03/05/2026 National TAB - Anthony Taylor**
  - EF-1 has been fixed and is now in balance.

## CheckList List

- 01: RTU's/AHU's
- 02: Exhaust Fans
- 03: Hoods
- 04: Final Tests



**03-02-26 QT #1730 FORSYTH, GA**

**CheckList Information**

**Name :** 01: RTU's/AHU's **Status :** Completed  
**Assigned Organization :** National TAB **Asset :**  
**Requesting Organization :** National TAB  
**Created Date :** 02/05/2026 - Trinity Dodds - National TAB  
**Completed Date :** 03/02/2026 - Anthony Taylor - National TAB

**CheckList Item Details**

RTU's/AHU's

Evaporator coils are clean? Pass

Comment:

Condenser coils are clean? Pass

Comment:

Gas piping is installed and valves are turned on? Pass

Comment:

Unit free of noticeable noise and vibration Pass

Comment:



03-02-26 QT #1730 FORSYTH, GA

CheckList Information

**Name :** 02: Exhaust Fans **Status :** Completed

**Assigned Organization :** National TAB **Asset :**

**Requesting Organization :** National TAB

**Created Date :** 02/05/2026 - Trinity Dodds - National TAB

**Completed Date :** 03/03/2026 - Anthony Taylor - National TAB

CheckList Item Details

EF's

Hinge kit installed installed on hood fan?	Pass
--	------

Comment:

Flex conduit is long enough so that fan can be completely tilted back?	Pass
--	------

Comment:

No major leakage around the fan base	Pass
--------------------------------------	------

Comment:

Unit is free of noise and vibration	Pass
-------------------------------------	------

Comment:



**03-02-26 QT #1730 FORSYTH, GA**

**CheckList Information**

**Name :** 03: Hoods **Status :** Completed  
**Assigned Organization :** National TAB **Asset :**  
**Requesting Organization :** National TAB  
**Created Date :** 02/05/2026 - Trinity Dodds - National TAB  
**Completed Date :** 03/02/2026 - Anthony Taylor - National TAB

**CheckList Item Details**

**HOODS**

---

**Hood is free of alarms?** Pass

**Comment:**

---

**Hood is free of damage?** Pass

**Comment:**

---

**End panels are installed per prototype?** Fail

**Comment:**

Hinge Kit is not installed.

---



03-02-26 QT #1730 FORSYTH, GA

CheckList Information

**Name :** 04: Final Tests **Status :** Completed

**Assigned Organization :** National TAB **Asset :**

**Requesting Organization :** National TAB

**Created Date :** 02/05/2026 - Trinity Dodds - National TAB

**Completed Date :** 03/02/2026 - Anthony Taylor - National TAB

CheckList Item Details

FINAL CHECKS

HOOD CAPTURE TEST

List kitchen equipment turned on for testing

Comment:

Fryer

List smoke candle type used

Comment:

NTAB

Smoke test capture % - Perimeter of hood

Comment:

100%

Smoke test capture % - Top of cooking surface

Comment:

100%

WITNESS

Date test was completed

03/02/2026

**Comment:**

---

**TAB tech name / Firm**

**Comment:**

Anthony Taylor

---

**Site super name / Firm**

**Comment:**

Jonathan Byoyd

---

**Owner representative name / Firm (if Applicable)**

**Comment:**

QT

---

**BUILDING PRESSURE**

---

**Do actual net building airflow, design net building airflow, and pressure coincide? If not why? (All three should either be positive or negative)**

Pass

---

**Comment:**

---



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

## System/Unit: AHU/RTU

Asset: RT-1

AREA:SALES FLOOR

Unit Data	
	Actual
MFG	AAON
Serial Num	202201-ANEL23446
Model Num	RN-015-8-0-EA0A-152
Num OA Filters 1	1
OA Filter Size 1	23X45
Num Final Filter 1	4
Final Filter Size 1	20X25X2

Motor Data	
	Actual
Motor MFG	AAON
Horsepower	5
Motor Rpm	1760
Phase	3
Rated Voltage	208
Rated Amperage	16.7

Test Data		
	Design	Actual
SF CFM	5000	4975
SF RPM	-	1760
OA CFM (Hoods On)	865	900
OA CFM (Hoods Off)	415	440
RL Voltage	-	163 - VFD
RL Amperage	-	9.7 - VFD
VFD Max SetPt	-	48 hz
VFD Min SetPt	-	24 hz
OA Damper Position (Hoods On)	-	46% - MANUAL ADJUSTMENT
OA Damper Position (Hoods Off)	-	26% - MANUAL ADJUSTMENT

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.37"
Fan Suction SP	-	-0.78"
Fan Discharge SP	-	0.27"
Total ESP	-	0.64"
Fan Total SP	-	1.05"

General	
	Actual
Fan Rotation Correct	YES
Unit Filters Clean	YES
Condensate Drain Installed	YES

Completed By: Anthony Taylor on 03/02/2026

Notes:  
Economizer needed to be manually adjusted as it was not operating via Emerson.

Written By: Anthony Taylor on 03/02/2026

## Unit Data - PHOTO LOG



03/02/2026



03/02/2026



# National TAB

Project:03-02-26 QT #1730 FORSYTH, GA

## AHU/RTU

**Diffuser Supply (GRD)**

**RT-1/SALES FLOOR**

Asset									
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	CFM(2)	FINAL CFM	% to design
SGRD1	ENTRANCE	ES	12"	350	0.84	105	209	209	59.7
SGRD2	SALES	ES	10"	450	1	480	421	421	93.6
SGRD3	SALES	ES	10"	450	1	501	471	471	104.7
SGRD4	SALES	ES	12"	550	1	250	526	526	95.6
SGRD5	SALES	ES	12"	550	1	600	553	553	100.5
SGRD6	SALES	ES	10"	450	1	404	398	398	88.4
SGRD7	SALES	ES	10"	450	1	493	444	444	98.7
SGRD8	SALES	ES	12"	550	1	628	624	624	113.5
SGRD9	WOMEN'S RR	ES	10"	250	1	297	303	303	121.2
SGRD10	SIDE ENTRANCE	ES	10"	400	1	250	398	398	99.5
SGRD11	TEA AREA	ES	8"	250	1	459	328	328	131.2
SGRD12	BACK HALLWAY	ES	10"	300	1	200	200	200	66.7
Total				5000		4667	4875	4875	97.5%



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

## System/Unit: AHU/RTU

Asset: RT-2

AREA:SALES FLOOR

Unit Data	
	Actual
MFG	AAON
Serial Num	202201-ANEL23447
Model Num	RN-015-8-0-EA0A-152
Num OA Filters 1	1
OA Filter Size 1	23X45
Num Final Filter 1	4
Final Filter Size 1	RN-015-8-0-EA0A-152

Motor Data	
	Actual
Motor MFG	AAON
Horsepower	5
Motor Rpm	1760
Phase	3
Rated Voltage	208
Rated Amperage	16.7

Test Data		
	Design	Actual
SF CFM	5000	4968
SF RPM	-	1760
OA CFM (Hoods On)	865	831
OA CFM (Hoods Off)	415	405
RL Voltage	-	163
RL Amperage	-	8.3
VFD Max SetPt	-	48 hz
VFD Min SetPt	-	24 hz
OA Damper Position (Hoods On)	-	46% - MANUAL ADJUSTMENT
OA Damper Position (Hoods Off)	-	23% - MANUAL ADJUSTMENT

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.58"
Fan Suction SP	-	-0.84"
Fan Discharge SP	-	0.51"
Total ESP	-	1.09"
Fan Total SP	-	1.35"

General	
	Actual
Fan Rotation Correct	YES
Unit Filters Clean	YES
Condensate Drain Installed	YES

Completed By: Anthony Taylor on 03/02/2026

Notes:

Economizer needed to be manually adjusted as it was not operating via Emerson.

Written By: Anthony Taylor on 03/02/2026

## Unit Data - PHOTO LOG



03/02/2026



03/02/2026



# National TAB

Project:03-02-26 QT #1730 FORSYTH, GA

## AHU/RTU

**Diffuser Supply (GRD)**

**RT-2/SALES FLOOR**

Asset									
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	CFM(2)	FINAL CFM	% to design
SGRD1	ENTRANCE	ES	12"	350	0.84	113	218	218	62.3
SGRD2	SALES	ES	10"	450	1	423	375	375	83.3
SGRD3	SALES	ES	12"	675	1	722	699	699	103.6
SGRD4	SALES	ES	12"	675	1	684	674	674	99.9
SGRD5	FOUNTAIN AREA	ES	8"	250	1	303	284	284	113.6
SGRD6	SIDE ENTRANCE	ES	10"	400	1	427	427	427	106.8
SGRD7	MEN'S RR	ES	10"	400	1	419	419	416	104.0
SGRD8	SALES	ES	12"	650	1	723	723	723	111.2
SGRD9	SALES	ES	8"	250	1	180	180	180	72.0
SGRD10	SERVICE AREA	ES	10"	450	1	461	461	461	102.4
SGRD11	SERVICE AREA	ES	10"	450	1	501	501	511	113.6
Total				5000		4956	4961	4968	99.36%



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

## System/Unit: AHU/RTU

Asset: RT-3

AREA:KITCHEN

Unit Data	
	Actual
MFG	AAON
Serial Num	202201-ANEK23448
Model Num	RN-013-8-0-EA0A-152
Num OA Filters 1	1
OA Filter Size 1	23X45
Num Final Filter 1	4
Final Filter Size 1	20X25X2

Motor Data	
	Actual
Motor MFG	AAON
Horsepower	3
Motor Rpm	1760
Phase	3
Rated Voltage	208
Rated Amperage	10.6


Test Data		
	Design	Actual
SF CFM	-	4184
SF RPM	-	1760
OA CFM (Hoods On)	856	880
OA CFM (Hoods Off)	415	419
RL Voltage	-	170 - VFD
RL Amperage	-	8.3 - VFD
VFD Max SetPt	-	48 hz
VFD Min SetPt	-	24 hz
OA Damper Position (Hoods On)	-	46% - MANUAL ADJUSTMENT
OA Damper Position (Hoods Off)	-	23%

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.38"
Fan Suction SP	-	-0.69"
Fan Discharge SP	-	0.48"
Total ESP	-	0.86"
Fan Total SP	-	1.17"

General	
	Actual
Fan Rotation Correct	YES
Unit Filters Clean	YES
Condensate Drain Installed	YES

Completed By: Anthony Taylor on 03/02/2026

## Unit Data - PHOTO LOG

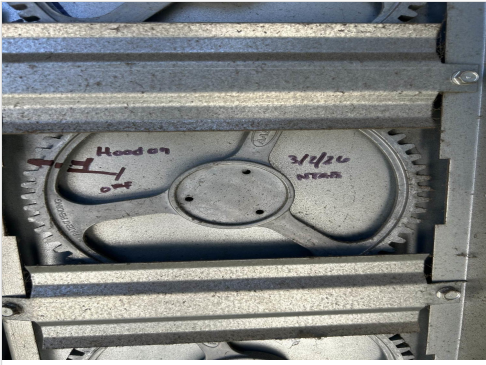

03/02/2026



03/02/2026



# National TAB

Project:03-02-26 QT #1730 FORSYTH, GA

## AHU/RTU

**Diffuser Supply (GRD)**

**RT-3/KITCHEN**

Asset									
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	CFM(2)	FINAL CFM	% to design
SGRD1	SALES	SI	12"	700	1	752	759	759	108.4
SGRD2	SUPPORT SERVICE	SI	12"	875	1	738	805	805	92.0
SGRD3	SUPPORT SERVICE	SI	12"	875	1	833	811	811	92.7
SGRD4	SUPPORT SERVICE	SI	12"	875	1	1029	865	865	98.9
SGRD5	SUPPORT SERVICE	ES	12"	875	1	899	944	944	107.9
Total				4200		4251	4184	4184	99.62%



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

## System/Unit: AHU/RTU

Asset: RT-4

AREA:BOH

Unit Data	
	Actual
MFG	AAON
Serial Num	202201-AYEF05213
Model Num	RQ-006-8-V-EA09-132
Num OA Filters 1	1
OA Filter Size 1	12X18
Num Final Filter 1	2
Final Filter Size 1	20X25X2

Motor Data	
	Actual
Motor MFG	AAON
Horsepower	2
Motor Rpm	1760
Phase	3
Rated Voltage	208
Rated Amperage	7.5

Test Data		
	Design	Actual
SF CFM	1800	1731
SF RPM	-	1760
OA CFM (Hoods On)	160	170
OA CFM (Hoods Off)	160	170
RL Voltage	-	146
RL Amperage	-	3.96
VFD Max SetPt	-	45 hz
VFD Min SetPt	-	24 hz
OA Damper Position (Hoods On)	-	46%

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.27"
Fan Suction SP	-	-0.45"
Fan Discharge SP	-	0.35"
Total ESP	-	0.62"
Fan Total SP	-	0.80"

General	
	Actual
Fan Rotation Correct	YES
Unit Filters Clean	YES
Condensate Drain Installed	YES

Completed By: Anthony Taylor on 03/02/2026

## Unit Data - PHOTO LOG



03/02/2026



03/02/2026



# National TAB

Project:03-02-26 QT #1730 FORSYTH, GA

## AHU/RTU

**Diffuser Supply (GRD)**

**RT-4/BOH**

Asset									
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	CFM(2)	FINAL CFM	% to design
SGRD1	ELECTRICAL		8"	360	1	202	275	332	92.2
SGRD2	DOCK		10"	360	1	414	403	362	100.6
SGRD3	DOCK		10"	360	1	354	370	340	94.4
SGRD4	DOCK		10"	360	1	331	334	362	100.6
SGRD5	DOCK		10"	360	1	454	378	335	93.1
Total				1800		1755	1760	1731	96.17%



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

System/Unit: FAN - Exhaust

Asset: EF1

AREA: MEN'S RR/SUPPORT SERVICE

Unit Data		
	Design	Actual
MFG	NA	CAPITIVEAIRE
Model Num	NA	DR33HFA
Serial Num	-	5157507
Type	-	DOWNBLAST
Configuration	-	VERTICAL

Motor Data		
	Design	Actual
Motor MFG	-	CAPTIVEAIRE
Horsepower	-	0.333
Motor Rpm	-	1800
Phase	-	1
Voltage (rated)	-	115
Amperage (rated)	-	4.3

Test Data		
	Design	Actual
CFM	650	661
Fan RPM	-	1641
Fan Rotation	-	CCW
Motor RPM	-	1641
System SetPt	-	84 %
RL Voltage	-	115
RL Amperage	-	3.8
Total ESP	-	0.17"
Fan Inlet SP	-	-0.17"
Fan Discharge SP	-	ATM

Completed By: Anthony Taylor on 03/05/2026

**Unit Data - PHOTO LOG**



**03/02/2026**



# National TAB

Project:03-02-26 QT #1730 FORSYTH, GA

Diffuser Ret/Exh (GRD)

## EF1/MEN'S RR/SUPPORT SERVICE

Asset									
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	CFM(2)	FINAL CFM	% to design
EGRD1	SUPPORT SERVICE	RI	8"	150	1	61	90	138	92.0
Total				150		61	90	138	92%



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

System/Unit: FAN - Exhaust

Asset: EF2

AREA:WOMEN'S RR

Unit Data		
	Design	Actual
MFG	NA	CAPTIVEAIRE
Model Num	NA	DR12HFA
Serial Num	-	5157507
Type	-	DOWNBLAST
Configuration	-	VERTICAL

Motor Data		
	Design	Actual
Motor MFG	-	CAPTIVEAIRE
Horsepower	-	0.250
Motor Rpm	-	1800
Phase	-	1
Voltage (rated)	-	115
Amperage (rated)	-	2.9

Test Data		
	Design	Actual
CFM	350	329
Fan RPM	-	1360
Fan Rotation	-	CCW
Motor RPM	-	1360
System SetPt	-	71 %
RL Voltage	-	115
RL Amperage	-	1.27
Total ESP	-	-0.14"
Fan Inlet SP	-	0.14
Fan Discharge SP	-	ATM

Completed By: Anthony Taylor on 03/02/2026

**Unit Data - PHOTO LOG**



**03/02/2026**



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

System/Unit: FAN - Exhaust

Asset: EF3

AREA:KITCHEN HD

Unit Data		
	Design	Actual
MFG	NA	CAPTIVEAIRE
Model Num	NA	DU50HFA
Serial Num	-	8385043
Type	UPBLAST	UPBLAST
Configuration	VERTICAL	VERTICAL

Motor Data		
	Design	Actual
Motor MFG	-	CAPTIVEAIRE
Horsepower	0.50	0.50
Motor Rpm	-	1800
Phase	1	1
Voltage (rated)	208	208
Amperage (rated)	-	3.8

Test Data		
	Design	Actual
CFM	1350	1460
Fan RPM	-	1177
Fan Rotation	-	CCW
Motor RPM	-	1177
System SetPt	-	53.6 hz
RL Voltage	-	212
RL Amperage	-	1.81
Total ESP	0.75"	0.43"
Fan Inlet SP	-	-0.43"
Fan Discharge SP	-	ATM

Completed By: Anthony Taylor on 03/02/2026

**Unit Data - PHOTO LOG**



**03/02/2026**



**03/02/2026**



# National TAB

Project: 03-02-26 QT #1730 FORSYTH, GA

## System/Unit: Kitchen Hood Type I

Asset: HD1

AREA:GRIDDLE

Unit Data		
	Design	Actual
MFG	CAPTIVEAIRE	CAPTIVEAIRE
Model Num	6030ND-2	6030ND-2
Job / Serial Num	-	8385043
Type	TYPE I CANOPY	TYPE I CANOPY
Hood length	108"	108"
Hood Width	60"	60"

Test Data Exhaust		
	Design	Actual
Filter Type	CAPTRATE SOLO FILTER	CAPTRATE SOLO FILTER
Filter Size 1	20X16	20x16
Filter Qty 1	6	6
Filter AK factor size 1	2.08	2.08
Filter Total AK Area	12.48	12.48
Filter1 FPM	-	117
Filter2 FPM	-	116
Filter3 FPM	-	124
Filter4 FPM	-	132
Filter5 FPM	-	112
Filter6 FPM	-	107
Filter Ave FPM(corr)	-	117
CFM	1350	1460

Cooking Equipment	
	Actual
Item 1	FRYER
Item 2	PIZZA OVEN

Completed By: Anthony Taylor on 03/02/2026

**Unit Data - PHOTO LOG**



**03/02/2026**

### AIR BALANCE SCHEDULE

UNIT	AREA SERVED	HOOD ON OA		HOOD OFF OA		HOOD ON EXHAUST		HOOD OFF EXHAUST	
		DESIGN	ACTUAL	DESIGN	ACTUAL	DESIGN	ACTUAL	DESIGN	ACTUAL
RTU 1	SALES	865	900	415	440				
RTU-2	SALES	865	831	415	405				
RTU-3	KITCHEN	865	880	415	419				
RTU-4	BOH	160	170	160	170				
EF-1	MEN'S RR/COMBI					650	661	650	661
EF-2	WOMEN'S RR					350	329	350	329
EF-3	HOOD					1350	1460	0	
<b>TOTALS</b>		<b>2755</b>	<b>2781</b>	<b>1405</b>	<b>1434</b>	<b>2350</b>	<b>2450</b>	<b>1000</b>	<b>990</b>

### HOODS ON

#### NET AIRFLOW CALCULATION

TOTALS	DESIGN	ACTUAL
TOTAL OA	2755	2781
TOTAL EXHAUST	2350	2450
<b>NET AIRFLOW</b>	<b>405</b>	<b>331</b>

DOOR TESTED	BUILDING PRESSURE MEASUREMENTS
FRONT	0.003
SIDE	0.0042
REAR	0.006
<b>AVERAGE</b>	<b>0.0044</b>

### HOODS OFF

#### NET AIRFLOW CALCULATION

TOTALS	DESIGN	ACTUAL
TOTAL OA	1405	1434
TOTAL EXHAUST	1000	990
<b>NET AIRFLOW</b>	<b>405</b>	<b>444</b>

DOOR TESTED	BUILDING PRESSURE MEASUREMENTS
FRONT	0.0018
SIDE	0.002
REAR	0.003
<b>AVERAGE</b>	<b>0.0023</b>

NOTES:

