

Report By:

National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246



Report: TAB REPORT
Function: Test, Adjust, & Balance
Date: 10/30/2023

PROJECT
10-23-23 CARMAX #7190 - AUSTIN, TX

4400 SOUTH INTERSTATE HIGHWAY 35

AUSTIN, TX 78745

Client

Comfort Systems USA
9450 W Wingfoot Rd
Houston, TX 77041

Project Summary

The summary below provides a quick understanding of our scope of work and general testing procedures. Enclosed in the report is further detail about your building performance including recommendations, asset data, and pictures. Our focus is to work with the trades to remedy any issues or deficiencies during the actual field balancing and not after the balancing has occurred to achieve a positive environment and outcome. The level of success is determined by the availability of the trades, possible parts needed, or time constraints.

Facility Identification and TAB Requirements

The mechanical equipment to be tested, adjusted, and balanced includes all RTU's and EF's on the Test and Balance Scope on the mechanical drawings.

Standard RTU's

Each of the RTU's were measured at their terminal devices utilizing a flow hood or via total traverse. The sum of these readings is equal to the total flow for that particular unit. The total flow of each RTU was then adjusted to within tolerance of the specified design. Outside airflow was measured by reading the inlet with a velocity grid times the area of the filter. Any equipment that fell outside of this tolerance is noted throughout the report.

Bypass RTU's

The Bypass RTU's were measured by first closing the bypass damper completely. By doing this, the outside airflow is equal to the total flow for the unit. The airflow was measured using a velgrid at the outdoor air intake and multiplying by the free area of the filters. Adjustments made to the motor sheave in order to get airflow within tolerance of design. The bypass damper is then adjusted so that bypass and OA flows are within tolerance.

ERV RTU's

The supply air portion of the ERV is 100% OA that is supplied to the space via two fans in series. The airflow was measured by reading the intake air filter with a velgrid and multiplying by the free area of the filter. Adjustments were made to the airflow by adjusting the motor sheaves to balance airflow within design tolerances. The exhaust system has one fan and was measured via either traverse or by reading the inlets with a velgrid and multiplying by the free area of the filter.

Exhaust Fans

The exhaust fans were measured by reading each air device with a flow hood or via a velgrid reading times the free area of the inlets. The total airflow for each fan is equivalent to the sum of these readings. Fan speed was then adjusted so that the airflow was within tolerance of design. Any equipment that fell outside of this tolerance is noted throughout the report.

Issue List

- EF-11 SPEED CONTROLLER
- RTU GAS VALVE SHUT



10-23-23 CARMAX #7190 - AUSTIN, TX

Project Issue Information

Issue Name : EF-11 SPEED CONTROLLER
Description : EF-11 SPEED CONTROLLER WAS NOT OPERATIONAL. MECHANICAL WILL BE GETTING NEW SPED CONTROLLER TO INSTALL AT SOME POINT IN THE FUTURE.
Created By : National TAB **Assigned To :** National TAB - Will Turnbough
Status : Open
Originated Date : 10/25/2023 - Bayley Morvant - National TAB

Project Issue File Details



EF_11SPEEDCONTROLLER...
10/25/2023



10-23-23 CARMAX #7190 - AUSTIN, TX

Project Issue Information

Issue Name : RTU GAS VALVE SHUT
Description : RTU-9 GAS VALVE SHUT. RTU-1 GAS VALVE SHUT.
Created By : National TAB **Assigned To :** National TAB - Will Turnbough
Status : Open
Originated Date : 10/24/2023 - Bayley Morvant - National TAB

Project Issue File Details



CARMX_7190_RTU_9_GAS_..
10/24/2023



RTU_1GASVALVESHUTCARM..
10/25/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU1

AREA:SHOWROOM

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622E03512
Model Num	LGH240H4M	LGH240H4MS4G
Type	RTU	RTU
Configuration	VERTICAL	VERTICAL
Num OA Filters 1	-	3
OA Filter Size 1	-	24x14x1
Num Final Filter 1	-	6
Final Filter Size 1	-	20x24x2

Motor Data		
	Design	Actual
Motor MFG	-	NIDEC
Frame	-	213TZ
Horsepower	5.0	7.50
Motor Rpm	-	1765
Phase	3	3
Rated Voltage	480	460
Rated Amperage	-	10.6

Drive Data		
	Design	Actual
Motor Sheave Size	-	1VP65B
Motor Bore Size	-	1 3/8"
Motor Sheave SetPt	-	2 TURNS OUT
Fan Sheave Size	-	10.5"
Fan Sheave Bore	-	1 3/16"
Belt CL Distance	-	21.5"
Num of Belts	-	1
Belt Size	-	BX66
Belt Alignment	-	VERIFIED

Test Data		
	Design	Actual
SF CFM	8000	7906
SF RPM	-	850
RA CFM	7220	7097
OA CFM	780	809
RL Voltage	-	490/486/491
RL Amperage	-	5.0/6.3/5.7
SF Rotation	-	CCW
RA Damper Position	-	80% OPEN
Min OA Damper Position	-	20% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	55 DEGREES

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.78
Fan Suction SP	-	-1.05
Fan Discharge SP	-	0.73
Total ESP	0.6"	1.51
Fan Total SP	-	1.78

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/25/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU2

AREA:SHOWROOM

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622E03091
Model Num	LGH156H4M	LGH156H4MS5G
Type	RTU	RTU
Configuration	VERTICAL	VERTICAL
Num OA Filters 1	-	3
OA Filter Size 1	-	24x14x1
Num Final Filter 1	-	6
Final Filter Size 1	-	24x24x2

Motor Data		
	Design	Actual
Motor MFG	-	INTERLINK
Frame	-	56HZ
Horsepower	3.0	3.00
Motor Rpm	-	1750
Phase	3	3
Rated Voltage	480	460
Rated Amperage	-	4.0

Drive Data		
	Design	Actual
Motor Sheave Size	-	1VL40
Motor Bore Size	-	7/8"
Motor Sheave SetPt	-	0 TURNS OUT
Fan Sheave Size	-	BK72
Fan Sheave Bore	-	1 3/16"
Belt CL Distance	-	21.5"
Num of Belts	-	1
Belt Size	-	BX55
Belt Alignment	-	VERIFIED

Test Data		
	Design	Actual
SF CFM	5500	5376
SF RPM	-	621
RA CFM	4980	4859
OA CFM	520	517
RL Voltage	-	489/485/489
RL Amperage	-	2.8/2.9/2.8
SF Rotation	-	CCW
RA Damper Position	-	80% OPEN
Min OA Damper Position	-	20% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	55 DEGREES

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.43
Fan Suction SP	-	-0.56
Fan Discharge SP	-	0.32
Total ESP	0.8"	0.75
Fan Total SP	-	0.88

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/24/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU3

AREA: CUSTOMER

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622G09659
Model Num	LGH048H4E	LGH048H4ES5G
Type	RTU	RTU
Configuration	VERTICAL	VERTICAL
Num OA Filters 1	-	1
OA Filter Size 1	-	30x14x1
Num Final Filter 1	-	4
Final Filter Size 1	-	16x20x2

Motor Data		
	Design	Actual
Motor MFG	-	GENTEQ
Frame	-	NA
Horsepower	0.75	0.75
Motor Rpm	-	NA
Phase	3	1
Rated Voltage	480	120
Rated Amperage	-	3.1

Drive Data		
	Design	Actual
Motor Sheave Size	-	DIRECT DRIVE
Motor Bore Size	-	DIRECT DRIVE
Motor Sheave SetPt	-	DIRECT DRIVE
Fan Sheave Size	-	DIRECT DRIVE
Fan Sheave Bore	-	DIRECT DRIVE
Belt CL Distance	-	DIRECT DRIVE
Num of Belts	-	DIRECT DRIVE
Belt Size	-	DIRECT DRIVE
Belt Alignment	-	DIRECT DRIVE

Test Data		
	Design	Actual
SF CFM	1280	1281
SF RPM	-	DIRECT DRIVE
RA CFM	1080	974
OA CFM	300	307
RL Voltage	-	121
RL Amperage	-	1.8
SF Rotation	-	CCW
RA Damper Position	-	70% Open
Min OA Damper Position	-	30% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	55 DEGREES

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.09
Fan Suction SP	-	-0.21
Fan Discharge SP	-	0.40
Total ESP	0.6"	0.49
Fan Total SP	-	0.61

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/24/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU4

AREA:BUSINESS

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622G09705
Model Num	LGH060H4E	LGH060H4ES5G
Type	RTU	RTU
Configuration	VERTICAL	VERTICAL
Num OA Filters 1	-	1
OA Filter Size 1	-	30x14x1
Num Final Filter 1	-	4
Final Filter Size 1	-	20x20x2

Motor Data		
	Design	Actual
Motor MFG	-	GENTEQ
Frame	-	NA
Horsepower	1.0	1.00
Motor Rpm	-	NA
Phase	3	1
Rated Voltage	480	115
Rated Amperage	-	3.7

Drive Data		
	Design	Actual
Motor Sheave Size	-	DIRECT DRIVE
Motor Bore Size	-	DIRECT DRIVE
Motor Sheave SetPt	-	DIRECT DRIVE
Fan Sheave Size	-	DIRECT DRIVE
Fan Sheave Bore	-	DIRECT DRIVE
Belt CL Distance	-	DIRECT DRIVE
Num of Belts	-	DIRECT DRIVE
Belt Size	-	DIRECT DRIVE
Belt Alignment	-	DIRECT DRIVE

Test Data		
	Design	Actual
SF CFM	1300	1392
SF RPM	-	DIRECT DRIVE
RA CFM	1000	1104
OA CFM	300	288
RL Voltage	-	123
RL Amperage	-	1.7
SF Rotation	-	CCW
RA Damper Position	-	70% OPEN
Min OA Damper Position	-	30% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	55 DEGREES

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.12
Fan Suction SP	-	-0.24
Fan Discharge SP	-	0.20
Total ESP	-	0.32
Fan Total SP	-	0.44

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/25/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU5

AREA:BUYERS

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622G09652
Model Num	LGH048H4E	LGH048H4ES5G
Type	-	RTU
Configuration	-	VERTICAL
Num OA Filters 1	-	1
OA Filter Size 1	-	30x14x1
Num Final Filter 1	-	4
Final Filter Size 1	-	16x20x2

Motor Data		
	Design	Actual
Motor MFG	-	GENTEQ
Frame	-	NA
Horsepower	0.75	0.75
Motor Rpm	-	NA
Phase	3	1
Rated Voltage	480	115
Rated Amperage	-	3.1

Drive Data		
	Design	Actual
Motor Sheave Size	-	DIRECT DRIVE
Motor Bore Size	-	DIRECT DRIVE
Motor Sheave SetPt	-	DIRECT DRIVE
Fan Sheave Size	-	DIRECT DRIVE
Fan Sheave Bore	-	DIRECT DRIVE
Belt CL Distance	-	DIRECT DRIVE
Num of Belts	-	DIRECT DRIVE
Belt Size	-	DIRECT DRIVE
Belt Alignment	-	DIRECT DRIVE

Test Data		
	Design	Actual
SF CFM	1300	1327
SF RPM	-	DIRECT DRIVE
RA CFM	1100	1123
OA CFM	200	204
RL Voltage	-	119
RL Amperage	-	1.8
SF Rotation	-	CCW
RA Damper Position	-	75% OPEN
Min OA Damper Position	-	25% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	55 DEGREES

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.10
Fan Suction SP	-	-0.25
Fan Discharge SP	-	0.24
Total ESP	0.6"	0.34
Fan Total SP	-	0.49

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/25/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU6

AREA: BREAKROOM

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622G09709
Model Num	LGH060H4E	LGH060H4ES5G
Type	RTU	RTU
Configuration	VERTICAL	VERTICA.
Num OA Filters 1	-	1
OA Filter Size 1	-	30x14x1
Num Final Filter 1	-	4
Final Filter Size 1	-	20x20x2

Motor Data		
	Design	Actual
Motor MFG	-	GENTEQ
Frame	-	NA
Horsepower	1.0	1.0
Motor Rpm	-	NA
Phase	3	1
Rated Voltage	480	115
Rated Amperage	-	3.7

Drive Data		
	Design	Actual
Motor Sheave Size	-	DIRECT DRIVE
Motor Bore Size	-	DIRECT DRIVE
Motor Sheave SetPt	-	DIRECT DRIVE
Fan Sheave Size	-	DIRECT DRIVE
Fan Sheave Bore	-	DIRECT DRIVE
Belt CL Distance	-	DIRECT DRIVE
Num of Belts	-	DIRECT DRIVE
Belt Size	-	DIRECT DRIVE
Belt Alignment	-	DIRECT DRIVE

Test Data		
	Design	Actual
SF CFM	1600	1618
SF RPM	-	DIRECT DRIVE
RA CFM	1350	1376
OA CFM	250	242
RL Voltage	-	122
RL Amperage	-	3.0
SF Rotation	-	CCW
RA Damper Position	-	80% OPEN
Min OA Damper Position	-	20% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	55 DEGREES

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.93
Fan Suction SP	-	-1.07
Fan Discharge SP	-	0.23
Total ESP	.6"	1.16
Fan Total SP	-	1.30

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/25/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU7

AREA:PBX

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622H07180
Model Num	LCH036H4M	LCH036H4EN4G
Type	RTU	RTU
Configuration	VERTICAL	VERTICAL
Num Final Filter 1	-	4
Final Filter Size 1	-	16x20x2

Motor Data		
	Design	Actual
Motor MFG	-	GENTEQ
Frame	-	NA
Horsepower	0.5	0.5
Motor Rpm	-	NA
Phase	3	1
Rated Voltage	480	120
Rated Amperage	-	2.2

Drive Data		
	Design	Actual
Motor Sheave Size	-	DIRECT DRIVE
Motor Bore Size	-	DIRECT DRIVE
Motor Sheave SetPt	-	DIRECT DRIVE
Fan Sheave Size	-	DIRECT DRIVE
Fan Sheave Bore	-	DIRECT DRIVE
Belt CL Distance	-	DIRECT DRIVE
Num of Belts	-	DIRECT DRIVE
Belt Size	-	DIRECT DRIVE
Belt Alignment	-	DIRECT DRIVE

Test Data		
	Design	Actual
SF CFM	975	999
SF RPM	-	DIRECT DRIVE
RA CFM	975	999
OA CFM	0	0
RL Voltage	-	121
RL Amperage	-	1.2
SF Rotation	-	CCW

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.16
Fan Suction SP	-	-0.26
Fan Discharge SP	-	0.19
Total ESP	0.8"	0.35
Fan Total SP	-	0.45

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/25/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU8

AREA:SERVICE WRITER

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622G09701
Model Num	LGH060H4E	LGH060H4ES5G
Type	RTU	RTU
Configuration	VERTICAL	VERTICAL
Num OA Filters 1	-	1
OA Filter Size 1	-	30X14X1
Num Final Filter 1	-	4
Final Filter Size 1	-	20x20x2

Motor Data		
	Design	Actual
Motor MFG	-	GENTEQ
Frame	-	NA
Horsepower	1.0	1.00
Motor Rpm	-	NA
Phase	3	1
Rated Voltage	480	120
Rated Amperage	-	3.7

Drive Data		
	Design	Actual
Motor Sheave Size	-	DIRECT DRIVE
Motor Bore Size	-	DIRECT DRIVE
Motor Sheave SetPt	-	DIRECT DRIVE
Fan Sheave Size	-	DIRECT DRIVE
Fan Sheave Bore	-	DIRECT DRIVE
Belt CL Distance	-	DIRECT DRIVE
Num of Belts	-	DIRECT DRIVE
Belt Size	-	DIRECT DRIVE
Belt Alignment	-	DIRECT DRIVE

Test Data		
	Design	Actual
SF CFM	1800	1860
SF RPM	-	DIRECT DRIVE
RA CFM	1600	1656
OA CFM	200	204
RL Voltage	-	122
RL Amperage	-	3.5
SF Rotation	-	CCW
RA Damper Position	-	80% OPEN
Min OA Damper Position	-	20% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	55 DEGREES

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.38
Fan Suction SP	-	-0.52
Fan Discharge SP	-	0.36
Total ESP	0.6"	0.74
Fan Total SP	-	0.88

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/24/2023

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU9

AREA:SERVICE AREA

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622E03191
Model Num	LGH240H4B	LGH240H4MH4G
Type	RTU	RTU
Configuration	VERTICAL	VERTICAL
Num OA Filters 1	-	2
OA Filter Size 1	-	31X17X1
Num Final Filter 1	-	6
Final Filter Size 1	-	24x24x2

Motor Data		
	Design	Actual
Motor MFG	-	NIDEC
Frame	-	184TZ
Horsepower	5.0	5.00
Motor Rpm	-	1765
Phase	3	3
Rated Voltage	480	460
Rated Amperage	-	6.50

Drive Data		
	Design	Actual
Motor Sheave Size	-	1VP65B
Motor Bore Size	-	1.125"
Motor Sheave SetPt	-	3 TURNS OUT
Fan Sheave Size	-	10.5"
Fan Sheave Bore	-	1.25"
Belt CL Distance	-	21"
Num of Belts	-	1
Belt Size	-	BX65
Belt Alignment	-	VERIFIED

Test Data		
	Design	Actual
SF CFM	5600	5629
SF RPM	-	714
RA CFM	1600	1713
OA CFM	4000	3916
RL Voltage	-	482/486/487
RL Amperage	-	4.6/4.5/4.5
SF Rotation	-	CCW
RA Damper Position	-	50% OPEN
Min OA Damper Position	-	100% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	NA

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.24
Fan Suction SP	-	-0.58
Fan Discharge SP	-	0.49
Total ESP	0.8"	0.73
Fan Total SP	-	1.07

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/25/2023

National TAB

Project:10-23-23 CARMAX #7190 - AUSTIN, TX

AHU/RTU



Diffuser Supply (GRD)

RTU9/SERVICE AREA

Asset								
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	FINAL CFM	% to design
RTU9-SGRD1	SERVICE AREA	24/12	26"x14"	710	2.31	683	1007	141.8
RTU9-SGRD2	SERVICE AREA	24/12	26"x14"	710	2.31	942	990	139.4
RTU9-SGRD3	SERVICE AREA	24/12	26"x14"	710	2.31	979	1001	141.0
RTU9-SGRD4	SERVICE AREA	24/12	26"x14"	710	2.31	1000	1031	145.2
RTU9-SGRD5	SERVICE AREA	24/12	26"x14"	710	2.31	953	1011	142.4
RTU9-SGRD6	TOILET	24/12	8"	50	NA	25	51	102.0
RTU9-SGRD7	STORAGE	24/12	12"x12"	200	2.31	568	269	134.5
RTU9-SGRD8	STORAGE	24/12	12"x12"	200	2.31	508	269	134.5
Total				4000		5658	5629	140.72%

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: AHU/RTU



Asset: RTU10

AREA:SERVICE AREA

Unit Data		
	Design	Actual
MFG	LENNOX	LENNOX
Serial Num	-	5622E03167
Model Num	LGH240H4B	LGH240H4MH4G
Type	RTU	RTU
Configuration	VERTICAL	VERTICAL
Num OA Filters 1	-	2
OA Filter Size 1	-	31x17x1
Num Final Filter 1	-	6
Final Filter Size 1	-	24x24x2

Motor Data		
	Design	Actual
Motor MFG	-	NIDEC
Frame	-	184TZ
Horsepower	5.0	5.00
Motor Rpm	-	1765
Phase	3	3
Rated Voltage	480	460
Rated Amperage	-	6.50

Drive Data		
	Design	Actual
Motor Sheave Size	-	1VP65B
Motor Bore Size	-	1.125"
Motor Sheave SetPt	-	3 TURNS OUT
Fan Sheave Size	-	10.5"
Fan Sheave Bore	-	1.25"
Belt CL Distance	-	21
Num of Belts	-	1
Belt Size	-	BX65
Belt Alignment	-	VERIFIED

Test Data		
	Design	Actual
SF CFM	5600	5541
SF RPM	-	739
RA CFM	1600	1457
OA CFM	4000	4084
RL Voltage	-	482/487/487
RL Amperage	-	4.9/4.8/4.8
SF Rotation	-	CCW
RA Damper Position	-	50% OPEN
Min OA Damper Position	-	100% OPEN
Min OA Damper Type	-	OPOSED BLADE
OA Enthalpy Setpt	-	NA

Performance Data		
	Design	Actual
MA Plenum SP	-	-0.21
Fan Suction SP	-	-0.62
Fan Discharge SP	-	0.53
Total ESP	0.8"	0.74
Fan Total SP	-	1.15

General		
	Design	Actual
Fan Rotation Correct	-	YES
Unit Filters Clean	-	YES
Condensate Drain Installed	-	YES

Completed By: Bayley Morvant on 10/25/2023

National TAB

Project:10-23-23 CARMAX #7190 - AUSTIN, TX

AHU/RTU



Diffuser Supply (GRD)

RTU10/SERVICE AREA

Asset								
Asset Name	Location	Type	Size	DESIGN CFM	AK	CFM(1)	FINAL CFM	% to design
RTU10-SGRD1	SERVICE AREA	24/12	26"x14"	665	2.65	1354	908	136.5
RTU10-SGRD2	SERVICE AREA	24/12	26"x14"	665	2.65	924	958	144.1
RTU10-SGRD3	SERVICE AREA	24/12	26"x14"	665	2.65	779	932	140.2
RTU10-SGRD4	SERVICE AREA	24/12	26"x14"	665	2.65	559	921	138.5
RTU10-SGRD5	SERVICE AREA	24/12	26"x14"	665	2.65	551	916	137.7
RTU10-SGRD6	SERVICE AREA	24/12	26"x14"	665	2.65	1356	906	136.2
Total				3990		5523	5541	138.87%

National TAB

Project: 10-23-23 CARMAX #7190 - AUSTIN, TX

System/Unit: FAN - Exhaust



Asset: EF11

AREA:SALES TOILETS

Unit Data		
	Design	Actual
MFG	GREENHECK	GREENHECK
Model Num	CUE-121-A	CUE-120-A-5-1-19-X
Serial Num	-	23256134
Type	UPBLAST	UPBLAST
Configuration	VERTICAL	VERTICAL


Motor Data		
	Design	Actual
Motor MFG	-	US MOTORS
Frame	-	NA
Horsepower	1/2	1/2
Motor Rpm	-	1650
Phase	1	1
Voltage (rated)	120	115
Amperage (rated)	-	5.4
Service Factor	-	1.0

Test Data		
	Design	Actual
CFM	1500	1798
Fan RPM	-	DIRECT DRIVE
Fan Rotation	-	CCW
Motor RPM	-	DIRECT DRIVE
System SetPt	-	NA
RL Voltage	-	121
RL Amperage	-	3.4
Total ESP	.375	0.22
Fan Inlet SP	-	-0.22
Fan Discharge SP	-	ATM

Completed By: Bayley Morvant on 10/25/2023

Notes:
FAN SPEED CONTROLLER NOT OPERATIONAL.

Written By: Bayley Morvant on 10/25/2023

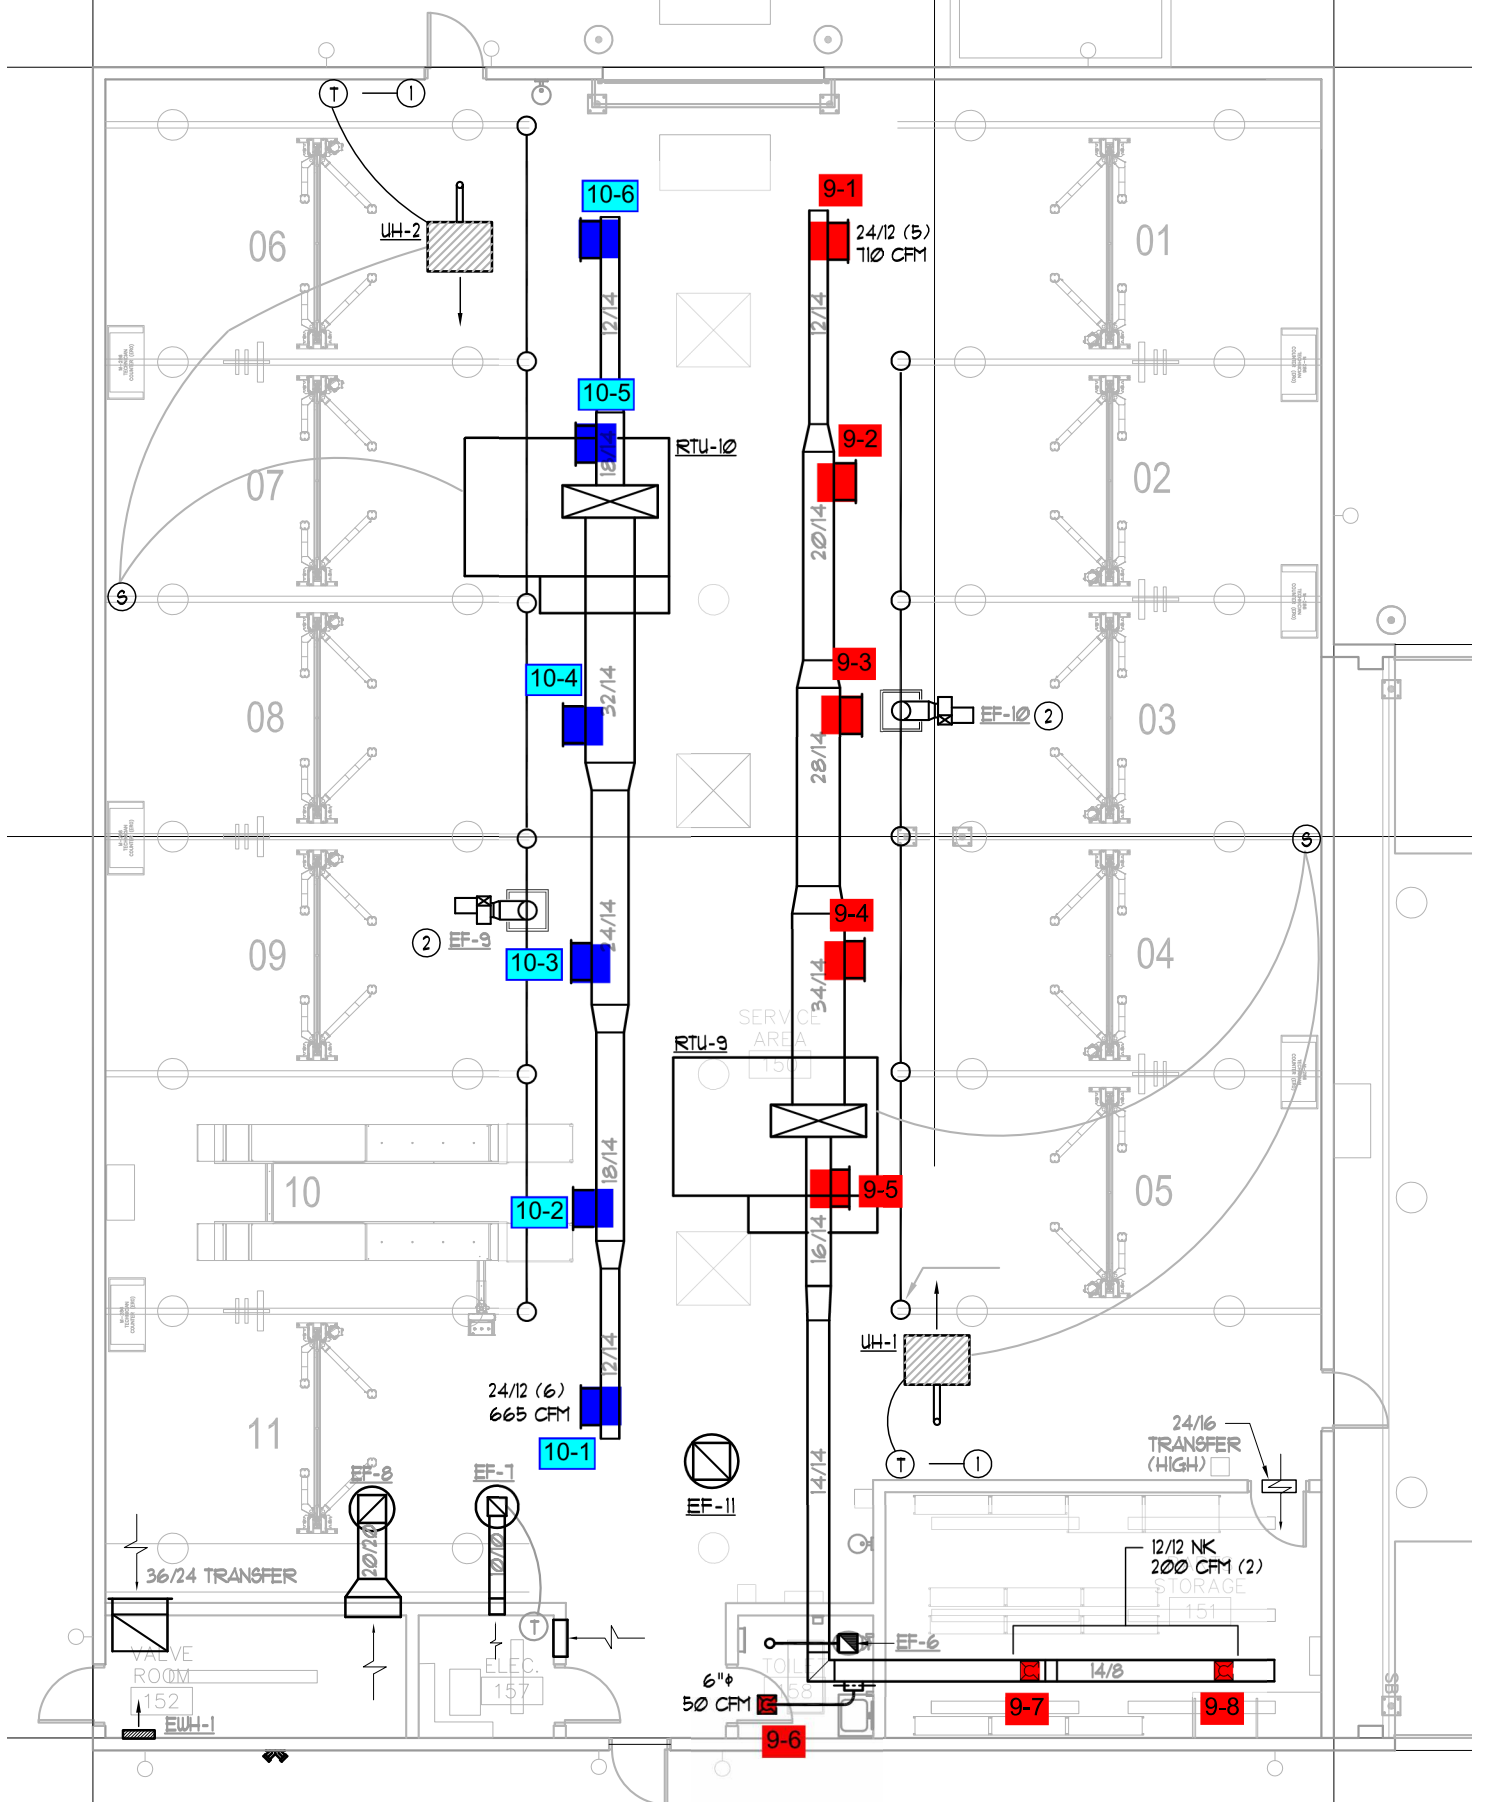

NOTE: SHOWN FOR TEST AND BALANCE PURPOSES ONLY.
SEE TEST AND BALANCE SCOPE ON M3.0
