

Report By:

National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246



Report: PUNCHLIST
Function: Test, Adjust, & Balance
Date: 11/13/2025
Completed By: National TAB

PROJECT
Marshalltown (Kansas City, KS)

9800 Leavenworth Rd

Kansas City, KS 66109

Client

Temp-Con, Inc.
15670 S Keller St
Olathe, KS 66062

National TAB

Project: Marshalltown (Kansas City, KS)

Table Of Contents

Section	Page #
Issue Data	3

Issue List

- EF-1: Fan not running
- EF-2: Fan not running
- EF10: Fan not running
- EF11: Fan not running
- EF9: Fan not installed



Marshalltown (Kansas City, KS)

Project Issue Information

Issue Name : EF-1: Fan not running
Description : EF1 is not running. There seems to be a wiring issue. Unable to test/balance airflow.
Created By : National TAB **Assigned To :** National TAB - Kalen Kemp
Status : Open
Priority : Urgent **Asset Tag :** EF-1
Originated Date : 11/15/2025 - Kalen Kemp - National TAB

Project Issue File Details



11/15/2025



Marshalltown (Kansas City, KS)

Project Issue Information

Issue Name : EF-2: Fan not running
Description : EF2 is not running. There seems to be a wiring issue. Unable to test/balance airflow.
Created By : National TAB **Assigned To :** National TAB - Kalen Kemp
Status : Open
Priority : Urgent **Asset Tag :** EF-2
Originated Date : 11/15/2025 - Kalen Kemp - National TAB

Project Issue File Details



11/15/2025




Marshalltown (Kansas City, KS)


Project Issue Information

Issue Name : EF10: Fan not running
Description : EF10 is not running. Seems like it's not getting power or there is a wiring issue. Unable to test/balance.
Created By : National TAB **Assigned To :** National TAB - Kalen Kemp
Status : Open
Priority : Urgent **Asset Tag :** EF-10
Originated Date : 11/15/2025 - Kalen Kemp - National TAB

Project Issue File Details

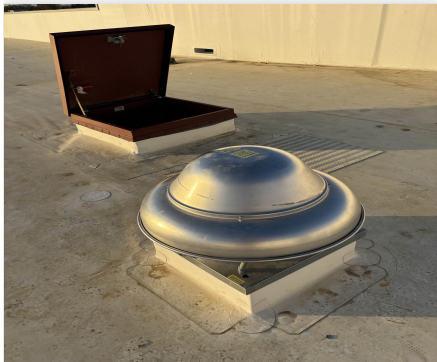

11/15/2025

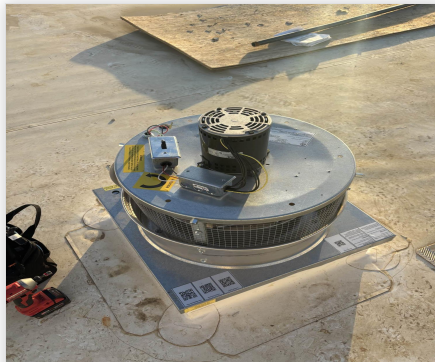

11/15/2025




Marshalltown (Kansas City, KS)


Project Issue Information

Issue Name : EF11: Fan not running
Description : EF10 is not running. There is no power/signal at the VFD in the fan housing. Unable to test/balance airflow.
Created By : National TAB **Assigned To :** National TAB - Kalen Kemp
Status : Open
Priority : Urgent **Asset Tag :** EF-11
Originated Date : 11/15/2025 - Kalen Kemp - National TAB

Project Issue File Details

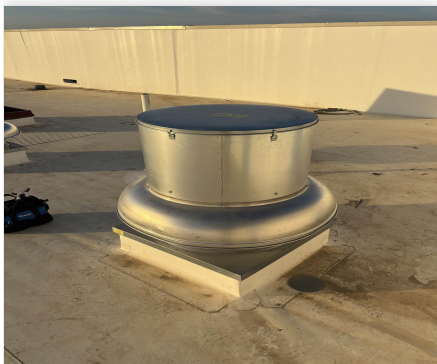

11/15/2025

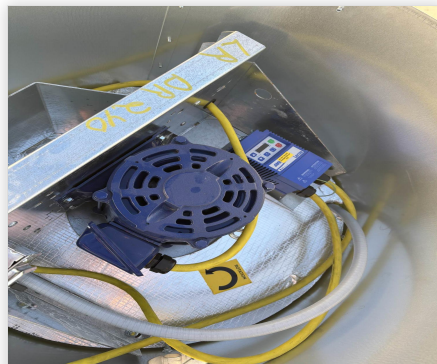

11/15/2025




Marshalltown (Kansas City, KS)

Project Issue Information

Issue Name : EF9: Fan not installed
Description : EF9 is not installed. Unable to test/balance.
Created By : National TAB **Assigned To :** National TAB - Kalen Kemp
Status : Open
Priority : **Urgent** **Asset Tag :** EF-9
Originated Date : 11/15/2025 - Kalen Kemp - National TAB

Project Issue File Details

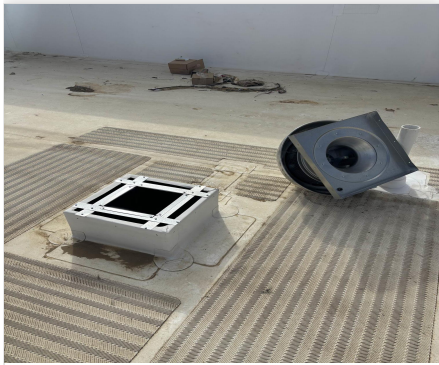

11/15/2025
