

PlanGrid Task Report - Jun 26, 2025

Prepared by Dale Wheeler

Jun 26, 2025

Description

35 tasks in this report.

Contents

#40 [DUCT 499] [NEW] CRITICAL (MISC) – [AC1 - MASTIC].....	3
#39 [DUCT 501] [NEW] Insulation stick pins.....	4
#38 [DUCT 498] [NEW] CRITICAL (DESIGN) – [MISSING DIFFUSERS].....	6
#37 [CNTL 004] [NEW] CRITICAL – Annunciators not powered.....	8
#36 [DUCT 006] [NEW] CRITICAL – Flex duct installation.....	9
#34 [EXHA 499] [NEW] CRITICAL (MISC) – [HOODS AND FANS NOT POWERED]	11
#33 [CNTL 001] [NEW] CRITICAL – MECHANICAL DAMPER.....	13
#30 [EXHA 509] [NEW] Grease exhaust duct is not painted.....	15
#29 [EXHA 506] [NEW] Exhaust fan discharge nozzle.....	16
#28 [EXHA 508] [NEW] Exhaust fan G2 Drip Guard.....	18
#27 [EXHA 511] [NEW] Grease exhaust duct curb cap.....	20
#26 [EXHA 510] [NEW] Grease exhaust duct is not supported.....	22
#24 [UNIT 518] [NEW] Equipment not secured properly.....	24
#23 [CNTL 017] [NEW] CRITICAL Thermostat terminations incorrect.....	25
#22 [UNIT 517] [NEW] Condensate piping construction.....	27
#21 [DUCT 005] [NEW] CRITICAL – Duct leaks observed.....	29
#20 [DUCT 005] [NEW] CRITICAL – Duct leaks observed.....	31
#19 [UNIT 504] [NEW] Equipment Fresh Air Tempering.....	32
#18 [UNIT 521] [NEW] Equipment is missing specified options.....	34

#17 [UNIT 514] [NEW] Equipment gas piping. 35

#16 [UNIT 514] [NEW] Equipment gas piping. 36

#15 [EXHA 007] [NEW] CRITICAL – Restroom fan not powered..... 38

#14 [UNIT 510] [NEW] Gas inlet grommet. 40

#13 [UNIT 513] [NEW] Equipment is damaged..... 41

#12 [CNTL 508] [NEW] Controls labeling..... 42

#11 [CNTL 505] [NEW] New sensors not installed 44

#10 [CURT 501] [NEW] Air curtain power. 45

#9 [HOOD 512] [NEW] Grease cup..... 46

#8 [HOOD 499] [NEW] CRITICAL (MISC) – [CAPTURE JET NOT POWERED]..... 47

#7 [CNTL 511] [NEW] Ansul system controls. 48

#6 [HOOD 505] [NEW] Hood shipping brackets..... 49

#5 [HOOD 508] [NEW] Sidejet arm angle bracket. 51

#4 [DUCT 008] [NEW] CRITICAL – Start collar damper orientation. 52

#3 [DUCT 010] [NEW] CRITICAL – Damper(s) missing hardware. 54

#2 [DUCT 507] [NEW] Ductwork is not fully insulated..... 55

#40 [DUCT 499] [NEW] CRITICAL (MISC) – [AC1 - MASTIC]

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 3:24 PM
dale@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 3:31 PM

Description

AC1 mastic not installed at diffuser collars for all supply grills, also ensure that all hard duct joint connections are sealed with mastic.

Photos



IMG_8104

Dale Wheeler

Jun 24, 2025 3:24 PM

#39 [DUCT 501] [NEW] Insulation stick pins.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 3:05 PM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 3:10 PM

Description

More stick pins are needed to ensure duct does not sag. Existing stick pins need to be taped over.

Photos



IMG_6987
Jordan Best
Jun 24, 2025 3:06 PM



IMG_6988
Jordan Best
Jun 24, 2025 3:06 PM

#38 [DUCT 498] [NEW] CRITICAL (DESIGN) – [MISSING DIFFUSERS]

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 3:04 PM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 3:19 PM

Description

AC-2, diffuser 1 is not installed. For diffuser 2 there is a large gap in the duct work allowing air to escape the duct.

Photos



IMG_7031

Jordan Best

Jun 24, 2025 3:05 PM

#37 [CNTL 004] [NEW] CRITICAL – Annunciators not powered.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 2:43 PM
dale@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 2:50 PM

Description

AC1, AC2, AC3, AC4, AC5
annunciators are not labeled
or energized.

Photos



20250624_144327_photo

Dale Wheeler

Jun 24, 2025 2:43 PM

#36 [DUCT 006] [NEW] CRITICAL – Flex duct installation.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 2:35 PM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 3:03 PM

Description

AC1 supply grills were spot checked and Inner flex cores was banded but not taped. Recommend all supply grills be check / verified band and tape were used.

Photos



IMG_6994

Jordan Best

Jun 24, 2025 2:38 PM

#34 [EXHA 499] [NEW] CRITICAL (MISC) – [HOODS AND FANS NOT POWERED]

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 2:29 PM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 3:21 PM

Description

Hoods and exhaust fans are not energized.

Photos



IMG_7041

Jordan Best

Jun 24, 2025 2:30 PM



IMG_7040

Jordan Best

Jun 24, 2025 2:30 PM



IMG_7042

Jordan Best

Jun 24, 2025 2:30 PM

#33 [CNTL 001] [NEW] CRITICAL – MECHANICAL DAMPER.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 2:28 PM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 26, 2025 8:17 AM

Description

AC1 mechanical damper
office damper is not
powered, and thermostat is
not installed.

Photos



IMG_7037
Jordan Best
Jun 24, 2025 2:29 PM



IMG_7038
Jordan Best
Jun 24, 2025 2:29 PM

#30 [EXHA 509] [NEW] Grease exhaust duct is not painted.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 9:50 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 1:15 PM

Description

EF-1 & EF-2 grease duct on rooftop is not painted.

Photos



IMG_7030

Jordan Best

Jun 24, 2025 9:50 AM

#29 [EXHA 506] [NEW] Exhaust fan discharge nozzle.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 9:43 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 1:16 PM

Description

EF-1 & EF-2 factory
discharge flange is not
installed.

Photos



20250624_094604_photo

Jordan Best

Jun 24, 2025 9:46 AM

#28 [EXHA 508] [NEW] Exhaust fan G2 Drip Guard.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 9:42 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 2:52 PM

Description

EF1 & EF-2 PVC drain & G2
grease guards are not
installed.

Photos



IMG_7027

Jordan Best

Jun 24, 2025 2:39 PM

#27 [EXHA 511] [NEW] Grease exhaust duct curb cap.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 9:35 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 1:20 PM

Description

EF1 & EF2 grease duct curb cap is to be screwed at all four corners to curb.

Photos



20250624_093605_photo

Jordan Best

Jun 24, 2025 9:36 AM

#26 [EXHA 510] [NEW] Grease exhaust duct is not supported.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 9:32 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 1:21 PM

Description

EF-1 & EF-2 grease ducts
support stands are not
installed.

Photos



IMG_7025

Jordan Best

Jun 24, 2025 9:35 AM

#23 [CNTL 017] [NEW] CRITICAL Thermostat terminations incorrect.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 9:25 AM
jordanb@nationaltab.com

List

TAB Critical Item


Last Updated

Jun 24, 2025 1:28 PM

Description

AC-1, 2, 3, 4, 5 terminal D-1 wire is not landed at terminal J-18 inside each unit.

Photos

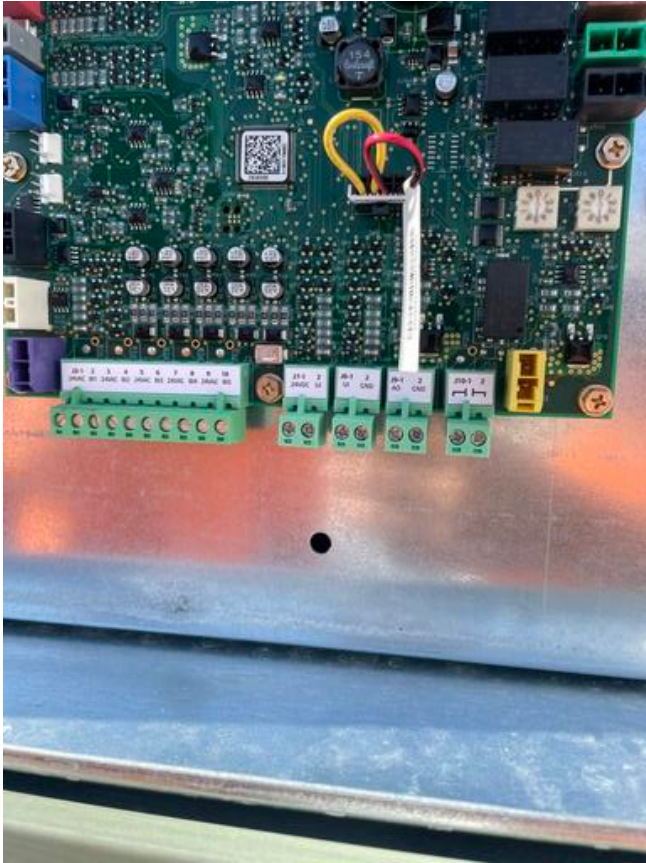

IMG_7023

Jordan Best

Jun 24, 2025 9:26 AM

#22 [UNIT 517] [NEW] Condensate piping construction.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 9:07 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 1:32 PM

Description

AC1, 2, 3, 4, 5 condensate line and p-traps are not installed.

Photos



IMG_7021

Jordan Best

Jun 24, 2025 9:09 AM

#21 [DUCT 005] [NEW] CRITICAL – Duct leaks observed.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 8:59 AM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 1:37 PM

Description

AC-1 new ductwork is not aligned with opening at curb of unit. Can see directly into space. Unit unable to be balanced till issue is resolved.

Photos



IMG_7020
Jordan Best
Jun 24, 2025 9:01 AM



IMG_7019
Jordan Best
Jun 24, 2025 9:01 AM

#20 [DUCT 005] [NEW] CRITICAL – Duct leaks observed.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 8:57 AM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 1:48 PM

Description

AC-2, 3, 4, 5 existing supply ductwork does not meet flush with bottom of rooftop unit allowing supply air to escape through the gaps. Units are unable to be balanced till ductwork issue is resolved.

Photos



IMG_7015

Jordan Best

Jun 24, 2025 8:59 AM

#19 [UNIT 504] [NEW] Equipment Fresh Air Tempering.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 8:56 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 1:49 PM

Description

AC-1, 2, 3, 4, 5 fresh air tempering kits are not installed.

Photos



IMG_7020

Jordan Best

Jun 24, 2025 8:57 AM

#18 [UNIT 521] [NEW] Equipment is missing specified options.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 8:19 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 1:55 PM

Description

AC-1, 2, 3, 4, 5 power exhaust is not installed.

Photos



IMG_7013

Jordan Best

Jun 24, 2025 8:20 AM

#17 [UNIT 514] [NEW] Equipment gas piping.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 7:45 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 2:00 PM

Description

AC-1, 2, 3, 4, 5 gas piping is not completed.

Photos



IMG_7012

Jordan Best

Jun 24, 2025 7:45 AM

#16 [UNIT 514] [NEW] Equipment gas piping.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 7:44 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 2:02 PM

Description

AC-1, 2, 3, 4, 5 grommets need to be installed around penetrations for low voltage wiring.

Photos



IMG_7011

Jordan Best

Jun 24, 2025 7:44 AM

#15 [EXHA 007] [NEW] CRITICAL – Restroom fan not powered.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 7:39 AM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 2:05 PM

Description

New EF-3 has not been attached to curb or powered at this time.

Photos



20250624_074015_photo

Jordan Best

Jun 24, 2025 7:40 AM

#14 [UNIT 510] [NEW] Gas inlet grommet.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 7:35 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 2:05 PM

Description

AC-1 gas pipe grommet is not installed.

Photos



IMG_7008

Jordan Best

Jun 24, 2025 7:36 AM

#13 [UNIT 513] [NEW] Equipment is damaged.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 24, 2025 7:34 AM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 3:32 PM

Description

AC-2 exterior is damaged.

Photos



IMG_7007

Jordan Best

Jun 24, 2025 7:34 AM

#12 [CNTL 508] [NEW] Controls labeling.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 4:22 PM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 3:33 PM

Description

AC-1, 2, 3, 4, 5 temp and humidity sensors are not labeled.

Photos



IMG_7005

Jordan Best

Jun 23, 2025 4:23 PM

#11 [CNTL 505] [NEW] New sensors not installed

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 4:18 PM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 3:33 PM

Description

AC-5 temp and humidity sensors not installed.

Photos



IMG_7004

Jordan Best

Jun 23, 2025 4:19 PM

#10 [CURT 501] [NEW] Air curtain power.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 3:50 PM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 3:22 PM

Description

AD-1, 2, 3 are not energized.

Photos



IMG_7044

Jordan Best

Jun 24, 2025 3:22 PM

#9 [HOOD 512] [NEW] Grease cup.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 3:27 PM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 3:33 PM

Description

Hood 2 grease cup is not installed.

Photos



20250624_153314_photo

Jordan Best

Jun 24, 2025 3:33 PM

#8 [HOOD 499] [NEW] CRITICAL (MISC) – [CAPTURE JET NOT POWERED]

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 3:25 PM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 1:42 PM

Description

Capture jet fans not powered

Photos



IMG_7002

Jordan Best

Jun 23, 2025 3:26 PM

#7 [CNTL 511] [NEW] Ansul system controls.

Status
Open

Start Date
Jun 24, 2025

Type
Planned Work

Created
Jun 23, 2025 3:20 PM
jordanb@nationaltab.com

List
TAB Non-Critical

Last Updated
Jun 24, 2025 1:50 PM

Description
ANSUL pull station for hood 1 is not installed.

Photos



IMG_6999
Jordan Best
Jun 23, 2025 3:21 PM



IMG_7001
Jordan Best
Jun 23, 2025 3:21 PM

#6 [HOOD 505] [NEW] Hood shipping brackets.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 3:15 PM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 3:34 PM

Description

Gusset bracket holes need screws installed.

Comments

Side bracket holes unoccupied

Jordan Best Jun 23, 2025

Photos



IMG_6998

Jordan Best

Jun 23, 2025 3:16 PM

#5 [HOOD 508] [NEW] Sidejet arm angle bracket.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 3:10 PM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 2:11 PM

Description

Hood 2 and hood 3 side arm brackets are not installed.

Photos



IMG_6997
Jordan Best
Jun 23, 2025 3:15 PM



IMG_6996
Jordan Best
Jun 23, 2025 3:15 PM

#4 [DUCT 008] [NEW] CRITICAL – Start collar damper orientation.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 2:22 PM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 2:15 PM

Description

AC-1 return diffuser damper handles are located on the sides of the duct and should be located on the bottom of the duct.

Photos



IMG_6991
Jordan Best
Jun 23, 2025 2:23 PM



IMG_6992
Jordan Best
Jun 23, 2025 2:23 PM

#3 [DUCT 010] [NEW] CRITICAL – Damper(s) missing hardware.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 2:21 PM
jordanb@nationaltab.com

List

TAB Critical Item

Last Updated

Jun 24, 2025 2:17 PM

Description

Damper is missing
necessary hardware.

Photos



IMG_6993

Jordan Best

Jun 23, 2025 2:22 PM

#2 [DUCT 507] [NEW] Ductwork is not fully insulated.

Status

Open

Start Date

Jun 24, 2025

Type

Planned Work

Created

Jun 23, 2025 1:44 PM
jordanb@nationaltab.com

List

TAB Non-Critical

Last Updated

Jun 24, 2025 3:13 PM

Description

AC1 has exposed sheet metal & and insulation seems that are not taped also no insulation vapor barrier around diffuser tops.

Photos



20250623_134655_photo

Jordan Best

Jun 23, 2025 1:47 PM
