



Comfort. Under control.


## 02-06-23 SWEETGREEN #AUS285 - AUSTIN, TX (MUELLER) CX, TAB, IAQ

### CheckList Information

**Name :** 7- Kitchen Hood Installation Verification **Status :** Submitted  
**Assigned Organization :** National TAB **Asset :**  
**Requesting Organization :** National TAB

### CheckList Item Details

#### ENSURE HOOD IS INSTALLED PER MFG DETAILS

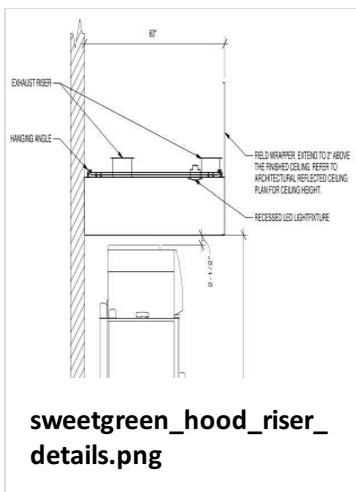

Attach a minimum 3 photo's of hood installation (below ceiling)



**HD-1.jpeg**



**HD-2.jpeg**



**HD-3.jpeg**

Attach a minimum 3 photo's of hood installation  
(above ceiling)



**HOOD-1.jpeg**



**HOOD-2.jpeg**



**HOOD-3.jpeg**

Record the Manufacturer and Model of the Kitchen Hood

CAPTIVE-AIRE M/N: 6012 VHB

Record the Length X Width X Height of the Hood

48"x60"x12"

Record the size of both exhaust risers (center riser dimension, front riser dimension)

CENTER RISER 10" ROUND FRONT RISER 10" ROUND

**RISERS.jpeg**

---

Measure the height from the bottom of the hood to the finished floor. 85"

---

Measure and record the left side distance from oven door to the end of the hood 7"

**LEFT\_OVERHANG.jpeg**

---

Measure and record the right side distance from oven door to the end of the hood 8"



**RIGHT\_OVERHANG.jpeg**

Ensure all-thread with spring isolation is installed to support the hood from the buildings structure

ALL THREAD INSTALLED BETWEEN HOOD AND BUILDINGS STRUCTURE, BUT NO ISOLATION SPRINGS ARE PRESENT.



**SPRINGS\_MISSING.jpeg**

Indicate the on/off switch is properly installed and accessible.

CANNOT LOCATE ON/OFF SWITCH.



**MISSING\_SWITCH.jpeg**

**Notes/Comments :**
