



Comfort. Under control.


02-06-23 SWEETGREEN #AUS285 - AUSTIN, TX (MUELLER) CX, TAB, IAQ

CheckList Information

Name : 7- Kitchen Hood Installation Verification **Status :** Submitted
Assigned Organization : National TAB **Asset :**
Requesting Organization : National TAB

CheckList Item Details

ENSURE HOOD IS INSTALLED PER MFG DETAILS

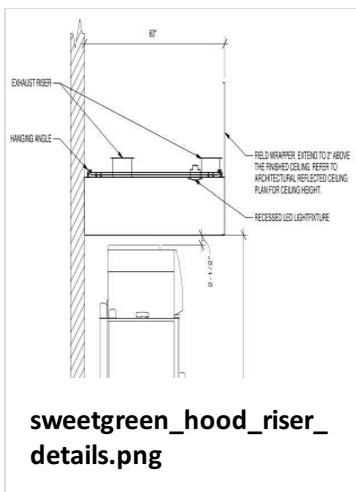

Attach a minimum 3 photo's of hood installation (below ceiling)



HD-1.jpeg



HD-2.jpeg



HD-3.jpeg

Attach a minimum 3 photo's of hood installation
(above ceiling)



HOOD-1.jpeg



HOOD-2.jpeg



HOOD-3.jpeg

Record the Manufacturer and Model of the Kitchen Hood

CAPTIVE-AIRE M/N: 6012 VHB

Record the Length X Width X Height of the Hood

48"x60"x12"

Record the size of both exhaust risers (center riser dimension, front riser dimension)

CENTER RISER 10" ROUND FRONT RISER 10" ROUND

**RISERS.jpeg**

Measure the height from the bottom of the hood to the finished floor. 85"

Measure and record the left side distance from oven door to the end of the hood 7"

**LEFT_OVERHANG.jpeg**

Measure and record the right side distance from oven door to the end of the hood 8"



RIGHT_OVERHANG.jpeg

Ensure all-thread with spring isolation is installed to support the hood from the buildings structure

ALL THREAD INSTALLED BETWEEN HOOD AND BUILDINGS STRUCTURE, BUT NO ISOLATION SPRINGS ARE PRESENT.



SPRINGS_MISSING.jpeg

Indicate the on/off switch is properly installed and accessible.

HOOD ON/OFF IS DESIGNED TO BE CONTROLLED THROUGH LUTRON TIMER CLOCK. CX-AGENT HAS NO CONTROL/ACCESS TO THIS SYSTEM. AT 12:33 am EF1 AND EF2 ARE STILL RUNNING.



MISSING_SWITCH.jpeg

Notes/Comments :
