

Report By:

National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246



Report: Deficiency Report
Function: Test, Adjust, & Balance
Date: 05/06/2025
Completed By: National TAB

PROJECT

05-05-25 WHATABURGER #1365 DAPHNE, AL

US HIGHWAY 98 & LAVENDER LANE

DAPHNE, AL 36526

Client

Whataburger Restaurants
300 Concord Plaza Dr
San Antonio, TX 78216

Issue List

- Building Pressure
- EF 1 - Backdraft Damper
- RTU 1 - Float Switch



05-05-25 WHATABURGER #1365 DAPHNE, AL

Project Issue Information

Issue Name : Building Pressure
Description : Building pressure was measured to be +0.0086” at the end of TAB, lower than the target of +0.02”. No obvious building leakages were observed. Not anticipated to be create an issue long-term.
Created By : National TAB **Assigned To :** National TAB - Dan Hertenstein
Status : Open
Priority : InfoOnly **Asset Tag :**
Originated Date : 05/09/2025 - Mark Johnson - National TAB



05-05-25 WHATABURGER #1365 DAPHNE, AL

Project Issue Information

Issue Name : EF 1 - Backdraft Damper
Description : EF-1 is missing a backdraft damper. Recommend installing per mechanical plans.
Created By : National TAB **Assigned To :** National TAB - Dan Hertenstein
Status : Open
Priority : Low **Asset Tag :** EF1
Originated Date : 05/09/2025 - Mark Johnson - National TAB

Project Issue File Details



05/09/2025



05-05-25 WHATABURGER #1365 DAPHNE, AL

Project Issue Information

Issue Name : RTU 1 - Float Switch
Description : RTU 1 (kitchen) periodically locks out due to float switch activation. Excessive condensate is present inside unit, and drains slowly. Recommend inspection.
Created By : National TAB **Assigned To :** National TAB - Dan Hertenstein
Status : Open
Priority : Medium **Asset Tag :** RTU1
Originated Date : 05/06/2025 - Mark Johnson - National TAB


Project Issue File Details



05/06/2025



05/06/2025

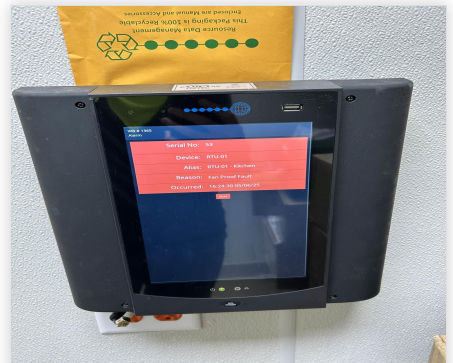

05/06/2025

Project Issue Response Details

- **05/09/2025 National TAB - Mark Johnson**
 - Issue still occurring periodically at the end of TAB. Recommend observing for changes and a mechanical inspection if issue persists.
