

REVIEW+RECTIFY

Assigned To All Hoods

Hoods do not have exhaust dampers installed. The initial readings show that all hoods are within +/-10, all hoods pass smoke capture. Should be reviewed by mechanical engineer if these need to be installed.



CRITICAL

Assigned To AC1

Unit has alarm 92, indoor enth sensor error.



REVIEW+RECTIFY

Assigned To AC4 EXISTING

Dampers was found broken on existing ductwork.



NON-CRITICAL

Assigned To Hoods

Fire pull stations are not labeled.



NON-CRITICAL

Assigned To All ACs


Condensate lines have not been completely installed



NON-CRITICAL

Assigned To All ACs

No seismic clips installed.

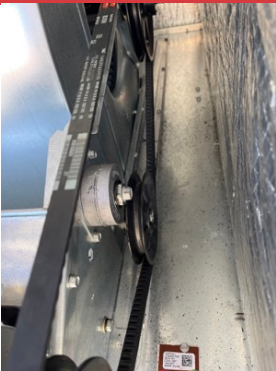

NON-CRITICAL

Assigned To AC3

Pulley cannot be properly tensioned. A smaller belt will need to be installed in order to tension to 3 ticks.
