

**Report By:**

National TAB  
1329 E. KEMPER ROAD  
SUITE 4210  
CINCINNATI, OH 45246



**Report: REMARKS**  
**Function: Test, Adjust, & Balance**  
**Date: 03/05/2026**  
**Completed By: National TAB**

**PROJECT**  
**03-02-26 CULVERS - MESA, AZ**

1830 E McKellips Road

Mesa, AZ 85203

**Client**

Accurex  
PO Box 410  
Schofield, WI 54476

# National TAB

Project: 03-02-26 CULVERS - MESA, AZ

## Table Of Contents

Section	Page #
REMARKS	3

## Issue List

- NONFUNCTIONAL DAMPER
- RIGID DUCT NOT INSTALLED



**03-02-26 CULVERS - MESA, AZ**

**Project Issue Information**

**Issue Name :** NONFUNCTIONAL DAMPER  
**Description :** SGRD1-7: Flow varies between 345-380cfm regardless of lever movement (DR)  
**Created By :** National TAB                      **Assigned To :** National TAB - Brianna Biggs  
**Status :** Open  
**Priority :** Urgent                                      **Asset Tag :** SGRD7  
**Originated Date :** 03/06/2026 - Christine Weale - National TAB




## 03-02-26 CULVERS - MESA, AZ

### Project Issue Information

**Issue Name :** RIGID DUCT NOT INSTALLED  
**Description :** MSET details cookline duct flex to come from a rigid straight pipe. Duct is flex only on some branches and is not straight. Recommend installing straight pipe from main supply drop and duct coming down straight, not in a curve, so no smoke issues arise in kitchen and flow balances properly.

**Created By :** National TAB                      **Assigned To :** National TAB - Brianna Biggs  
**Status :** Open  
**Priority :** High                                      **Asset Tag :** RTU-2  
**Originated Date :** 03/05/2026 - Christine Weale - National TAB

#### Project Issue File Details

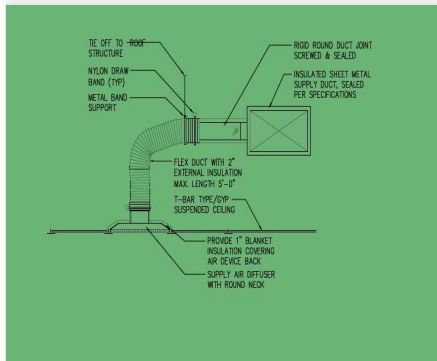

03/05/2026



03/05/2026
