



06-03-24 FREDDY'S - MT. VERNON, IL - RENEW

CheckList Information

Name :	Renew-Certificate of Completion	Status :	Completed
Assigned Organization :	National TAB	Asset :	
Requesting Organization :	National TAB		
Created Date :	06/04/2024 - Kyle Henry - National TAB		
Completed Date :	06/10/2024 - Dylan Crisman - National TAB		

CheckList Item Details


ROOFTOP UNITS

DEBRIS CLEANED FROM MIXED AIR AND BLOWER COMPARTMENT, BLOWER WHEEL, DRIVE ASSEMBLY, COMBUSTION FAN COMPARTMENT AND HEAT EXCHANGER. EACH COMPARTMENT THEN VACUUMED USING A SHOP VAC AND THEN WIPED CLEAN WITH A DAMP CLOTH	Yes
---	-----

Comment:



IMG_4500
06/10/2024

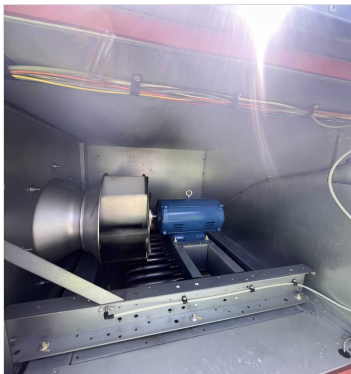

IMG_4502
06/10/2024




IMG_4508
06/10/2024

MOTOR AIR VENTS HAVE BEEN CLEANED AND SHOP VACUUMED TO ENSURE DEBRIS DOES NOT FALL BACK INTO THE MOTOR CASING	Yes
---	-----

Comment:

EVAPORATIVE COIL DEGREASED AND WASHED CLEAN	Yes
---	-----

Comment:

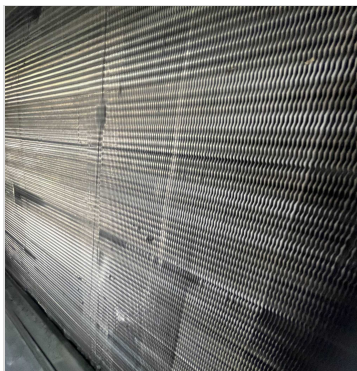

IMG_4509
06/10/2024



IMG_4505
06/10/2024

DRAIN PAN WASHED DOWN AND CLEANED, FREE OF DEBRIS

Yes

Comment:

CONDENSATE DRAIN FLUSHED TO ENSURE NO BLOCKAGE - WATER FREELY FLOWS FROM DRAIN PAN THROUGH THE CONDENSATE DRAIN LINE TO THE ROOF DRAIN.

Yes

Comment:

CONDENSER COIL HAIL GAURD REMOVED, COIL DEGREASED AND WASHED FROM REAR OF COIL, ALL EXCESS DEBRIS REMOVED PRIOR TO REINSTALLING THE HAIL GUARD

Yes

Comment:



IMG_4512
06/10/2024

CONDENSER FANS CHECKED FOR LOOSE FASTENERS AND UNUSUAL VIBRATION, MOTOR AND FAN WHEELS CLEANED OF DEBRIS AND WIPED DOWN WITH DAMP CLOTH

Yes

Comment:

EVAPORATIVE COIL FILTERS REPLACED WITH CLEAN FILTERS

Yes

Comment:



IMG_4510
06/10/2024



IMG_4506
06/10/2024

OUTDOOR AIR FILTERS CLEANED AND REINSTALLED IN THE OA AWNING

Yes

Comment:



IMG_4503
06/10/2024



IMG_4504
06/10/2024

MOTOR AND BLOWER WHEEL INSPECTED FOR FAILING/FAILED BEARINGS

Yes

Comment:

BELT REPLACED ON DRIVE IF CURRENT CYCLE REQUIRES A NEW BELT

N/A

Comment:

UNIT TURNED BACK ON AND VALIDATED THE UNIT IN RUNNING CONDITION PRIOR TO LEAVING	Yes
--	-----

Comment:**EXHAUST FANS**

EXHAUST STACK REMOVED TO ACCESS MOTOR HOUSING (IF STACK INSTALLED ON THE FAN)	Yes
---	-----

Comment:

MOTOR HOUSING WIPED DOWN WITH DRY CLOTH AND DRY SHOP VACUUM USED TO REMOVE ALL EXCESS DEBRIS.	Yes
---	-----

Comment:

MOTOR AIR VENTS HAVE BEEN CLEANED AND SHOP VACUUMED TO ENSURE DEBRIS DOES NOT FALL BACK INTO THE MOTOR CASING	Yes
---	-----

Comment:

COOLING TUBE FROM FAN SHELL TO MOTOR HOUSING INSPECTED AND CLEANED OF ALL DIRT AND DEBRIS	Yes
---	-----

Comment:

USE DAMP CLOTH TO WIPE DOWN ALL FINAL SURFACES	Yes
--	-----

Comment:

MOTOR AND FAN WHEELS INSPECTED FOR FAILING/FAILED BEARINGS	Yes
--	-----

Comment:

BELT REPLACED ON DRIVE IF CURRENT CYCLE REQUIRES A NEW BELT	N/A
---	-----

Comment:

MOTOR LID PUT BACK ON HOUSING AND STACK RE-INSTALLED (IF PRESENT)	Yes
---	-----

Comment:

HINGE KIT AND ELECTRICAL WHIP INSPECTED FOR PROPER INSTALLATION	Yes
---	-----

Comment:

GREASE CUP / GREASE CATCH SYSTEM INSPECTED FOR PROPER INSTALLATION	Yes
--	-----

Comment:

FAN TURNED BACK ON PRIOR TO LEAVING SITE AND ENSURED PROPER OPERATION OF THE FAN AT THE ROOF AND KITCHEN HOOD.	Yes
--	-----

Comment:**MUA FAN**

BLOWER AND HEATER HOUSING WIPED DOWN WITH DRY CLOTH AND DRY SHOP VACUUM USED TO REMOVE ALL EXCESS DEBRIS. INCLUDES: BLOWER WHEEL, BLOWER HOUSING, DRIVE ASSEMBLY, MOTOR BASE AND MOTOR, ALL INTERNAL WALLS AND CEILINGS, BURNER PROFILE PLATES, BURNER, BURNER ASSEMBLY, & MOTORIZED DAMPER	N/A
---	-----

Comment:

MOTOR AIR VENTS HAVE BEEN CLEANED AND SHOP VACUUMED TO ENSURE DEBRIS DOES NOT FALL BACK INTO THE MOTOR CASING	N/A
---	-----

Comment:

USE DAMP CLOTH TO WIPE DOWN ALL FINAL SURFACES	N/A
--	-----

Comment:

MOTOR AND FAN WHEELS INSPECTED FOR FAILING/FAILED BEARINGS	N/A
--	-----

Comment:

BELT REPLACED ON DRIVE IF CURRENT CYCLE REQUIRES A NEW BELT	N/A
---	-----

Comment:

OA MESH FILTERS HAVE BEEN CLEANED AND FREE OF DEBRIS	N/A
--	-----

Comment:

UNIT HAS BEEN TURNED BACK ON AND CONFIRMED OPERATIONAL AT THE UNIT AND THE KITCHEN HOOD	N/A
---	-----

Comment:**MUA HEAT SECTION**

GAS HEAT TURNED ON (IF IN SEASON) AND ENSURED FLAME WITH PROPER INTAKE AND DISCHARGE TEMPERATURE SETTINGS

N/A

Comment:

MUA COOLING SECTION

IF UNIT HAS COOLING: DX COIL WAS DEGREASED AND WASHED DOWN

N/A

Comment:

DRAIN PAN CLEANED OF DEBRIS

N/A

Comment:

CONDENSATE DRAIN IS INSTALLED AND FLUSHED TO ALLOW ALL WATER TO PROPERLY DRAIN

N/A

Comment:

CONDENSER COIL(S) CLEANED

N/A

Comment:

ADDITIONAL INSPECTIONS

ALL UNITS INSPECTED FOR CORRECT INSTALLATION, DEFECTS, OR OPERATIONAL ISSUES. IF ANY FOUND A ISSUE WAS CREATED WITH REQUIRED PHOTO'S OR VIDEO.

Yes

Comment:

BUILDING PRESSURE IS NEUTRAL

Yes

Comment:

HOOD CAPTURE IS 100% DURING NORMAL COOKING PERIODS

Yes

Comment:

THERMOSTATS ARE PROPERLY PROGRAMMED

Yes

Comment:
