

Report By:

**National TAB
105 Stone Village Drive
Fort Mill, SC 29708**



**Report: Deficiency Report
Function: Test, Adjust, & Balance
Date: 09/30/2025
Completed By: National TAB**

**PROJECT
09-29-25 QT #1107 ANDERSON, SC**

4123 CLEMSON BLVD

ANDERSON, SC

Client

**QUIKTRIP
4705 SOUTH 129TH EAST AVENUE
TULSA, OK 74134**

Issue List

- EF-1 speed controller
- RTU-3 economizer doesn't close all the way



09-29-25 QT #1107 ANDERSON, SC

Project Issue Information

Issue Name : EF-1 speed controller
Description : The speed controller on EF-1 is not working, fan was left on high, above design.
Created By : National TAB **Assigned To :** National TAB - Brianna Biggs
Status : Open
Priority : Medium **Asset Tag :** EF1
Originated Date : 09/30/2025 - Christian Moller - National TAB

Project Issue File Details



09/30/2025



09/30/2025



09-29-25 QT #1107 ANDERSON, SC


Project Issue Information

Issue Name : RTU-3 economizer doesn't close all the way
Description : The economizer on RTU 3 does not close more than 0.75". This is enough for 807 CFM of OA but does not close enough to find a set point for the 350CFM of OA also required. (Picture shows lowest set point)
Created By : National TAB **Assigned To :** National TAB - Brianna Biggs
Status : Open
Priority : Medium **Asset Tag :** RT-3
Originated Date : 09/30/2025 - Christian Moller - National TAB

Project Issue File Details



09/30/2025

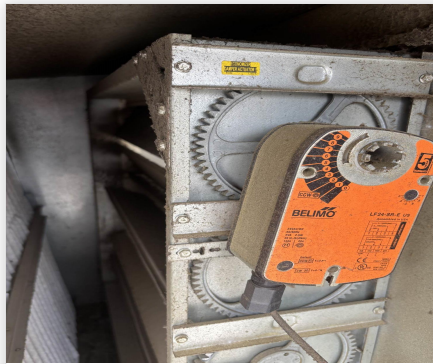

09/30/2025
