

HVAC Findings

Prepared by David Annan

Sep 17, 2024

Description

2 tasks in this report.

Contents

#302 Condensate drains only have 1 union	2
#301 Info Only: AHU-1 has limited access	3

#302 Condensate drains only have 1 union

Status
Open

Type
Issue

Location
Roof Items

Root Cause
Quality >
Installation

Description

All condensates drains for the RTUs only have 1 union. The plans show 2 unions between the P-traps. Refer to page P3.1 "detail 2" for specifications.

Assignees
cbrown@horizonc.com
jrichardson@horizonc.com


Watchers
jrichardson@horizonc.com
alberto.gonzalez2@jll.com
cbrown@horizonc.com

Start Date
Sep 3, 2024

Due At
Sep 30, 2024

Last Updated
Sep 17, 2024 5:26 PM

Sheet
P3.1

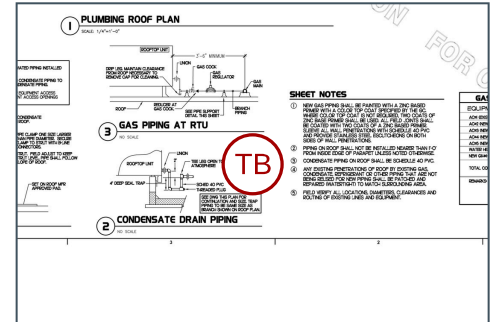

Photos



IMG_5354
David Annan
Sep 17, 2024 5:26 PM

#301 Info Only: AHU-1 has limited access

Status

Open

Watchers

alberto.gonzalez2@jll.com
cbrown@horizonc.com
will@nationaltab.com

Type

Other

Start Date

Sep 5, 2024

Location

Above the walk in cooler

Due At

Sep 30, 2024

Description

AHU-1, which is located above the walk in cooler has limited access to the units due to the tight space between the cooler and ceiling.

Last Updated

Sep 16, 2024 6:54 AM

Photos



IMG_5343
David Annan
Sep 16, 2024 6:54 AM



IMG_5346
David Annan
Sep 16, 2024 6:54 AM



IMG_5348

David Annan

Sep 16, 2024 6:54 AM
