

TAB PUNCHLIST - CFA 05535 08/27/24

Prepared by Jacob Davidson

Aug 27, 2024

Description

10 tasks in this report.

Contents

#190 [SITE 008] [NEW] CRITICAL – Building envelope. (In-Line).....	2
#189 [UNIT 999] [NEW] (MISC) P/P1 not connected to economizer module on AC4	3
#187 [UNIT 517] [NEW] Condensate piping construction.	4
#185 [UNIT 522] [NEW] AC air filters.	6
#183 [EXHA 500] [NEW] Restroom rectangular duct riser.	7
#182 [DUCT 002] [NEW] CRITICAL – Turning vanes in return duct.	8
#181 [HOOD 499] [NEW] CRITICAL (MISC) – Capture Jet Fan not wired	10
#180 [HOOD 508] [NEW] Sidejet arm angle bracket.	11
#179 [HOOD 500] [NEW] Hood lighting.	12
#178 [CNTL 509] [NEW] Amerex pull labeling.	14

L05535_South Topeka Blvd (KS) FSU

3231 Southwest Topeka Boulevard, Topeka, Kansas

L1020005535

#190 [SITE 008] [NEW] CRITICAL – Building envelope. (In-Line)

Status

Open

Start Date

Aug 26, 2024

Description

Building envelope not sealed between adjoining spaces, unable to obtain accurate building pressure.

Created

Aug 27, 2024 10:27 AM
jacobd@nationaltab.com

#189 [UNIT 999] [NEW] (MISC) P/P1 not connected to economizer module on AC4


Status
Open

Start Date
Aug 26, 2024

Description
On AC4, P/P1 from the Suncoast panel should connect to P/P1 on the economizer module inside the unit.

Created
Aug 27, 2024 9:56 AM
jacobd@nationaltab.com

Photos

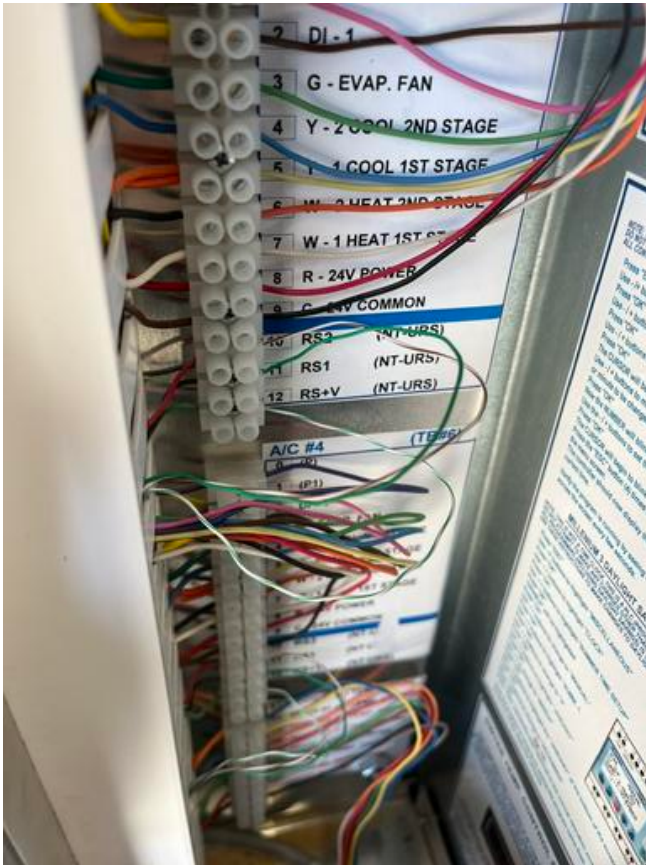

20240827_100110_photo
Jacob Davidson
Aug 27, 2024 10:01 AM



IMG_8874
Jacob Davidson
Aug 27, 2024 10:00 AM

#187 [UNIT 517] [NEW] Condensate piping construction.

Status
Open

Start Date
Aug 26, 2024


Sheet
M-502

Description

Equipment condensate piping or p-trap is not constructed per normal CFA specifications.

Created

Aug 26, 2024 12:04 PM
jacobd@nationaltab.com

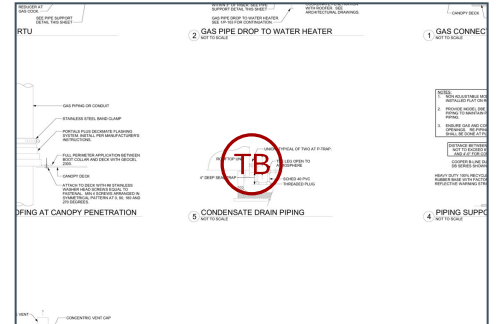

Photos



IMG_8847
Jacob Davidson
Aug 26, 2024 12:06 PM



IMG_8848
Jacob Davidson
Aug 26, 2024 12:06 PM

L05535_South Topeka Blvd (KS) FSU

3231 Southwest Topeka Boulevard, Topeka, Kansas

L1020005535



IMG_8850

Jacob Davidson

Aug 26, 2024 12:06 PM



IMG_8849

Jacob Davidson

Aug 26, 2024 12:06 PM

#185 [UNIT 522] [NEW] AC air filters.

Status

Open

Start Date

Aug 26, 2024

Description

Filters in AC3 are not pleated per design. The units are also missing extra set per specification.

Created

Aug 26, 2024 11:50 AM
jacobd@nationaltab.com

Photos



IMG_8861

Jacob Davidson

Aug 26, 2024 11:54 AM

#183 [EXHA 500] [NEW] Restroom rectangular duct riser.

Status

Open

Start Date

Aug 26, 2024

Description

Restroom exhaust
rectangular duct riser not
correctly lined per
specification

Created

Aug 26, 2024 11:46 AM
jacobd@nationaltab.com

Photos



IMG_8875

Jacob Davidson

Aug 26, 2024 11:53 AM

#182 [DUCT 002] [NEW] CRITICAL – Turning vanes in return duct.

Status

Open

Start Date

Aug 26, 2024

Description

Turning vanes are present in the return duct and need to be removed per specification. Present in return ducts of AC1, AC2, and AC3

Created

Aug 26, 2024 11:42 AM
jacobd@nationaltab.com

Photos



IMG_8862

Jacob Davidson

Aug 26, 2024 11:53 AM



IMG_8870

Jacob Davidson

Aug 26, 2024 11:53 AM

L05535_South Topeka Blvd (KS) FSU

3231 Southwest Topeka Boulevard, Topeka, Kansas

L1020005535



IMG_8863

Jacob Davidson

Aug 26, 2024 11:53 AM

#181 [HOOD 499] [NEW] CRITICAL (MISC) – Capture Jet Fan not wired

Status

Open

Start Date

Aug 26, 2024

Description

Capture jet fans are not wired currently for operation.

Created

Aug 26, 2024 10:18 AM
jacobd@nationaltab.com

Photos



IMG_8835

Jacob Davidson

Aug 26, 2024 10:20 AM

#180 [HOOD 508] [NEW] Sidejet arm angle bracket.

Status

Open

Start Date

Aug 26, 2024

Description

The Halton supplied angle bracket that connects the integral sidejet arm to the counter is missing or not installed correctly. Secure bracket to arm and bracket to counter underneath removeable fry dump via stainless steel rivets.

Created

Aug 26, 2024 10:14 AM
jacobd@nationaltab.com

Photos



IMG_8834

Jacob Davidson

Aug 26, 2024 10:20 AM



IMG_8833

Jacob Davidson

Aug 26, 2024 10:20 AM

#179 [HOOD 500] [NEW] Hood lighting.

Status

Open

Start Date

Aug 26, 2024

Description

Hood has lighting not energized properly with exhaust fans on or light(s) is flickering.

Created

Aug 26, 2024 10:12 AM
jacobd@nationaltab.com

Photos



IMG_8840

Jacob Davidson

Aug 26, 2024 10:21 AM



IMG_8839

Jacob Davidson

Aug 26, 2024 10:21 AM

L05535_South Topeka Blvd (KS) FSU

3231 Southwest Topeka Boulevard, Topeka, Kansas

L1020005535



IMG_8838

Jacob Davidson

Aug 26, 2024 10:21 AM

#178 [CNTL 509] [NEW] Amerex pull labeling.

Status

Open

Start Date

Aug 26, 2024

Description

Label all Amerex pull stations for which hoods they serve.

Created

Aug 26, 2024 10:11 AM
jacobd@nationaltab.com

Photos



IMG_8837

Jacob Davidson

Aug 26, 2024 10:21 AM
