

Report By:

**National TAB
1329 E. KEMPER ROAD
SUITE 4210
CINCINNATI, OH 45246**

NATIONAL

TAB

Comfort. Under control.

**Report: Issue Report
Function: Test, Adjust, & Balance
Date: 09/19/2022**

**PROJECT
09-19 CULVERS - LOGANSPOORT, IN**

3919 EAST MARKET STREET

LOGANSPOORT, IN 46947

Client

Captive-Aire Region #60

National TAB

Project: 09-19 CULVERS - LOGANSPOORT, IN

Table Of Contents

Section	Page #
Issue Data	3



Comfort. Under control.

09-19 CULVERS - LOGANSPO, IN

Project Issue Information

Issue Name : BOTH HOOD EXHAUST GREASE CUPS

Description : The grease cups for both PRV 2 and 3 are in the motor compartment but are not installed.

Created By : National TAB

Assigned To : National TAB - Will Turnbough

Status : Open

Originated Date : 09/19/2022 - Jack Bain - National TAB

Project Issue File Details



FuselT1436f9919b33436...



FuselT46491912a39241f...



Comfort. Under control.

09-19 CULVERS - LOGANSPORT, IN

Project Issue Information

Issue Name : CONDUIT FOR PRV1 is tight.

Description : When you lean the exhaust fan back or try to remove it you can not lift it more then 2-3 inches. Looks like the wires will rip or short out if the fan is pulled back too far. This also may be why backdraft damper is not yet installed.


Created By : National TAB

Assigned To : National TAB - Will Turnbough

Status : Open

Originated Date : 09/19/2022 - Jack Bain - National TAB

Project Issue File Details

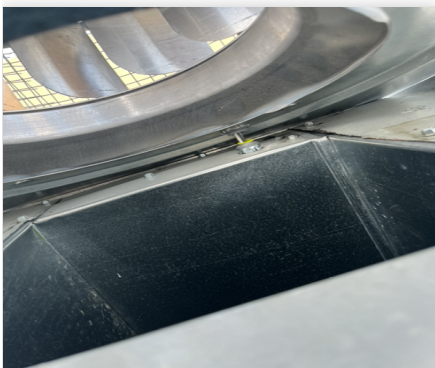

FuselT93772fcbff504a2...



Comfort. Under control.

09-19 CULVERS - LOGANSPORT, IN

Project Issue Information

Issue Name : HMI for both RTUS not powered

Description : HMI for RTU1 and RTU2 are missing CAT5 cable and are not powered.

Created By : National TAB

Assigned To : National TAB - Will Turnbough

Status : Open

Originated Date : 09/19/2022 - Jack Bain - National TAB

Project Issue File Details



FuselTf1ec4fca42dd4f7...



Comfort. Under control.

09-19 CULVERS - LOGANSPORT, IN

Project Issue Information

Issue Name : HOOD CONTROL NOT POWERED

Description : The HMI for hoods is not wired and so there is no speed controller for either hood exhaust fan.

Created By : National TAB

Assigned To : National TAB - Will Turnbough

Status : Open

Originated Date : 09/19/2022 - Jack Bain - National TAB

Project Issue File Details



FuselTaba84227ae6f4f0...

