




Comfort. Under control.

08-29 ARBY'S #1191 - FORT SMITH, AR (TOWSON) RE-BALANCE

Project Issue Information

Issue Name : New Trane Unit does not appear to have dehumidification
Description : According to the manual, digit 22 should be B for dehumidification option. For the RTU that is installed, digit 22 is 0 which is "Standard refrigeration System".
Created By : National TAB Assigned To : National TAB - Michael McDonnell
Status : Open
Originated Date : 08/30/2022 - Will Turnbough - National TAB

Project Issue File Details

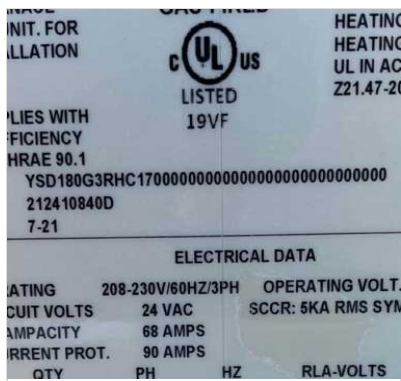

trane_label.png

6 = Building Automation Control Network Communications Interface
Digit 22 - Refrigeration System Option
0 = Standard refrigeration system
B = Dehumidification (Hot Gas Reheat)
Digit 23 - Refrigeration Controls
0 = Without Refrigeration Controls
1 = Froststat
Digit 24 - Smoke Detector

manual.png
